

May 13, 2011

Mr. D. Jesse Hegemier, P.E.
County Engineer
Fort Bend County
1124 Blume Road
Rosenberg, Texas 77471

Re: Invoice No. 7
Burney Road (FBC Project No. 719)
Partial Payment for Work Authorization No. 2

Project No. 300701.02

Dear Mr. Hegemier:

We have reviewed the enclosed invoice by CLR, Inc., and recommend payment in the amount of \$76,592.90, as submitted. The contract amount shown for CLR was authorized in Work Authorization No. 2, which is effective until December 31, 2011. CLR has also prepared a progress report, which is attached to the invoice for your review.

Please call me if you have any questions.

Sincerely,



Peter A. Ring, P.E.
Project Manager

PAR/bl

Enclosure



May 12, 2011

Mr. Pete Ring, PE
Schaumburg & Polk, Inc.
11767 Katy Freeway
Suite 900
Houston, Texas 77079

By e-mail

Re: Billing No. 11
Services thru April 30, 2011
Work Authorization: #2
FBC Project No.: 719 WA #2
FBC Purchase Order: 37740
CLR Project No.: 04-028-02

Dear Mr. Ring:

Please find enclosed Billing No. 11 (Consultant's Invoice No. 37991) in the amount of \$76,592.90 for your consideration and processing. The following items are included:

- Billing Summary
- PS&E Progress Report No. 3
- Project Schedule (reflecting 5/3/2011 50% submittal)

If you have any questions on the invoice, please call me at 832.928.5232.

Sincerely,
CLR, Inc.

Mike Terechenok, PE
Project Engineer

HMT/hmt
Enclosures

ENGINEERS • SURVEYORS • GIS

P.O. Box 450, Waller, Texas 77484
Phone 713-462-0993 • Fax 713-462-2732 • Toll Free 800-694-8241 • www.clri.com

REMIT TO:CLR, Inc.
P.O. Box 450
Waller, TX 77484**Invoice**Invoice Number: 37971
Invoice Date: May 12, 2011To: FORT BEND COUNTY
C/O SCHAUMBERG & POLK
11767 KATY FREEWAY, SUITE 900
HOUSTON, TX 77079
Attention: PETER RINGProject: 04-028-02 BURNEY ROAD WIDENING IMPROVEMENT
FBC PROJECT NO. 719; P.O. 37740; WORK AUTHORIZATION #2

Professional Services through 4/30/2011

INVOICE GRAND TOTAL: \$ 76,592.90

Billing Group: 001M CLR ENGINEERING

Contract Amount:	\$339,405.00
Percent Complete:	45.00%
Fee Earned:	\$152,732.25
Prior Fee Billings:	\$91,639.35
Current Fee Total:	\$61,092.90

Billing Group: 004SB TRAFFIC SIGNALS - GUNDA

Contract Amount:	\$31,000.00
Percent Complete:	50.00%
Fee Earned:	\$15,500.00
Prior Fee Billings:	\$0.00
Current Fee Total:	\$15,500.00

Total Project Invoice Amount

\$76,592.90

PS&E PROGRESS REPORT No. 3

Highway:	Burney Road
Limits:	Voss Rd north to Old Richmond Rd
FBC Purchase Order No.:	37740
FBC Project No.:	719 WA #2
CLR Project No.:	04-028-02

PROGRESS REPORT No. 03 April, 2011

SUMMARY – On April 4, 2011, CLR distributed meeting minutes from the March 25, 2011 meeting held at Schaumburg, Polk, Inc. with representatives of the City of Sugar Land and Ft. Bend County.

PLANS

- Continued development of construction documents including:
- Horizontal and Vertical geometrics.
- Cross street ties (horizontal & vertical)
- Roadway cross sections.
- Proposed sidewalk grading and location within ROW.
- Plan and layout drawings.
- Profile of existing subsurface utilities along Burney Road ROW
- Construction details.

HYDROLOGY & HYDRAULICS

- Completed initial hydraulic calculations for 3-year and 100-year storm events.
- Reviewed connection point to MUD-119.
- Continued effort for roadway drainage system for collection and discharge into MUD-119.
- Drainage design from West Bellfort Drive north to Old Richmond Road.
- Drainage design from West Airport Blvd south to Voss Road.

TRAFFIC CONTROL PLAN (TCP)

- Began two phase TCP plans.

STORM WATER POLLUTION PREVENTION PLANS

- Continued SWPPP and detail sheets.
- Updated SWPPP quantities for cost estimate.

TRAFFIC SIGNAL DESIGN

- Coordinated with traffic consultant for traffic signal design, details and quantities.

Special note: The Traffic Consultant's scope has been modified. The design for a permanent span wire signal has been eliminated from the scope and a design for a temporary span wire signal has been added to the scope. The Traffic Consultant's fee will remain the same.

SIGNING AND PAVEMENT MARKING DESIGN

- Continued Signing & Pavement Markings per City of Sugar Land construction details.
- Updated preparation of PM&S quantities.

GENERAL NOTES, SPECIFICATIONS AND STANDARD DRAWINGS

- Reviewed County and City general notes.
- Reviewed County and City construction details.

QUANTITIES AND COST ESTIMATES

- Updated pavement removal quantities.
- Updated storm sewer removal quantities.


ANTICIPATED WORK FOR NEXT MONTH MAY, 2011

- Review and address 50% progress comments from City and County.
- Continue coordination with sub-consultants.
- Continue with construction plan preparation and refine cost estimate.
- Continue QA/QC review.
- Coordinate with SPI to conduct an updated utility coordination meeting.

EXHIBIT C

BURNEY ROAD

ROADWAY WIDENING IMPROVEMENTS VOSS RD to OLD RICHMOND ROAD

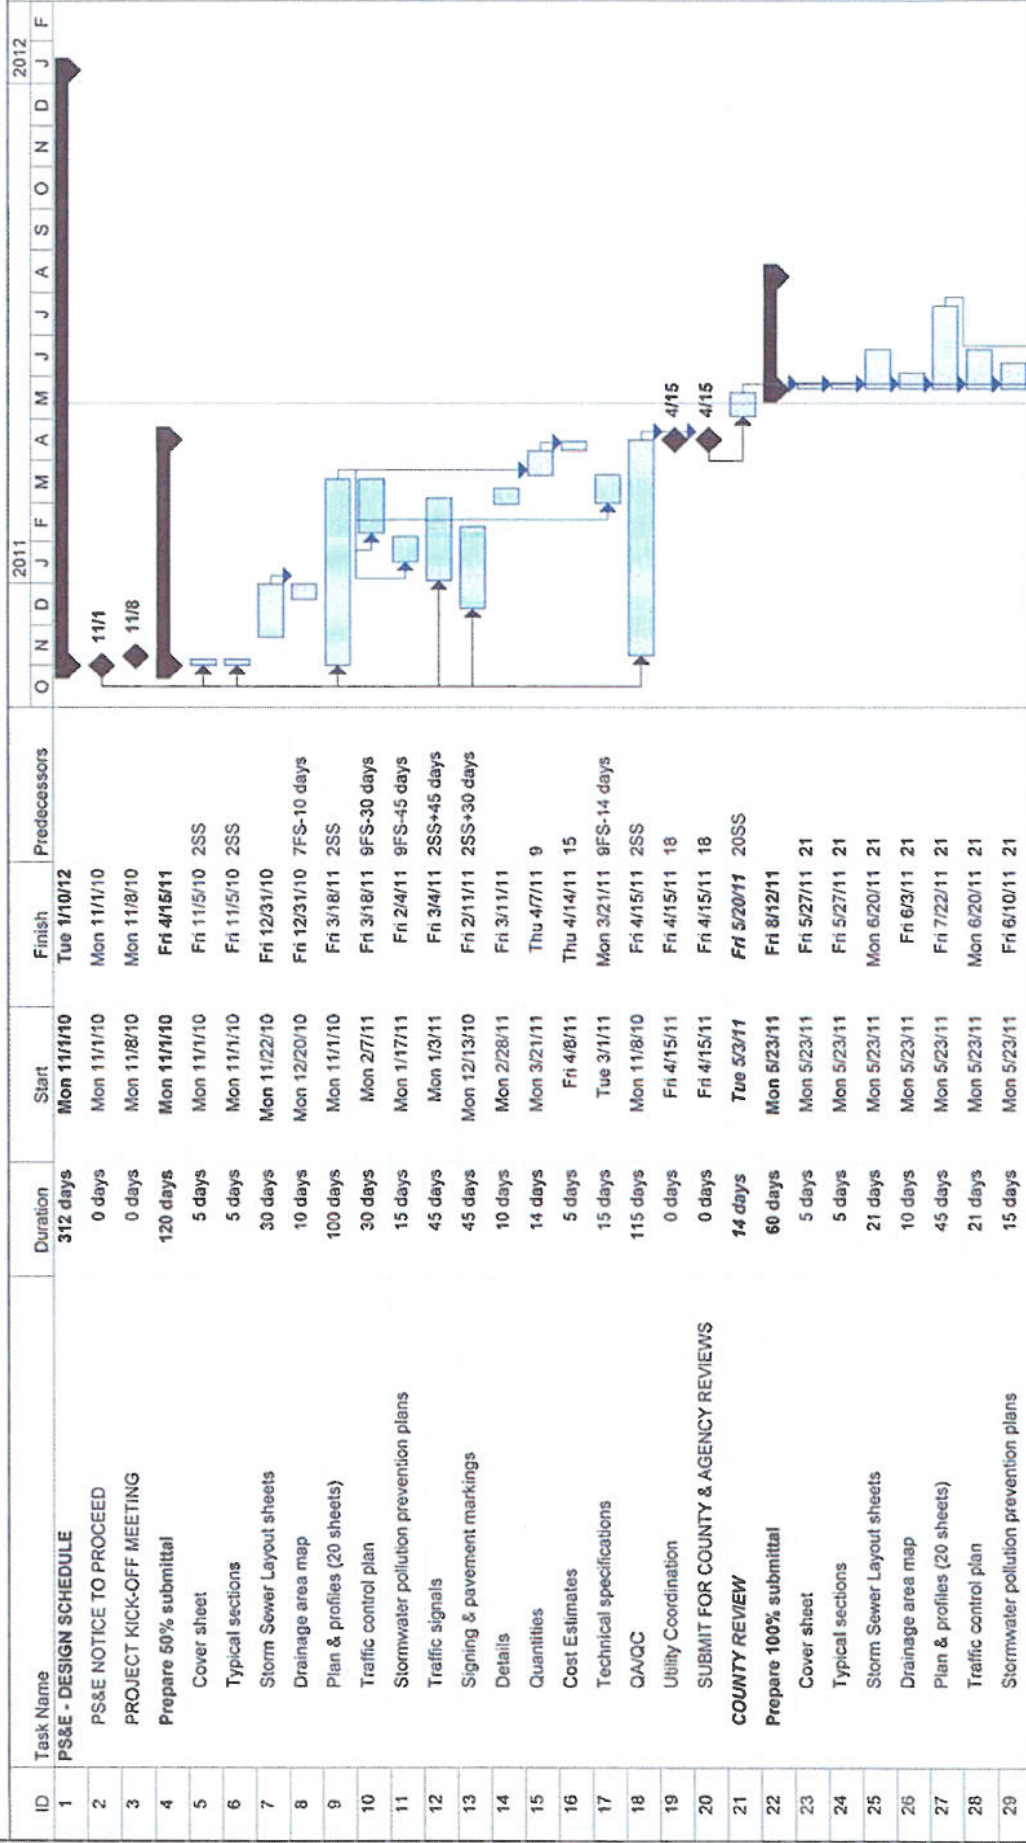



Project: Burney - PSE Schedule Nov
Date: Thu 5/12/11

PREPARED BY:
CLR, Inc.

EXHIBIT C

BURNEY ROAD

ROADWAY WIDENING IMPROVEMENTS VOSS RD to OLD RICHMOND ROAD

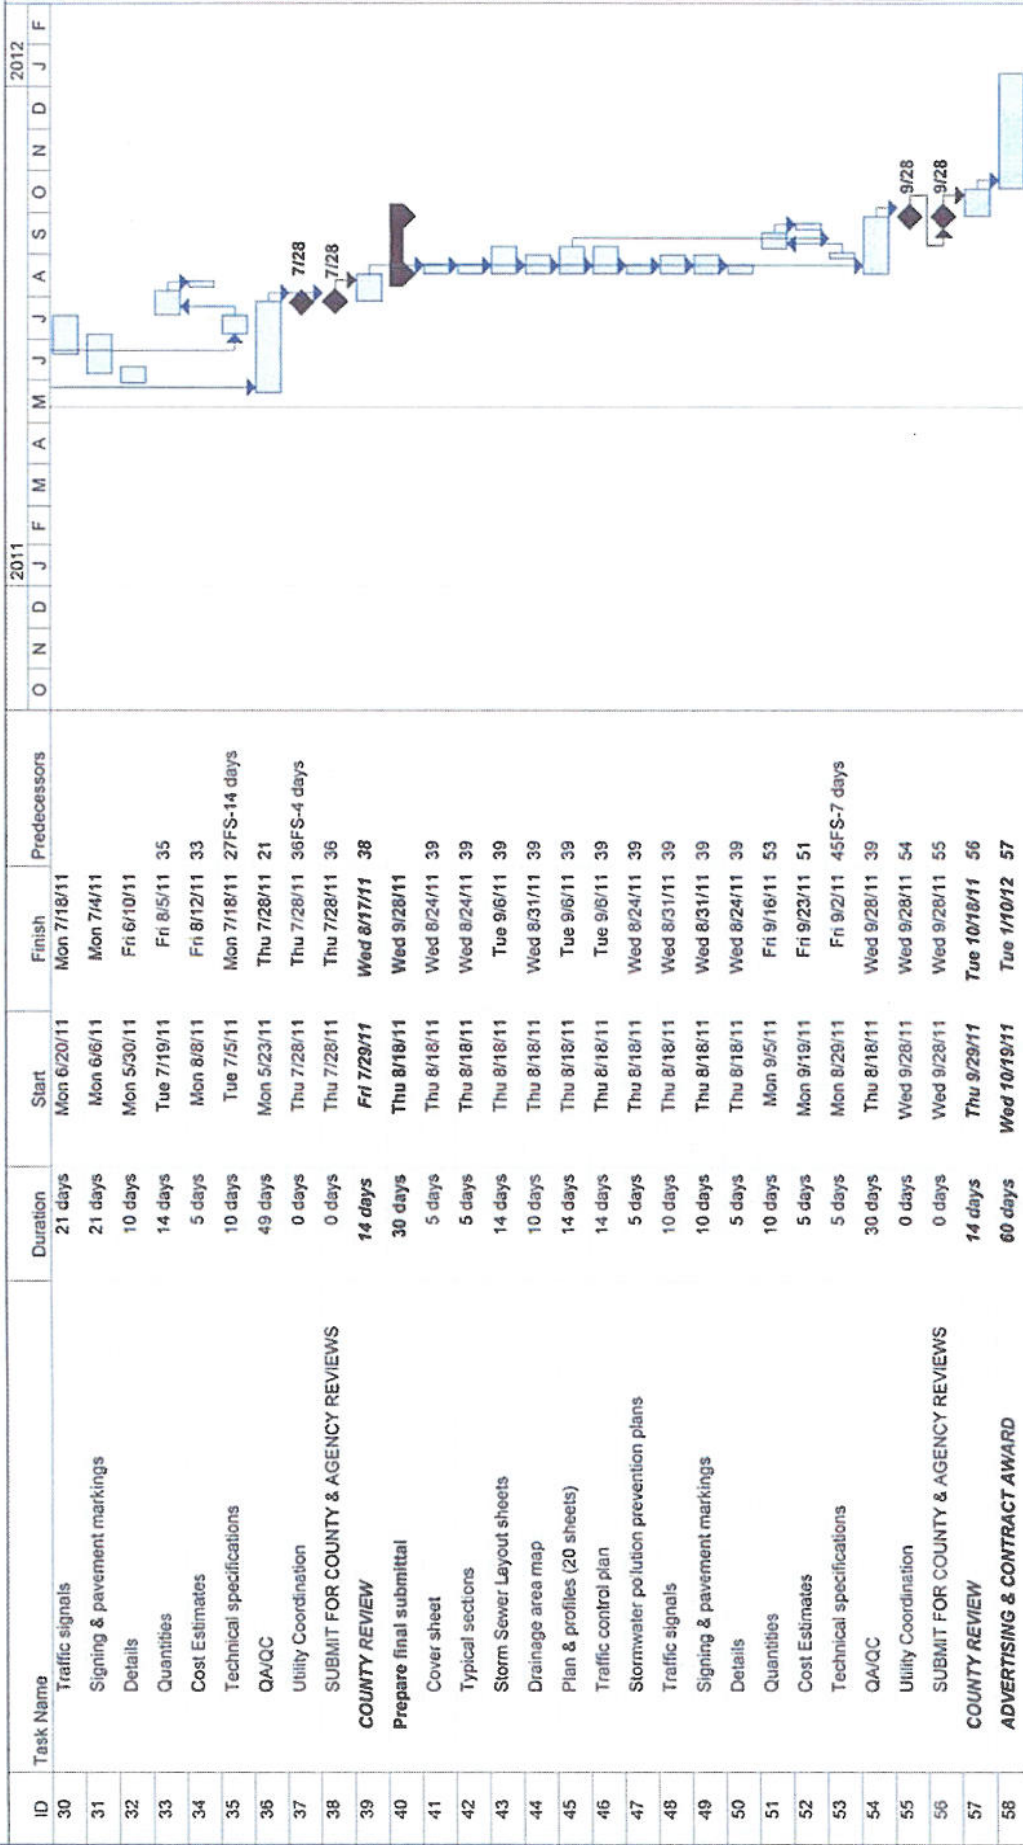

Project: Burney - PSE Schedule Nov
Date: Thu 5/12/11

PREPARED BY:
CLR, Inc.
