

PO # 159751

DMS

Rec 441539

Estimate and Certification for Payment

Company Name: Allgood Construction Company Inc.

Address: 1702 Settegast Ranch Rd

Phone #: 832-847-4071

Williams Way Blvd from FM 762 to US 59/IH 69 NB Frontage Road

Owner: Fort Bend County
 Address: 301 Jackson
 Richmond, Texas 77469

P.O. No: 159751
 FBC Mobility Project #: 13114

Attention: Stacy Slawinski
 Invoice No: Estimate #: 4
 Start Date: 11/13/2017
 Current Contract Completion Date: 10/13/2018
 Estimate Cut Off Date: 2/28/2018
 Date of Estimate: 3/1/2018

Initial Contract Time: 335 days
 Current Approved Extensions: 0 days
 Previous Approved Extensions: 0 days
 Total Contract Time: 335 days
 Spent Days: 108 days
 Days Remaining: 227 days

32%
100%

A. Contract Amount to Date:

1. Contract Price:		\$	4,645,912.45	✓
2. Approved Change Orders:	C.O. 1	\$	128,392.31	✓
	C.O. 2	\$	43,310.55	✓
	C.O. 3	\$	116,851.20	✓
	C.O. 4	\$	32,989.20	✓
Total Changes to Date:		\$	321,543.26	✓
Total Contract Amount:		\$	4,967,455.71	✓

B. Earnings to Date:

1. Previous Work Completed:	16.6%	Previous Earnings:	\$	791,994.27	✓
2. Work Completed this Period:	14.9%	Earnings this Period:	\$	738,613.92	Lawson
3. Work Completed to Date:	31.5%		\$	49,438.56	Lawson
4. Materials On Site:		Total Earnings:	\$	1,580,046.75	✓

C. Reductions:

1. Retainage:	10% of	\$	1,580,046.75	\$	158,004.68
Total Payments Due:		\$		\$	1,422,042.07
Less Previous Payments:		\$		\$	712,794.84

Total Amount Due Contractor This Estimate/Invoice: \$ 709,247.23 agenda

The undersigned Contractor certifies that to the best of his knowledge, information and belief that the Work has been completed in accordance with the Plans and Specifications and the current payment shown on this Application for Payment is now due.

Prepared By:

See
 Contractor

Date: 3-15-2018

The foregoing estimate of work completed is true and correct to the best of my knowledge and belief.

Approved By:

David M. Grant
 Project Representative

Date: 03/16/2018

Approved By:

J. A. Hill
 Engineer

Date: 03/20/18

PAY ESTIMATE: #4
PROJECT: WILLIAMS WAY BLVD
JOB # 1706

CONTRACTOR'S AFFIDAVIT AND RELEASE

STATE OF TEXAS
COUNTY OF FORT BEND


For and in consideration of the sum of **\$709,247.23**, representing payment under the above referenced contract for all labor, materials and/or services furnished by the undersigned for the **WILLIAMS WAY BLVD - FROM F.M. 762 TO US 59/IH 69 NB FRONTAGE RD** in Fort Bend County, Texas, and represented by payment request dated **MARCH 1, 2018** covering all such work from **2/1/18 to 2/28/18** less retention upto that date, undersigned hereby certifies that all labor and materials prior to the above date by undersigned in connection with the above named project have been paid in full. The undersigned agrees to indemnify and save harmless **FORT BEND COUNTY MUD 116** against all loss, damage or expense of any character whatsoever that may arise by reason of claims for labor or unpaid materials used in connection with said improvements, prior to the above date. The undersigned further hereby releases and waives any and all liens or lien-rights against all real property owned by **FORT BEND COUNTY** in **FORT BEND COUNTY**, Texas, arising out of work performed or materials furnished for or in connection with construction of said project.

AMOUNT OF ORIGINAL CONTRACT:		\$4,645,912.45
CHANGE ORDERS -	C.O. 1	\$128,392.31
	C.O. 2	\$43,310.55
	C.O. 3	\$116,851.20
	C.O. 4	\$32,989.20
TOTAL ADJUSTED CONTRACT:		\$4,967,455.71
Value of Completed Work		\$1,530,608.19
Less Retention 10%		\$158,004.68
Net value of Completed Work		\$1,372,603.51
AMOUNT OF PREVIOUS INVOICES:		\$712,794.84
MATERIALS ON HAND		\$49,438.56
AMOUNT DUE THIS INVOICE:		\$709,247.23
TOTAL INVOICED TO DATE:		\$1,372,603.51
CONTRACT BALANCE:		\$3,594,852.20
Amount Retainage This Invoice		\$78,805.25
Amount Retainage Previous		\$79,199.43
Total Retainage to Date		\$158,004.68

ALLGOOD CONSTRUCTION COMPANY, INCORPORATED
By: *Sterling Moore*
Sterling Moore/President

STATE OF TEXAS
COUNTY OF FORT BEND

This Instrument was acknowledged before me on March 15th, 2018, by Sterling Moore, President of Allgood Construction Company, Incorporated, a Texas Corporation, on behalf of said corporation. Sworn to and subscribed before me, a notary public on this the 15th day of March, 2018.



Kelsie Moore
Notary Public for the State of Texas
My Commission Expires: 5-8-18

ALLGOOD CONSTRUCTION CO., INC. - 1706 FBC Pay Estimate No. 4

NO	DESCRIPTION	UNIT	CONT QTY	QTY THIS MO	CONTRACT UNIT PRICE	TOTAL AMT THIS MO	MATERIALS ON HAND	QTY PREV MO	TOTAL QTY TO DATE	TOTAL AMT TO DATE	% COMPL
A. SITE PREPARATION											
1	Fort Bend County Project Sign (Furnish, Install and Remove)	EA	2.00		\$ 569.25	\$0.00		2.00	2.00	\$1,138.50	100%
2	Clearing and Grubbing (Including Outfalls)	LS	1.00		\$ 61,893.00	\$0.00		1.00	1.00	\$61,893.00	100%
3	Removing Old Concrete Pavement	SY	5440.00		\$ 2.59	\$0.00			-	\$0.00	0%
4	Removing Old Concrete, 6" Reinforced Concrete Curb (Removal and Disposal)	LF	2800.00		\$ 2.30	\$0.00			-	\$0.00	0%
5	Roadway Excavation (Including 3" Striping)	CY	18500.00	6,000.00	\$ 7.48	\$44,880.00		5,500.00	11,500.00	\$86,020.00	70%
6	Remove and Dispose of Existing, Concrete or Metal Pipe (18" - 36")	LF	723.00		\$ 11.50	\$0.00		100.00	100.00	\$1,150.00	14%
7	Remove and Dispose of Existing Plastic Pipe (All type and all sizes)	LF	60.00		\$ 11.50	\$0.00		60.00	60.00	\$690.00	100%
8	Removing Old Structures - Inlets (All Depths)	EA	3.00		\$ 402.50	\$0.00			-	\$0.00	0%
9	Removing Old Structures - Safety End Treatments	EA	2.00		\$ 402.50	\$0.00		2.00	2.00	\$805.00	100%
10	Removing Old Structures - Headwalls including Wingwalls	EA	7.00		\$ 575.00	\$0.00		2.00	2.00	\$1,150.00	29%
11	Removing Flex Beam Guard Rail	LF	256.00		\$ 5.75	\$0.00			-	\$0.00	0%
12	Removing Turn Down Section	EA	2.00		\$ 575.00	\$0.00			-	\$0.00	0%
13	Removing Old Structures - Wooden Bridge	EA	1.00		\$ 5,750.00	\$0.00		1.00	1.00	\$5,750.00	100%
14	Remove and Relocate Traffic Signs, Mail Boxes, Roadway Signs	LS	1.00		\$ 1,725.00	\$0.00			-	\$0.00	0%
15	Remove and Relocate Traffic Signal Items (As Required)	LS	1.00		\$ 5,456.75	\$0.00			-	\$0.00	0%
16	Remove and dispose of existing asphaltic surface and base material	SY	4118.00		\$ 2.53	\$0.00			-	\$0.00	0%
SUBTOTAL OF SITE PREPARATION ITEMS						\$44,880.00				\$158,596.50	
B. SUBGRADE AND PAVING											
17	Hydrated Lime (Slurry Applied) for Stabilization (6% by Dry Weight)	TON	614.00	150.00	\$ 171.35	\$25,702.50		160.00	310.00	\$53,118.50	50%
18	Fly Ash for Stabilization (8% by Dry Weight)	TON	818.00		\$ 92.00	\$0.00			-	\$0.00	0%
19	Lime-Fly Ash Stabilized Subgrade, 2 Manipulations at 8" Depth	SY	30994.00	11,220.00	\$ 2.53	\$28,386.60		10,331.00	21,551.00	\$54,524.03	70%
20	Hot Mix Asphaltic Concrete Base Course (Black Base), 8" Depth	TON	396.00		\$ 109.25	\$0.00			-	\$0.00	0%
21	Prime Coat for Base Course (0.30 gal/sy)	GAL	360.00		\$ 5.75	\$0.00			-	\$0.00	0%
22	HMAC - Tack Coat (0.15 gal/sy)	TON	170.00		\$ 5.75	\$0.00			-	\$0.00	0%

ALLGOOD CONSTRUCTION CO., INC. - 1706 FBC Pay Estimate No. 4

NO	DESCRIPTION	UNIT	CONT QTY	QTY THIS MO	CONTRACT UNIT PRICE	TOTAL AMT THIS MO	MATERIALS ON HAND	QTY PREV MO	TOTAL QTY TO DATE	TOTAL AMT TO DATE	% COMPL
23	HMAC Type "D" Surface Course - 2" Thick	SY	93.00		\$ 112.70	\$0.00			-	\$0.00	0%
24	Reinforced Concrete Pavement - 8" Depth	SY	24930.00	6,100.00	\$ 43.10	\$262,910.00			6,100.00	\$262,910.00	24%
25	Reinforced Concrete Pavement, High Early Strength - 8" Depth	SY	6992.00		\$ 46.00	\$0.00			-	\$0.00	0%
26	Reinforced Concrete Pavement, High Early Strength - 8" Depth for Driveways	SY	994.00		\$ 80.50	\$0.00			-	\$0.00	0%
27	Cement Stabilized Sand, Complete in Place 8" Thick	SY	8689.00		\$ 9.27	\$0.00			-	\$0.00	0%
28	Furnish & Install Flex Beam Guard Rail, 12 Gauge with Mowing Strip	LF	555.00		\$ 43.13	\$0.00			-	\$0.00	0%
29	Furnish & Install Turn Down Terminal Section (25' long), 12 Gauge, with Anchor	EA	12.00		\$ 805.00	\$0.00			-	\$0.00	0%
30	6" Concrete Curbs	LF	19140.00	1,350.00	\$ 2.53	\$3,415.50			1,350.00	\$3,415.50	7%
31	Esplanades, Medians, and Directional Islands	SY	86.00		\$ 69.00	\$0.00			-	\$0.00	0%
32	Colored Concrete Medians (Black)	SY	86.00		\$ 5.75	\$0.00			-	\$0.00	0%
SUBTOTAL OF SUBGRADE AND PAVING ITEMS											\$373,968.03
C. STORM SEWER											
33	Structural Concrete, Wingwalls	CY	15.00	8.00	\$ 1,092.50	\$8,740.00		7.00	15.00	\$16,387.50	100%
34	Structural Concrete, Headwalls	CY	20.00	8.00	\$ 1,092.50	\$8,740.00		8.00	16.00	\$17,480.00	80%
35	Trench Safety Systems, 5' to 10' Depth	LF	6302.00	386.00	\$ 0.12	\$46.32		5,916.00	6,302.00	\$756.24	100%
36	Timber Bent for 48" Pipe	EA	1.00		\$ 1,150.00	\$0.00		1.00	1.00	\$1,150.00	100%
37	Corrugated Plastic Pipe, Pre-coated (12")	LF	30.00		\$ 28.75	\$0.00		30.00	30.00	\$862.50	100%
38	Reinforced Concrete Pipe, C76, Class III, Rubber Gasket (24")	LF	3394.00	285.00	\$ 40.12	\$11,434.20		2,755.00	3,040.00	\$121,964.80	90%
39	Reinforced Concrete Pipe, C76, Class III, Rubber Gasket (equivalent 24") Elliptical 19" X 30"	LF	410.00		\$ 91.16	\$0.00		210.00	210.00	\$19,143.60	51%
40	Reinforced Concrete Pipe, C76, Class III, Rubber Gasket (30")	LF	744.00		\$ 52.87	\$0.00		744.00	744.00	\$39,335.28	100%
41	Reinforced Concrete Pipe, C76, Class III, Rubber Gasket (42")	LF	601.00	74.00	\$ 86.10	\$6,371.40		550.00	624.00	\$53,726.40	104%
42	Reinforced Concrete Pipe, C76, Class III, Rubber Gasket (48")	LF	1101.00		\$ 99.99	\$0.00		1,159.00	1,159.00	\$115,888.41	105%
43	Corrugated Metal Pipe-Pre-coated-Galvanized (16 Gauge) (24")	LF	129.00		\$ 39.10	\$0.00		105.00	105.00	\$4,105.50	81%
44	Corrugated Metal Pipe-Pre-coated-Galvanized (16 Gauge) (30")	LF	133.00		\$ 49.45	\$0.00		133.00	133.00	\$6,576.85	100%
45	Corrugated Metal Pipe-Pre-coated-Galvanized (16 Gauge) (48")	LF	118.00		\$ 95.45	\$0.00		118.00	118.00	\$11,263.10	100%

ALLGOOD CONSTRUCTION CO., INC. - 1706 FBC Pay Estimate No. 4

NO	DESCRIPTION	UNIT	CONT QTY	QTY THIS MO	CONTRACT UNIT PRICE	TOTAL AMT THIS MO	MATERIALS ON HAND	QTY PREV MO	TOTAL QTY TO DATE	TOTAL AMT TO DATE	% COMPL
46	Safety End Treatment - Type II, (6:1) (PD-SPR) 24" RCP	EA	2.00		\$ 1,477.75	\$0.00		2.00	2.00	\$2,955.50	100%
47	Safety End Treatment SET (TY II) (24IN) (RCP) (6:1) (P)	EA	2.00	2.00	\$ 1,006.25	\$2,012.50			2.00	\$2,012.50	100%
48	Precast Concrete Shallow Manhole, with a depth less than 6 feet	EA	16.00	2.00	\$ 2,587.50	\$5,175.00		12.00	14.00	\$36,225.00	88%
49	Precast Concrete Standard Manhole, with a depth greater than 6 feet & less than 10 feet	EA	3.00		\$ 2,725.50	\$0.00		3.00	3.00	\$8,176.50	100%
50	Precast Concrete Extra Depth Manhole, with a depth greater than 10 feet	EA	11.00		\$ 5,163.50	\$0.00		11.00	11.00	\$56,798.50	100%
51	Type "A" Inlet with Additional Depth greater than 6'	EA	5.00		\$ 1,569.75	\$0.00		5.00	5.00	\$7,848.75	100%
52	Standard Type "A" Inlet Modified Square (Pre-Cast or Cast) greater than 6'	EA	7.00	1.00	\$ 1,144.25	\$1,144.25		6.00	7.00	\$8,009.75	100%
53	Standard Type "B-B" Inlet	EA	12.00	1.00	\$ 1,788.25	\$1,788.25		10.00	11.00	\$19,670.75	92%
54	Type "B-B" Inlet with Additional Depth greater than 6'	EA	7.00		\$ 2,179.25	\$0.00		4.00	4.00	\$8,717.00	57%
55	Type "B-B" (Modified) Inlet with Additional Depth greater than 6'	EA	5.00		\$ 2,380.50	\$0.00		5.00	5.00	\$11,902.50	100%
56	Reinforced Concrete Box,C1433 (All Depths) - (5' x 3')	LF	174.00		\$ 162.60	\$0.00		174.00	174.00	\$28,292.40	100%
57	Reinforced Concrete Slope Paving (4" thick)	SY	215.00		\$ 92.00	\$0.00			-	\$0.00	0%
58	Reinforced Concrete Slope Paving (5" thick)	SY	1492.00		\$ 78.20	\$0.00			-	\$0.00	0%
59	Riprap - Gradation No. 1 (18" thick)	SY	250.00		\$ 86.25	\$0.00			-	\$0.00	0%
SUBTOTAL OF STORM SEWER ITEMS						\$45,451.92				\$599,249.33	
D. TRAFFIC CONTROL											
60	Work Zone Pavement Markings 4" White/Solid (Removable) Furnished -Applied & Removed	LF	1654.00		\$ 0.69	\$0.00			-	\$0.00	0%
61	Work Zone Pavement Markings 8" White/Solid (Removable) Furnished-Applied & Removed	LF	120.00		\$ 1.73	\$0.00			-	\$0.00	0%
62	Work Zone Pavement Markings 24" White/Solid (Removable) Applied & Removed	LF	59.00		\$ 4.03	\$0.00			-	\$0.00	0%
63	Work Zone Pavement Markings 4" Yellow/Solid (Removable) Furnished-Applied & Removed	LF	9424.00		\$ 0.59	\$0.00			-	\$0.00	0%
64	Work Zone Pavement Markings 8" White/Dashed (Removable) Furnished-Applied & Removed (4' over	LF	105.00		\$ 2.30	\$0.00			-	\$0.00	0%
65	Traffic Control - Furnish-Install & Remove	MON	11.00	1.00	\$ 1,790.55	\$1,790.55		2.50	3.50	\$6,266.93	32%
66	Temporary Commercial Driveways - Furnish-Install & Remove	EA	3.00		\$ 2,875.00	\$0.00			-	\$0.00	0%
67	Temporary Traffic Signal at FM 762 and Williams Way Boulevard (Relocate Signal Heads/Bag)	LS	1.00		\$ 9,487.50	\$0.00			-	\$0.00	0%
68	Constructing Detours for Two-Way Traffic (8" Black Base) for Installing-Maintaining & Removal	SY	206.00		\$ 65.96	\$0.00			-	\$0.00	0%

ALLGOOD CONSTRUCTION CO., INC. - 1706 FBC Pay Estimate No. 4

NO	DESCRIPTION	UNIT	CONT QTY	QTY THIS MO	CONTRACT UNIT PRICE	TOTAL AMT THIS MO	MATERIALS ON HAND	QTY PREV MO	TOTAL QTY TO DATE	TOTAL AMT TO DATE	% COMPL
69	Low Profile Concrete Barrier Type 1(Furnish and Install)	LF	805.00		\$ 28.75	\$0.00			-	\$0.00	0%
70	Low Profile Concrete Barrier Type 1 (Relocate)	LF	2474.00		\$ 11.50	\$0.00			-	\$0.00	0%
71	Low Profile Concrete Barrier Type 1 (Remove)	LF	805.00		\$ 17.25	\$0.00			-	\$0.00	0%
72	Low Profile Concrete Barrier Type 2 (Furnish and Install)	LF	80.00		\$ 28.75	\$0.00			-	\$0.00	0%
73	Low Profile Concrete Barrier Type 2 (Relocate)	LF	140.00		\$ 11.50	\$0.00			-	\$0.00	0%
74	Low Profile Concrete Barrier Type 2 (Remove)	LF	80.00		\$ 17.25	\$0.00			-	\$0.00	0%
SUBTOTAL OF TRAFFIC CONTROL ITEMS						\$1,790.55				\$6,266.93	
E. SIGNING AND PAVEMENT MARKING											
75	Solid Cast Aluminium Bridge Plaque	EA	2.00		\$ 2,300.00	\$0.00			-	\$0.00	0%
76	Aluminum Signs (Ground Mounted)- Furnish & Install	EA	45.00		\$ 253.00	\$0.00			-	\$0.00	0%
77	Furnish and Install Object Marker (Texas MUTCD: "OM-3R/L")	EA	2.00		\$ 151.80	\$0.00			-	\$0.00	0%
78	Reflectorized Pavement Markings Type I (Thermoplastic) 4" White/Solid - Furnish & Applied	LF	40.00		\$ 0.67	\$0.00			-	\$0.00	0%
78A	Reflectorized Pavement Markings Type 1 (Thermoplastic) 4" Yellow/Solid - Furnish & Applied	LF	1310.00		\$ 0.85	\$0.00			-	\$0.00	0%
79	Reflectorized Pavement Markings Type I (Thermoplastic) 8" White/Solid - Furnish & Applied	LF	824.00		\$ 1.21	\$0.00			-	\$0.00	0%
80	Reflectorized Pavement Markings Type I (Thermoplastic) 12" White/Solid - Furnish & Applied	LF	416.00		\$ 2.47	\$0.00			-	\$0.00	0%
81	Reflectorized Pavement Markings Type I (Thermoplastic) 24" White/Solid - Furnish & Applied	LF	636.00		\$ 5.18	\$0.00			-	\$0.00	0%
81A	Reflectorized Pavement Markings type 1 (Thermoplastic) 24" Yellow/Solid - Furnish and Applied	LF	115.00		\$ 8.00	\$0.00			-	\$0.00	0%
82	Reflectorized Pavement Markings Type I (Thermoplastic) 4" White/Dashed - Furnish & Applied	LF	9728.00		\$ 0.71	\$0.00			-	\$0.00	0%
83	Reflectorized Pavement Markings Type I (Thermoplastic) Single Arrow-LEFT - Furnish &	EA	10.00		\$ 132.25	\$0.00			-	\$0.00	0%
84	Reflectorized Pavement Markings Type I (Thermoplastic) RIGHT-STRAIGHT Combination	EA	2.00		\$ 132.25	\$0.00			-	\$0.00	0%
85	Reflectorized Pavement Markings Type I (Thermoplastic) Word "ONLY" - Furnish & Applied	EA	8.00		\$ 126.50	\$0.00			-	\$0.00	0%
86	Reflectorized Pavement Markings Type II, 12" Yellow/Solid, for 6" curb per Detail "D", Furnish &	LF	3020.00		\$ 0.92	\$0.00			-	\$0.00	0%
87	Reflectorized Pavement Markers Type I-C - Furnish & Install	EA	0.00		\$ 3.16	\$0.00			-	\$0.00	0%
88	Reflectorized Pavement Markers Type II-C-R - Furnish & Install	EA	385.00		\$ 3.16	\$0.00			-	\$0.00	0%
88A	Reflectorized Pavement Markers Type II-A-A - Furnish & Install	EA	80.00		\$ 5.50	\$0.00			-	\$0.00	0%

ALLGOOD CONSTRUCTION CO., INC. - 1706 FBC Pay Estimate No. 4

NO	DESCRIPTION	UNIT	CONT QTY	QTY THIS MO	CONTRACT UNIT PRICE	TOTAL AMT THIS MO	MATERIALS ON HAND	QTY PREV MO	TOTAL QTY TO DATE	TOTAL AMT TO DATE	% COMPL
89	Non-ReflectORIZED Ceramic Traffic Buttons (White) - Furnish & Install	EA	222.00		\$ 2.59	\$0.00			-	\$0.00	0%
SUBTOTAL OF SIGNING AND PAVEMENT MARKING ITEMS											
F. PERMANENT TRAFFIC SIGNALS (TXDOT Specifications)											
90	Drilled Shaft Foundation (TRF SIG. POLE)	LF	30.00		\$ 417.83	\$0.00			-	\$0.00	0%
91	Conduit (PVC) (SCHD 80) (2")	LF	150.00		\$ 7.39	\$0.00			-	\$0.00	0%
92	Electrical Conductors (No. 6) BARE	LF	145.00		\$ 2.20	\$0.00			-	\$0.00	0%
93	Tray Cable (4 CONR) (12 AWG)	LF	400.00		\$ 2.47	\$0.00			-	\$0.00	0%
94	Ground Boxes TY D (162922) W/ Apron	EA	1.00		\$ 1,270.75	\$0.00			-	\$0.00	0%
95	Zinc-Coated Steel Wire Strand (5/16 IN)	LF	400.00		\$ 4.27	\$0.00			-	\$0.00	0%
96	Zinc-Coated Steel Wire Strand (1/4 IN)	LF	400.00		\$ 4.19	\$0.00			-	\$0.00	0%
97	Zinc-Coated Steel Wire Strand (3/8 IN)	LF	400.00		\$ 4.35	\$0.00			-	\$0.00	0%
98	Intail Small Roadside Sign Assemblies TY 10BWG (1) SA (P)	EA	2.00		\$ 784.88	\$0.00			-	\$0.00	0%
99	"NO PEDESTRIAN CROSSING" (R9-3) (12" x 18")	EA	2.00		\$ 373.75	\$0.00			-	\$0.00	0%
100	"NO PEDESTRIAN CROSSING" (R9-3A) (18"x18")	EA	2.00		\$ 373.75	\$0.00			-	\$0.00	0%
101	RetorelectORIZED Pavement Markings TY I (W) 24" (SLD) (100 MIL)	LF	125.00		\$ 5.75	\$0.00			-	\$0.00	0%
102	Pavement Sealer 24"	LF	125.00		\$ 0.60	\$0.00			-	\$0.00	0%
103	Pavement Surface Preparation for Marking (BLAST CLN) (24")	LF	125.00		\$ 0.60	\$0.00			-	\$0.00	0%
104	Install Highway Traffic Signals (ISOLATED)	EA	1.00		\$ 16,445.00	\$0.00			-	\$0.00	0%
105	POLE 34' STEEL STRAIN	EA	2.00		\$ 7,624.50	\$0.00			-	\$0.00	0%
106	RDWY LIGHT ON TRAF SIGNAL POLE (250 WATT H.P.S.)	EA	1.00		\$ 867.10	\$0.00			-	\$0.00	0%
107	MAST ARM, 10' LUMINAIRE	EA	2.00		\$ 1,304.40	\$0.00			-	\$0.00	0%
108	Traffic Signal Cables (TY A) (12 AWG) (4 CONDR)	LF	270.00		\$ 2.25	\$0.00			-	\$0.00	0%
109	Traffic Signal Cables (TY A) (12 AWG) (7 CONDR)	LF	1050.00		\$ 2.55	\$0.00			-	\$0.00	0%
110	VIVDS Communication Cable (COAXIAL)	LF	1310.00		\$ 2.61	\$0.00			-	\$0.00	0%
111	3/C #16 - VIVDS POWER CABLE	LF	1310.00		\$ 2.61	\$0.00			-	\$0.00	0%

ALLGOOD CONSTRUCTION CO., INC. - 1706 FBC Pay Estimate No. 4

NO	DESCRIPTION	UNIT	CONT QTY	QTY THIS MO	CONTRACT UNIT PRICE	TOTAL AMT THIS MO	MATERIALS ON HAND	QTY PREV MO	TOTAL QTY TO DATE	TOTAL AMT TO DATE	% COMPL
SUBTOTAL OF PERMANENT TRAFFIC SIGNALS											
						\$0.00				\$0.00	
G. BRIDGE STRUCTURE (TxDOT Specifications)											
112	Cement Stabilized Backfill	CY	180.00		\$ 89.25	\$0.00			-	\$0.00	0%
113	Drilled Shaft Foundations (18-inch)	LF	112.00	56.00	\$ 68.25	\$3,822.00			56.00	\$3,822.00	50%
114	Drilled Shaft Foundations (36-inch)	LF	1736.00	910.00	\$ 231.00	\$210,210.00			910.00	\$210,210.00	52%
115	Concrete Structures (Class C Concrete) - Abutments	CY	86.00		\$ 866.25	\$0.00			-	\$0.00	0%
116	Concrete Structures (Class C Concrete) - Bents	CY	117.00		\$ 918.75	\$0.00	\$15,085.14		-	\$0.00	0%
117	Reinforced Concrete Slab	SF	14904.00		\$ 15.23	\$0.00			-	\$0.00	0%
118	Bridge Median	SF	1776.00		\$ 15.59	\$0.00			-	\$0.00	0%
119	Bridge Sidewalk	SF	4440.00		\$ 13.13	\$0.00			-	\$0.00	0%
120	Bridge Approach Slab	CY	242.00		\$ 446.25	\$0.00			-	\$0.00	0%
121	Precast Prestressed Concrete Structural Members (Prestressed Concrete Girder, TX34)	LF	1715.00		\$ 132.83	\$0.00	\$34,353.42		-	\$0.00	0%
122	Metal for Structures (Structural Steel) (Misc Non Bridge)	LB	582.00		\$ 11.55	\$0.00			-	\$0.00	0%
123	Railing (TY C223)	LF	492.00		\$ 136.50	\$0.00			-	\$0.00	0%
124	Bridge Expansion Joints, Sealed Expansion Joint (4- inch) (SEJ-A)	LF	130.00		\$ 128.10	\$0.00			-	\$0.00	0%
	SUBTOTAL OF BRIDGE ITEMS					\$214,032.00	\$49,438.56			\$214,032.00	
H. STORM WATER POLLUTION PREVENTION											
125	Sodding for Erosion Control and Stabilization	LF	11858.00		\$ 3.16	\$0.00			-	\$0.00	0%
126	Hydro-mulch Seeding	ACRE	5.00		\$ 1,437.50	\$0.00			-	\$0.00	0%
127	Reinforced Filter Fabric Barrier (60% of unit cost for furnish and installation and 40% of unit cost for removal)	LF	5610.00		\$ 1.44	\$0.00			-	\$0.00	0%
128	Inlet Protection Barrier (Stage 1, With Fiber Rolls, 60% of unit cost for furnish and installation, and 40% of unit cost for removal)	EA	35.00	1.00	\$ 51.75	\$51.75		20.00	21.00	\$1,086.75	60%
129	Stabilized Construction Access, Type 1 Rock	SY	222.00		\$ 11.50	\$0.00		222.00	222.00	\$2,553.00	100%

ALLGOOD CONSTRUCTION CO., INC. - 1706 FBC Pay Estimate No. 4

NO	DESCRIPTION	UNIT	CONT QTY	QTY THIS MO	CONTRACT UNIT PRICE	TOTAL AMT THIS MO	MATERIALS ON HAND	QTY PREV MO	TOTAL QTY TO DATE	TOTAL AMT TO DATE	% COMPL
130	Concrete Truck Washout Structures (60% of unit cost for furnish and installation, and 40% of unit cost for removal)	LS	1.00	0.60	\$ 977.50	\$586.50			0.60	\$586.50	60%
131	Inlet Protection Barrier (For Stage II Inlets, Gravel Bags; 60% of unit cost for furnish and installation, and 40% of unit cost removal)	EA	24.00		\$ 11.50	\$0.00		12.00	12.00	\$138.00	50%
132	Rock Filter Dam (Type 3; 60% of unit cost for furnish and installation, and 40% of unit cost for removal)	LF	80.00		\$ 29.90	\$0.00			-	\$0.00	0%
133	Reinforced Silt Fence (60% of unit cost for furnish and installation, and 40% of unit cost for removal)	LF	680.00		\$ 1.44	\$0.00			-	\$0.00	0%
134	SWPPP Inspection and Maintenance (Min. Bid - \$6,000/Month)	MONTH	11.00	1.00	\$ 6,000.00	\$6,000.00		2.50	3.50	\$21,000.00	32%
135	TPDES General Permit No. TXR 150000, Notice of Intent (NOI) Application Fees (Contractor's NOI Fee & Fort Bend County's NOI Fee, Each Fee shall be set price of \$325.00)	EA	2.00		\$ 325.00	\$0.00		2.00	2.00	\$650.00	100%
SUBTOTAL OF STORM WATER POLLUTION PREVENTION ITEMS						\$6,638.25				\$26,014.25	
I. EXTRA WORK											
136	Seal Slab, Class D Concrete, 7" thickness (Min. Bid \$25/SY)	SY	200.00		\$ 25.00	\$0.00			-	\$0.00	0%
137	Well Pointing System (Min. Bid \$15/LF)	LF	500.00		\$ 15.00	\$0.00			-	\$0.00	0%
138	5-Strand Barbed Wire Fence	LF	1227.00		\$ 6.49	\$0.00		1,100.00	1,100.00	\$7,139.00	90%
139	5-Strand Slick Wire Fence	LF	1000.00		\$ 6.50	\$0.00			-	\$0.00	0%
140	Galvanized Tube Gates, TY 2 Gate	EA	2.00		\$ 550.00	\$0.00		2.00	2.00	\$1,100.00	100%
141	Construction Safety Fence	LF	1000.00		\$ 1.25	\$0.00		120.00	120.00	\$150.00	12%
142	Mowing Project Site	CY	4.00		\$ 500.00	\$0.00			-	\$0.00	0%
143	Uniform Peace Officer (Minimum: \$25/HR)	HOUF	200.00		\$ 25.00	\$0.00			-	\$0.00	0%
144	Electrical Riser Relocation for Property Owner (Customer Owned)-Connection to Centerpoint Energy	LF	200.00		\$ 35.66	\$0.00			-	\$0.00	0%
145	Electrical Riser Relocation for Property Owner (Customer Owned)-Connection to Centerpoint Energy	LF	200.00		\$ 43.14	\$0.00			-	\$0.00	0%
SUBTOTAL OF EXTRA WORK ITEMS						\$0.00				\$8,389.00	
J. C.O. NO. 2 ITEMS											
146	72" CMP (To become property of FBC after removal)	LF	80.00		\$ 191.86	\$0.00		80.00	80.00	\$15,348.80	100%
147	Ditch Fill and Grading	LS	1.00		\$ 7,883.75	\$0.00		1.00	1.00	\$7,883.75	100%
					3/8/2018	1706 FBC Pay Estimate No. 4					

ALLGOOD CONSTRUCTION CO., INC. - 1706 FBC Pay Estimate No. 4

NO	DESCRIPTION	UNIT	CONT QTY	QTY THIS MO	CONTRACT UNIT PRICE	TOTAL AMT THIS MO	MATERIALS ON HAND	QTY PREV MO	TOTAL QTY TO DATE	TOTAL AMT TO DATE	% COMPL
148	Bank Cut and Grading	LS	1.00		\$ 2,500.00	\$0.00		1.00	1.00	\$2,500.00	100%
149	6" Crushed Concrete Drive 12' Wide X 131' Long	SY	175.00		\$ 31.16	\$0.00		175.00	175.00	\$5,453.00	100%
150	Removal of Low Water Crossing After Bridge Is Constructed	LS	1.00		\$ 3,125.00	\$0.00			-	\$0.00	0%
151	Hydromulch Ditch when Complete	EA	1.00		\$ 1,500.00	\$0.00			-	\$0.00	0%
152	Emergency Inlet Repair, Station 103+87 Williams Way	EA	1.00		\$ 7,500.00	\$0.00		1.00	1.00	\$7,500.00	100%
SUBTOTAL OF C.O. NO. 2 ITEMS						\$0.00				\$38,685.55	
K. C.O. NO. 3 ITEMS											
153	12" C900 PVC CL 150 Waterline (Including fittings, all depths, complete in place)	LF	369.00	369.00	\$ 34.61	\$12,771.09			369.00	\$12,771.09	100%
154	12" Restrained Joint Waterline (Including Fittings, All Depths, Complete in Place)	LF	91.00	91.00	\$ 96.31	\$8,764.21			91.00	\$8,764.21	100%
155	12" Waterline Casing (All Depths, Complete in Place)	LF	137.00	137.00	\$ 102.00	\$13,974.00			137.00	\$13,974.00	100%
156	12" TS&V W/ Box	EA	2.00	2.00	\$ 6,000.00	\$12,000.00			2.00	\$12,000.00	100%
157	12" Gate Valve & Box	EA	1.00	1.00	\$ 2,410.73	\$2,410.73			1.00	\$2,410.73	100%
158	Fire Hydrants (All Depths, Including 6" Tee & Gate Valve & Box)	EA	1.00	1.00	\$ 4,129.01	\$4,129.01			1.00	\$4,129.01	100%
159	6" C900 PVC CL 150 Fire Hydrant Lead	LF	6.00	6.00	\$ 24.00	\$144.00			6.00	\$144.00	100%
160	Fire Hydrant Reflector (To Be Added To Pavement Upon Roadway Completion - Per City Of Richmond Design	EA	1.00		\$ 18.00	\$0.00			-	\$0.00	0%
161	2" Blow-Off Valve & Box	EA	1.00	1.00	\$ 420.00	\$420.00			1.00	\$420.00	100%
162	Remove and Salvage Existing Fire Hydrant, Backfill and Compact Voids (Provide to City)	LS	1.00	1.00	\$ 900.00	\$900.00			1.00	\$900.00	100%
163	Remove and Salvage Existing Fire Hydrant, Backfill and Compact Voids (Provide to City)	LS	1.00	-	\$ 900.00	\$0.00			-	\$0.00	0%
164	Remove & Dispose of Existing 12" Gate Valves & Boxes, Backfill and Compact Voids	EA	2.00	2.00	\$ 600.00	\$1,200.00			2.00	\$1,200.00	100%
165	12" Plug & Clamp (Proposed Line)	EA	1.00	1.00	\$ 540.00	\$540.00			1.00	\$540.00	100%
166	12" Plug & Clamp (Abandoned Existing 12" Line)	EA	2.00	2.00	\$ 600.00	\$1,200.00			2.00	\$1,200.00	100%
167	Grout (Fill Abandoned Existing 12" Waterline)	CY	4.00	4.00	\$ 872.40	\$3,489.60			4.00	\$3,489.60	100%
168	Connection To Existing 4" Force Main	EA	2.00	2.00	\$ 180.00	\$360.00			2.00	\$360.00	100%
169	4" C900 PVC CL 150 Sanitary Sewer Force Main (Including Fittings, All Depths, Complete in Place)	LF	555.00	555.00	\$ 19.30	\$10,711.50			555.00	\$10,711.50	100%
170	Sewage Air Release Valve	EA	2.00	2.00	\$ 4,200.00	\$8,400.00			2.00	\$8,400.00	100%

ALLGOOD CONSTRUCTION CO., INC. - 1706 FBC Pay Estimate No. 4

NO	DESCRIPTION	UNIT	CONT QTY	QTY THIS MO	CONTRACT UNIT PRICE	TOTAL AMT THIS MO	MATERIALS ON HAND	QTY PREV MO	TOTAL QTY TO DATE	TOTAL AMT TO DATE	% COMPL
171	Sanitary Sewer Manhole (All Depths, Complete In Place)	EA	2.00	2.00	\$ 2,364.00	\$4,728.00			2.00	\$4,728.00	100%
172	4" Plug & Clamp (Abandoned Force Main)	EA	2.00	2.00	\$ 420.00	\$840.00			2.00	\$840.00	100%
173	4" Sanitary Force Main Casing (All Depths, Complete In Place)	LF	112.00	112.00	\$ 77.88	\$8,722.56			112.00	\$8,722.56	100%
174	OSHA Trench Safety System	LF	1025.00	1,025.00	\$ 0.14	\$143.50			1,025.00	\$143.50	100%
175	Utility Spoils (To Be Disposed of Off-Site)	CY	165.00	165.00	\$ 9.00	\$1,485.00			165.00	\$1,485.00	100%
176	Extra Bank Sand (To Be Used Only With Authorization From The Engineer)	CY	100.00		\$ 14.40	\$0.00			-	\$0.00	0%
177	Extra Cement Stabilized Sand (To Be Used Only With Authorization From The Engineer)	CY	100.00		\$ 21.60	\$0.00			-	\$0.00	0%
178	Dewatering (To Be Used Only With The Authorization From The Engineer)	LF	500.00		\$ 30.00	\$0.00			-	\$0.00	0%
SUBTOTAL OF C.O. NO. 3 ITEMS						\$97,333.20					

L. C.O. NO. 4 ITEMS

179	EXTRA NO. 4 REBAR TO MEET FBC STANDARD OF 18"X18" SPACING (LONGITUDINAL/ TRANSVERSE)	LB	89160.00	21,820.00	\$ 0.37	\$8,073.40			21,820.00	\$8,073.40	24%
SUBTOTAL OF C.O. NO. 4 ITEMS						\$8,073.40					

GRAND TOTAL FOR ITEMS (A TO K)

GRAND TOTAL						\$738,613.92	TOTAL THIS MONTH	PROJECT TO DATE
							\$1,530,608.19	33%

APPROVED: _____ DATE: _____

471

BEXAR CONCRETE WORKS I, LTD
PO BOX 700250
SAN ANTONIO, TX 78270

0118207

INVOICE

Invoice #: 589650
Date: 01/25/2018
Page: Page 1 of 1

BILL TO	TOM-MAC PO BOX 262541 HOUSTON, TX 77207	SHIP TO	TOM-MAC PO BOX 262541 HOUSTON, TX 77207
----------------	---	----------------	---

Customer # 202	Customer PO# 6580			Terms 10TH OF NEXT MONTH	Due Date 02/10/2018			
Project # WILLIAMS WAY	County FORT BEND	Job # 5540		PPD/COLL/PP&A PRE-PAID				
ITEM	DESCRIPTION			UOM	QTY SHIPPED	QTY APPROVED	UNIT PRICE	NET PRICE

1	PANELS	SF		970.57	5.380	5,221.66
				LESS FREIGHT:	0.790	766.75
				LESS BEARING PADS:	0.000	0.00

DETAILS							
Part Description		EA	Qty Shipped	Qty Approved			
5540.C1		22		970.57			
Lot Number							
M-1-22-01/12/18							

6580 4020 ~~43~~ 4,454.91

POSTED

TOTAL APPROVED TO DATE	TOTAL SHIPPED TO DATE	UOM
970.57	0.00	SF

Sub Total: 4,454.91
Handling: 0.00
Freight: 0.00
Sales Tax: 0.00
TOTAL: 4,454.91

BEXAR CONCRETE WORKS I, LTD
PO BOX 700250
SAN ANTONIO, TX 78270

471

0218053
INVOICE

Invoice #: 589829

Date: 02/01/2018

Page: Page 1 of 1

BILL TO	TOM-MAC PO BOX 262541 HOUSTON, TX 77207			SHIP TO	TOM-MAC PO BOX 262541 HOUSTON, TX 77207		

Customer # 202	Customer PO# 6580		Terms 10TH OF NEXT MONTH	Due Date 02/10/2018
Project # WILLIAMS WAY	County FORT BEND	Job # 5540	PPD/COLL/PP&A PRE-PAID	

ITEM	DESCRIPTION	UOM	QTY SHIPPED	QTY APPROVED	UNIT PRICE	NET PRICE
1	PANELS	SF		5,631.50	5.380	30,297.47
				LESS FREIGHT:	0.790	4,448.88
				LESS BEARING PADS:	0.000	0.00
	DETAILS					
	Part Description	EA	Qty Shipped	Qty Approved		
	8.0S-7.0	82		4,592.00		
	Lot Number					
	R-1-82-01/22/18					
	5.5S-7.0	27		1,039.50		
	Lot Number					
	H-11-37-01/18/18					
2	PANELS	SF		882.34	5.380	4,746.97
				LESS FREIGHT:	0.790	697.05
				LESS BEARING PADS:	0.000	0.00
	DETAILS					
	Part Description	EA	Qty Shipped	Qty Approved		
	5540.C1	20		882.34		
	Lot Number					
	M-1-20-01/19/18					
6580 4020 29.87851						
						

TOTAL APPROVED TO DATE	TOTAL SHIPPED TO DATE	UOM
7,484.41	0.00	SF

Sub Total: 29,898.51
Handling: 0.00
Freight: 0.00
Sales Tax: 0.00
TOTAL: 29,898.51

**Correspondence**

CMC Rebar
1 Steel Mill Drive
SEGUIN TX 78155-7515 USA
Phone: 214 631 5250
Fax: 214 637 1110

Payment Options
ACH Payments made to: Bank of America, N.A., New York
Check Payments made to: Commercial Metals Company
ABA # [REDACTED] ATTN: 1439
Account # [REDACTED] P.O. Box 844579
For Credit to Commercial Metals Company Dallas, TX 75284-4579
Online Payments: www.cmc.com/payments

CMC Rebar Houston-West
T028

BILL TO PARTY 3031666
Tom-Mac Inc
P.O Box 262541
Houston, TX 77207-0000

SALES INVOICE

Invoice No / Date: 92309484 01/31/2018
Salesorder/Ref No:
Customer : 3031666
Job : R/1723300768
Salesperson :
SHIP TO PARTY 3100102
Fort Bend Co - Williams Way Blvd.
59 To 762, Job # 6580 (Dw)
Williams Way Blvd. (59 to 762)
Richmond, TX 77469-0000

SHIP VIA		INCO-TERMS		PAYMENT TERMS	
Road / Truck		CPT Richmond		Net Due in 30 Days	
ITEM	DESCRIPTION	QTY-SHPP	PRICE	AMOUNT	
Reinforcing Steel by STR per CC OHWA ,Rel 1 - ABUT 1 DS @ FM 762 TO 59 NB FRTG RD PO# BOL# 72330910 Del# 3045729					
	Rebar Black 60/420	14,454.00 LB	34.50/CWT	4,986.63	
	Round Black 420/60	2,459.00 LB	34.50/CWT	848.36	
Reinforcing Steel by STR per CC OHWC ,Rel 2 - BENT 2 DS @ FM 762 TO 59 NB FRTG RD PO# BOL# 72330910 Del# 3045730					
	Rebar Black 60/420	19,079.00 LB	34.50/CWT	6,582.26	
	Round Black 420/60	2,982.00 LB	34.50/CWT	1,028.79	
REBAR Weight: 38,974.00 LB		Line Totals:		\$13,446.04	
		Tax:		\$0.00	
		Freight:		\$0.00	
		Total Invoice Value:		\$13,446.04	



1034

Correspondence

CMC Rebar
1 Steel Mill Drive
SEGUIN TX 78155-7515 USA
Phone: 214 631 5250
Fax: 214 637 1110

Payment Options

ACH Payments made to:
Bank of America, N.A., New York
ABA # [REDACTED]
Account # [REDACTED]
For Credit to Commercial Metals
Company

Check Payments made to:
Commercial Metals Company
ATTN: 1439
P.O. Box 844579
Dallas, TX 75284-4579

Online Payments: www.cmc.com/payments

SALES INVOICE

CMC Rebar Houston-West
T028

Invoice No / Date: 92309483 01/31/2018

Salesorder/Ref No:

Customer : 3031666

Job : R/1723300768

Salesperson :

BILL TO PARTY 3031666

Tom-Mac Inc
P.O Box 262541
Houston, TX 77207-0000

SHIP TO PARTY 3100102

Fort Bend Co - Williams Way Blvd.
59 To 762, Job # 6580 (Dw)
Williams Way Blvd. (59 to 762)
Richmond, TX 77469-0000

SHIP-VIA		INCO-TERMS		PAYMENT-TERMS	
Road / Truck		CPT Richmond		Net Due in 30 Days	
ITEM	DESCRIPTION	QTY	UNIT	PRICE	AMOUNT
Reinforcing Steel by STR per CC 0HWD ,Rel 3 - BENT 3 DS @ FM 762 TO 59 NB FRTG RD PO# BOL# 72330925 Del# 3045739					
	Rebar Black 60/420	20,507.00	LB	34.50/CWT	7,074.92
	Round Black 420/60	3,234.00	LB	34.50/CWT	1,115.73
Reinforcing Steel by STR per CC 0HWF ,Rel 5 - BENT 2 COL @ FM 762 - 59 NB FRTG RD PO# BOL# 72330925 Del# 3045744					
	Rebar Black 60/420	3,491.00	LB	34.50/CWT	1,204.40
	Round Black 420/60	560.00	LB		
Reinforcing Steel by STR per CC 0HWG ,Rel 6 - BENT 3 COL @ FM 762 - 59 NB FRTG RD PO# BOL# 72330925 Del# 3045748					
	Rebar Black 60/420	3,729.00	LB	34.50/CWT	1,286.51
	Round Black 420/60	602.00	LB	34.50/CWT	207.69

6580 4020 10,889.25



REBAR Weight: 32,123.00 LB

Line Totals: \$10,889.25

Tax: \$0.00

Freight: \$0.00

Total Invoice Value: \$10,889.25



1054
Correspondence

CMC Rebar
1 Steel Mill Drive
SEGUIN TX 78155-7515 USA
Phone: 214 631 5250
Fax: 214 637 1110

2218127
Payment Options
ACH Payments made to:
Bank of America, N.A., New York
ABA # [REDACTED]
Account # [REDACTED]
For Credit to Commercial Metals Company
Check Payments made to:
Commercial Metals Company
ATTN: 1439
P.O. Box 844579
Dallas, TX 75284-4579
Online Payments: www.cmc.com/payments

SALES INVOICE

CMC Rebar Houston-West
T028

SHIP TO PARTY 3031666

Tom-Mac Inc
P.O Box 262541
Houston, TX 77207-0000

Invoice No / Date: 92313028 02/05/2018

Salesorder/Ref No:

Customer : 3031666

Job : R/1723300768

Salesperson :

SHIP TO PARTY 3100102

Fort Bend Co - Williams Way Blvd.
59 To 762, Job # 6580 (Dw)
Williams Way Blvd. (59 to 762)
Richmond, TX 77469-0000

SHIP VIA		INCO-TERMS		PAYMENT TERMS	
Road / Truck		CPT Richmond		Net Due in 30 Days	
ITEM	DESCRIPTION	QTY-SHPD	PRICE	AMOUNT	
Reinforcing Steel by STR per CC OHWE ,Rel 4 - ABUT 4 DS @ FM 762 TO 59 NE FRTG RD PO# BOL# 72331905 Del# 3046654					
	Rebar Black 60/420	14,454.00 LB	34.50/CWT	4,986.63	
	Round Black 420/60	2,459.00 LB	34.50/CWT	848.36	
6580 4020 5183499					
POSTED					
REBAR Weight: 16,913.00 LB		Line Totals:		\$5,834.99	
		Tax:		\$0.00	
		Freight:		\$0.00	
		Total Invoice Value:		\$5,834.99	

Bexar Concrete Works I, Ltd.
PO Box 700250
San Antonio, TX 78270
Tel. (210) 497-3773 Fax. (210) 497-3810

March 15, 2018


To whom it may concern:

Please note that all material invoiced has been produced specifically for Williams Way Blvd – FBC Mobility Project – 13114. Per request, we have provided photographs of the material in question. Risk of loss for this material shall pass to Tom-Mac, Inc, Fort Bend County, and Allgood upon delivery.

Please let us know if you have any further questions.

Thank you,

Bexar Concrete Works I, Ltd.

A handwritten signature in black ink, appearing to read 'Colleen D', with a long horizontal stroke extending to the right.

Colleen Dake
Manager

SS40 M3 C1

1-12-18

7.0

SS40 M2 C1

1-12-18

7.0

SS40 M1 C1

1-12-18

7.0

SS40 M8 C1

1-12-18

7.0

SS40 M7 C1

1-12-18

7.0

SS40 M6 C1

1-12-18

7.0

SS40 M5 C1

1-12-18

SS40 M15 C1

1-19-18

7.0

SS40 M14 C1

1-19-18

7.0

SS40 M13 C1

1-19-18

7.0

SS40 M12 C1

1-19-18

7.0

SS40 M19 C1

1-19-18

7.0

SS40 M18 C1


1-19-18

7.0

SS40 M17 C1

1-19-18

7.0

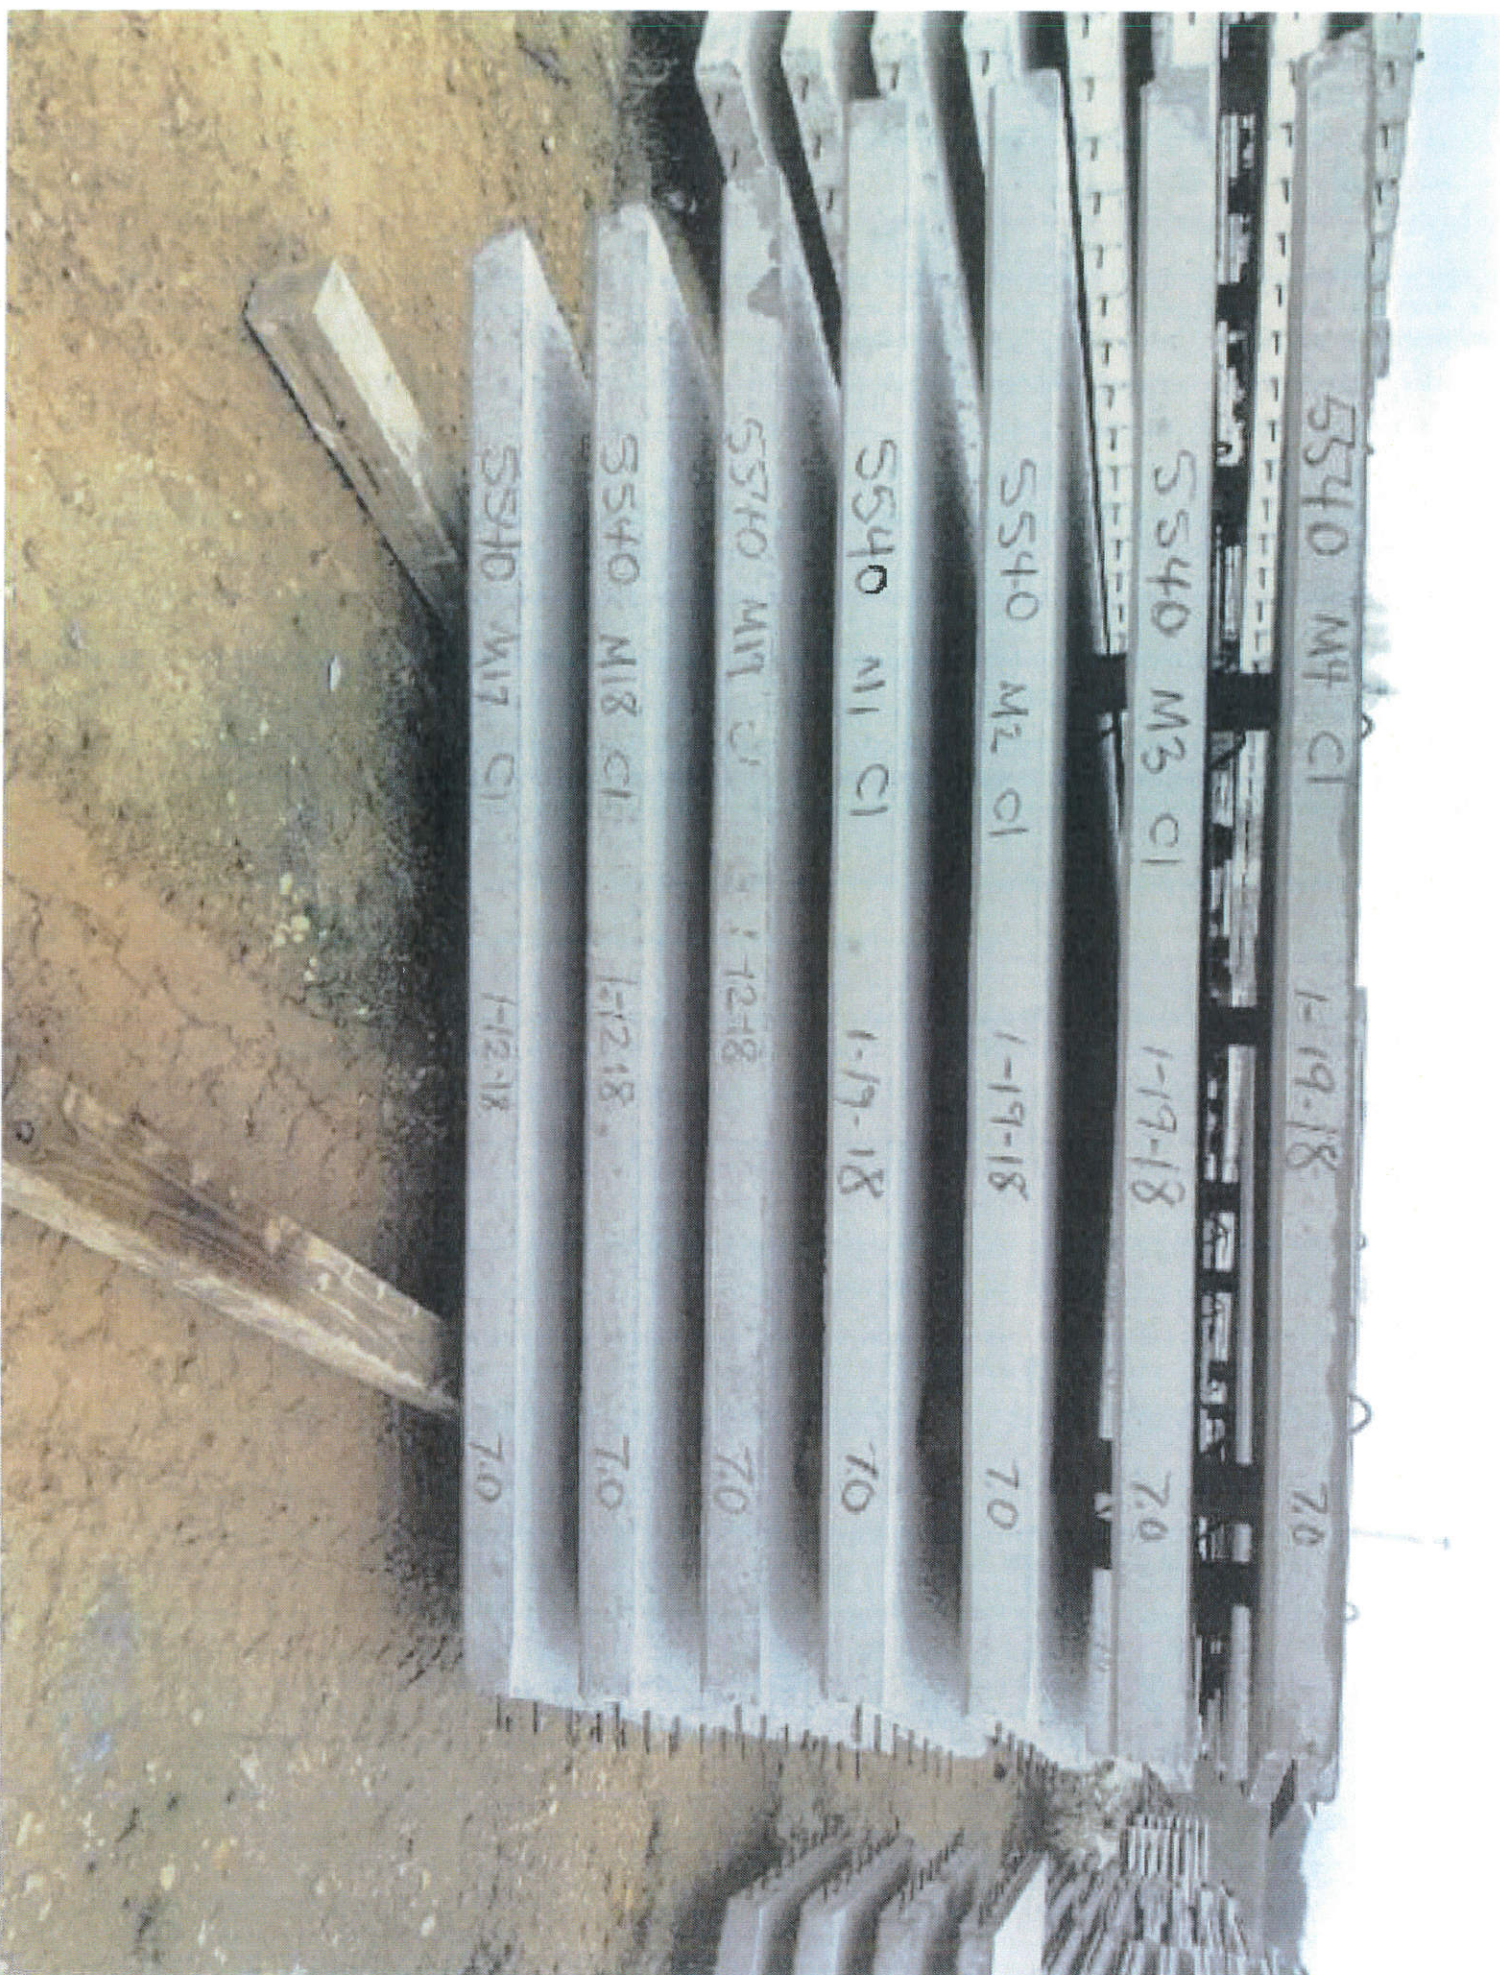

5540 M4 C1

1-19-18

7.0

5540 M3 C1

1-19-18

7.0

5540 M2 C1

1-19-18

7.0

5540 M1 C1

1-19-18

7.0

5540 M17 C1

1-12-18

7.0

5540 M18 C1

1-12-18

7.0

5540 M17 C1

1-12-18

7.0

SS40 6.4. 7.0 H- 28 2 13 18

SS40 6.4. 7.0 H- 27 2 13 18.

SS40 6.4. 7.0 H- 26 2 13 18.

SS40 6.4. 7.0 H- 25 2 13 18





5540 5,5 7,0 H-31 1 18 18

5540 5,5 7,0 H-31 1 18 18

5540 5,5 7,0 H-30 1 18 18

5540 5,5 7,0 H-39 1 18 18

5540 5,5 7,0 H-28 1 18 18

5540 5,5 7,0 H-27 1 18 18

5540 5,5 7,0 H-26 1 18 18





5540 8 70 R 24 / 22 18

5540 8 70 R 23 / 22 18

5540 8 70 R 22 / 22 18

5540 8 70 R 21 / 22 18

5540 8 70 R 68 / 22 18

5540 8 70 R 59 / 22 18

5540 8 70 R 58 / 22 18

5540 8 70 R 57 / 22 18





5540 8 70 K 52 122 18

5540 8 70 R 51 122 18

5540 8 70 K 50 122 18

5510 8 70 R 19 122 18
