

PO # 138400
DMS Rec 503648



Fort Bend County Engineering Department
301 Jackson Street
Richmond, TX 77469

Invoice Date: 7/31/2019
Invoice No.: 8591
Project No.: 12607.24

Attention: Mr. Richard W. Stolleis, P.E.

Project Name: Greenbusch Road Improvements (Project No. 13312)
PO No.: 138400

Services Performed: June 1, 2019 through July 31, 2019

TOTAL AMOUNT DUE THIS INVOICE: \$ 47,037.00

	Contract Amount	Percent Complete	Amount Complete	Previously Invoiced	Amount Remaining	Current Invoice
Preliminary Design	\$ 121,397.00	100.00%	\$ 121,397.00	\$ 121,397.00	\$ -	
Final Design	\$ 519,513.75	89.24%	\$ 463,630.75	\$ 417,383.75	\$ 55,883.00	\$ 46,247.00
Scope Change	\$ 14,740.00	100.00%	\$ 14,740.00	\$ 14,740.00	\$ -	
Bid & Construction	\$ 37,000.00	12.00%	\$ 4,440.00	\$ 3,650.00	\$ 32,560.00	\$ 790.00
Survey	\$ 119,775.00	100.00%	\$ 119,775.00	\$ 119,775.00	\$ -	
ROW Maps	\$ 64,905.00	78.43%	\$ 50,905.00	\$ 50,905.00	\$ 14,000.00	
Geotech	\$ 19,800.00	100.00%	\$ 19,800.00	\$ 19,800.00	\$ -	
Total	\$ 897,130.75	88.58%	\$ 794,687.75	\$ 747,650.75	\$ 102,443.00	\$ 47,037.00

OK, AIA
8/20/19

Progress Report:

AFLP submitted the 70% draft BID documents to Fort Bend County for review. Attended the field construction completion meeting, and continued with the design of Greenbusch Rd. Phase II, preparing the plan set and documents for the 95% draft submittal. This submittal will address the comments from FBC 70%, AFLP is working on the revision of the detailed design including the profile, design of intersections, location of ADA ramps, location of the sewer in plan and profile, final bridge design with details and standards, and recalculating quantities and cost estimate.



FORT BEND MOBILITY PROGRAM

PROJECT STATUS REPORT

PROJECT: Greenbusch Road Paving and Drainage Improvements

From Gaston Rd to Westheimer Pkwy

CONSULTANT: AGUIRRE & FIEDLS LP

PROJECT PHASE: Final Design

CONTRACT OR PROJECT NO. P.O. Number 138400

DATE: July 31, 2019

AFLP submitted the 70% draft BID documents to Fort Bend County for review. Attended the field construction completion meeting, and continued with the design of Greenbusch Rd. Phase II, preparing the plan set and documents for the 95% draft submittal. This submittal will address the comments from FBC 70%, AFLP is working on the revision of the detailed design including the profile, design of intersections, location of ADA ramps, location of the sewer in plan and profile, final bridge design with details and standards, and recalculating quantities and cost estimate.

ACTIVITIES ACHIEVED:

06/04/19	Phase-I, Field visit to verify survey control points
06/08/19	Phase-II, TCP and SW3P criteria and planning design meeting
06/14/19	Greenbusch 70% draft submittal
06/16/19	Review proposed profile with H&H sub-consultant
07/12/19	Construction Manual 70% submittal.
07/15/19	Revise as-built for location and profile of private utilities
07/19/19	Revise plan set, Construction Manual and estimate
07/30/19	Detailed design of driveways and intersection.

07/31/2019



Page 1



PLANNED ACTIVITIES FOR NEXT PERIOD:

- Submit 95% draft bid documents for FBC review.
- Update design of Westheimer intersection layout, details and quantities.
- Review Design Manual to address FBC comments
- Review all BID documents

OUTSTANDING ITEMS, NEEDS OR CONCERNS:

Revisit the field to observe changes in the area and validate the survey from 2016

Utility conflicts resolution

Driveway design for the property located at Northwest side of the bridge.

Update drainage design.

Revise TCP design and implementation


SCHEDULE UPDATE:

See attachment

Project Name: Greenbusch Road Paving & Drainage Improvements
 Project Limits: Gaston to Westheimer Parkway
 Wed 4/10/19



PROJECT SCHEDULE

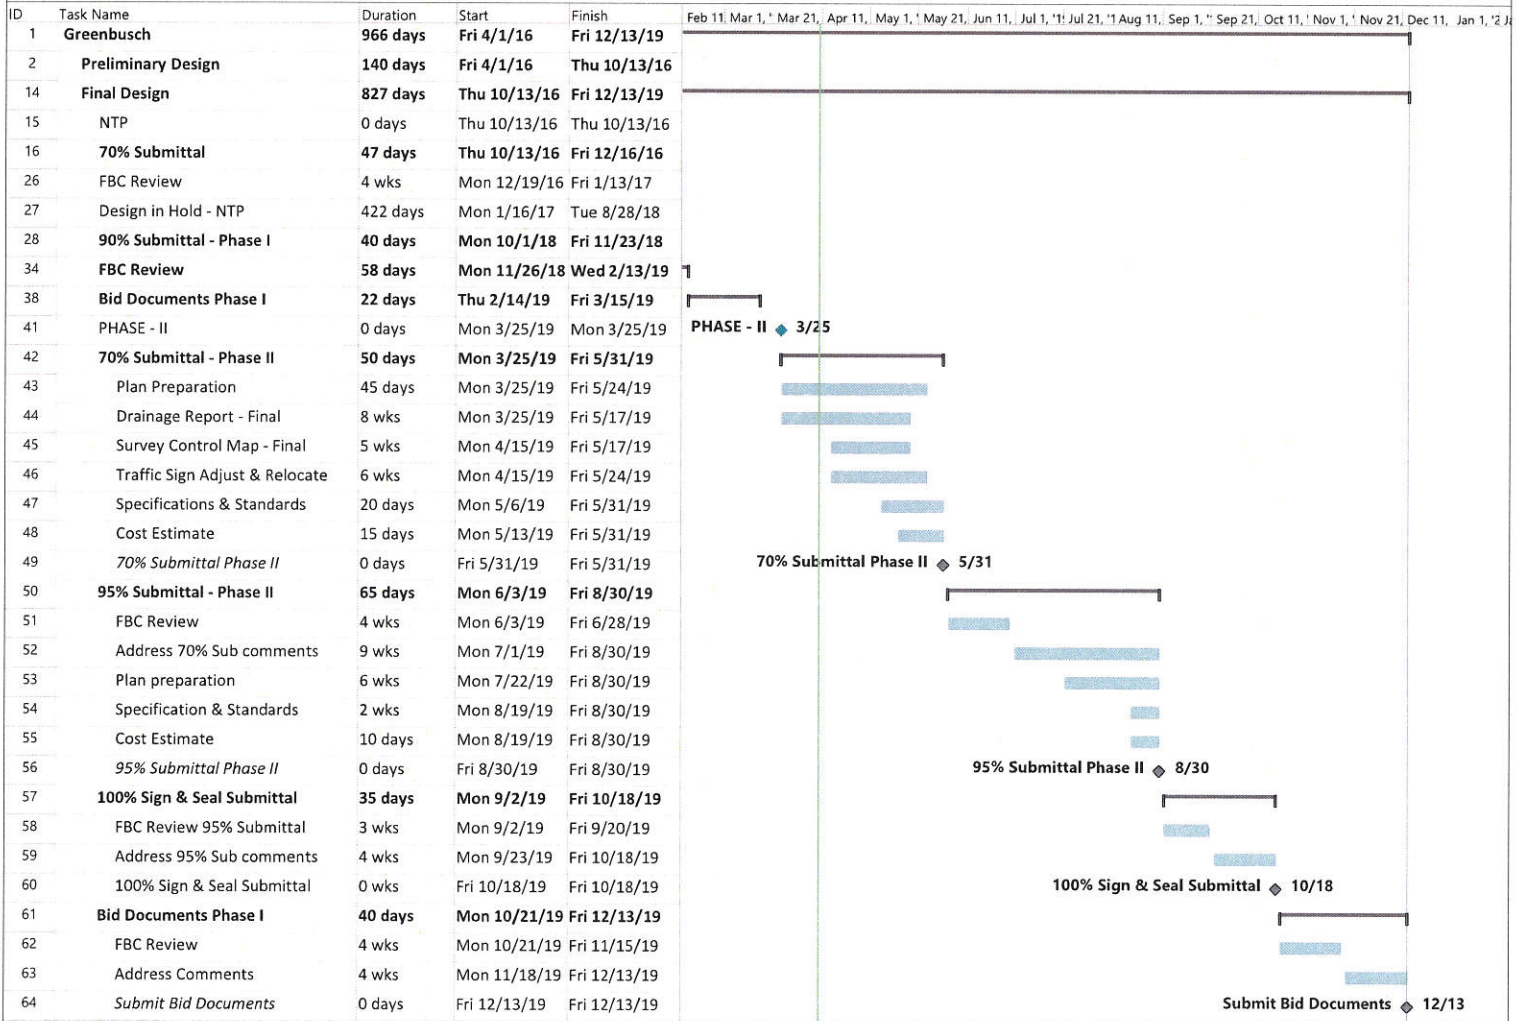

Svatek, Donna

From: Elise Dillow <edillow@spi-eng.com>
Sent: Tuesday, August 20, 2019 10:01 AM
To: ENGINvoices
Cc: Mark Dessens
Subject: Greenbusch Rd Invoice
Attachments: Invoice 8591 12607.24 2019-07-31 FBC.pdf

CAUTION: This email originated from outside of the organization. Do not click links or open attachments unless you recognize the sender and know the content is safe.

Good Morning,

Attached is Aguirre & Fields' invoice for Greenbusch Rd. I have reviewed the invoice and approve it for processing. Please let me know if you have any questions.

Thank you,

Elise Dillow | E.I.T.
p 281.920.0487 | f 281.920.9924



www.SPI-ENG.com
