

# Pay Estimate

PO 136676  
Rec 375381  
9/21/14  
APP

**Covering Period** 07/24/2016 Thru 08/27/2016

**Estimate No.** 06  
**Project No:** 1258-03-042, ETC.  
**Contract No:** 1258-03-042, ETC.  
**Job No:** 16-035

**Project Name:** FM 1093  
**Contractor:** Webber, LLC

**Contract Award Date:** 02/02/2016  
**Start Date:** 02/29/2016  
  
**Substantial Completion Date:**  
**Percentage By Time:** 25.14% **By Place** 29.12%

**CONTRACT TIME IN CALENDAR DAYS**

Original Contract Time : 720  
Approved Extensions : 0  
Total Contract Time : 720  
Days Charged to Date : 181  
Days Remaining to Date : 539

**CONTRACT AMOUNT TO DATE :**

- 1. Original Contract Amount \$63,811,753.94
- 2. Approved Change Orders

No	Date	Approved Extension	Amount
1.00	05/05/2016	0	\$21,200.00
2.00	05/05/2016	0	\$260,000.00
3.00	05/26/2016	0	\$12,585.59

Total Change Orders to Date \$293,785.59  
**TOTAL CONTRACT AMOUNT** \$64,105,539.53

**A. EARNINGS TO DATE**

- 1. Work Completed to Date 29.12% Complete \$18,670,510.85
  - 2. Material Stored on Site \$2,477,771.66
  - 3. Material Stored in Place \$1,786,152.12
  - 4. Balance-Material Accepted Not in Place \$691,619.54 @ 100% \$691,619.54
  - 5. Advance Allowance \$0.00
- TOTAL EARNINGS TO DATE** \$19,362,130.39

**B. DEDUCTIONS**

- 1. Retainage 0.00 % Of \$19,362,130.39 \$0.00
  - 2. Retainage Release 0.00 % Of \$19,362,130.39 \$0.00
  - 3. Total Retainage \$0.00
  - 4. Liquidated Damages 0.00 Days @ \$15,000.00 \$0.00
  - 5. Quality Control Retest Cost \$0.00
  - 6. Penalties and Items in Contract \$0.00
- TOTAL DEDUCTIONS** \$0.00

**C. AMOUNT DUE THIS PERIOD**

- 1. Total Earnings To Date \$19,362,130.39
- 2. Total Deductions \$0.00
- 3. Total Payments Due \$19,362,130.39
- 4. Less Previous Payments \$17,540,232.14
- 5. Restoration Adjustment \$0.00

**TOTAL AMOUNT DUE CONTRACTOR THIS DATE** \$1,821,898.25

# Pay Estimate

Covering Period 07/24/2016 Thru 08/27/2016

Estimate No. 06

Project Name: FM 1093  
Contractor: Webber, LLC

Project No: 1258-03-042, ETC.  
Contract No: 1258-03-042, ETC.  
Job No: 16-035

The Payment Invoice is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or Contractor under this Contract.

Approved By:  Date: 8/30/2016 2:43:44PM

Lead Inspector Robert Dick

Approved By:  Date: 9/1/2016 1:57:46PM


Contractor Emilio Chapa

Approved By:  Date: 9/2/2016 9:06:29AM

Resident Engineer Howard Caldwell, P.E.

Approved By:  Date: 9/13/2016 8:47:56AM

Construction Manager Mike Stone

Approved By:  Date: 9/13/2016 3:18:55PM

County Engineer Richard Stolleis, P.E.

# Pay Estimate

Covering Period 07/24/2016 Thru 08/27/2016

Estimate No. 06

Project Name: FM 1093  
 Contrator: Webber, LLC

Project No: 1258-03-042, ETC.  
 Contract No: 1258-03-042, ETC.  
 Job No: 16-035

LINE NO.	ITEM DESCRIPTION	UNIT	CONTRACT OR PROJECT ESTIMATE QUANTITY	TOTAL WORK DONE THIS ESTIMATE QUANTITY	TOTAL WORK DONE PREVIOUS ESTIMATE	TOTAL WORK DONE TO DATE QUANTITY	PERCENT COMPLETE	CONTRACT PRICE	AMOUNT
100 6002	PREPARING ROW	STA	222.00	4.80	157.85	162.65	73.27%	\$19,400.00	\$3,155,410.00
104 6001	REMOVING CONC (PAV)	SY	15,595.00	929.89	2,858.86	3,788.75	24.29%	\$3.85	\$14,586.69
104 6017	REMOVING CONC (DRIVEWAYS)	SY	4,006.00	1,022.56	0.00	1,022.56	25.53%	\$3.00	\$3,067.68
104 6022	REMOVING CONC (CURB AND GUTTER)	LF	3,681.00	663.00	0.00	663.00	18.01%	\$5.00	\$3,315.00
110 6001	EXCAVATION (ROADWAY)	CY	208,890.00	34,712.00	123,266.48	157,978.48	75.63%	\$4.65	\$734,599.93
132 6006	EMBANKMENT (FINAL)(DENS CONT)(TY C)	CY	313,830.00	54,632.61	93,508.45	148,141.06	47.20%	\$3.89	\$576,268.72
260 6006	LIME TRT (EXST MATL) (6")	SY	332,274.00	27,906.03	67,959.46	95,865.49	28.85%	\$1.20	\$115,038.59
275 6001	CEMENT	TON	2,000.00	396.47	734.73	1,131.20	56.56%	\$130.00	\$147,056.00
276 6224	CEM TRT(PLNT MX) (CL N)(TY E) (GR 4)(6")	SY	320,853.00	27,015.90	53,855.89	80,871.79	25.21%	\$7.45	\$602,494.84
292 6017	ASPHALT STAB BASE (GR 4) (PG 64)	TON	17,032.00	1,343.18	2,283.35	3,626.53	21.29%	\$69.24	\$251,100.94
360 6044	CONC PVMT (CONT REINF)(FAST TRK)(12")	SY	18,593.00	2,714.90	5,666.30	8,381.20	45.08%	\$57.80	\$484,433.36
400 6005	CEM STABIL BKFL	CY	28,636.00	2,118.03	19,554.24	21,672.27	75.68%	\$35.49	\$769,148.86
400 6006	CUT & RESTORING PAV	SY	874.00	97.91	840.63	938.54	107.38%	\$75.61	\$70,963.01
400 6009	CEMENT STAB BACKFILL (INLET OR MH)	CY	1,437.00	117.08	434.46	551.54	38.38%	\$35.49	\$19,574.15
402 6001	TRENCH EXCAVATION PROTECTION	LF	32,558.00	2,621.50	19,347.58	21,969.08	67.48%	\$1.08	\$23,726.61
462 6001	CONC BOX CULV (3 FT X 2 FT)	LF	1,042.00	745.00	290.50	1,035.50	99.38%	\$100.54	\$104,109.17
462 6003	CONC BOX CULV (4 FT X 2 FT)	LF	2,547.00	44.00	172.00	216.00	8.48%	\$114.14	\$24,654.24
462 6004	CONC BOX CULV (4 FT X 3 FT)	LF	1,908.00	5.00	838.00	843.00	44.18%	\$132.91	\$112,043.13

# Pay Estimate

Covering Period 07/24/2016 Thru 08/27/2016

Estimate No. 06

Project Name: FM 1093  
 Contractor: Webber, LLC

Project No: 1258-03-042, ETC.  
 Contract No: 1258-03-042, ETC.  
 Job No: 16-035

LINE NO.	ITEM DESCRIPTION	UNIT	CONTRACT OR PROJECT ESTIMATE QUANTITY	TOTAL WORK DONE THIS ESTIMATE QUANTITY	TOTAL WORK DONE PREVIOUS ESTIMATE	TOTAL WORK DONE TO DATE QUANTITY	PERCENT COMPLETE	CONTRACT PRICE	AMOUNT
462 6006	CONC BOX CULV (5 FT X 2 FT)	LF	1,026.00	419.00	216.00	635.00	61.89%	\$170.72	\$108,407.20
462 6010	CONC BOX CULV (6 FT X 3 FT)	LF	1,751.00	32.00	1,689.00	1,721.00	98.29%	\$188.63	\$324,632.23
462 6019	CONC BOX CULV (8 FT X 4 FT)	LF	2,247.00	46.00	2,133.00	2,179.00	96.97%	\$268.78	\$585,671.62
462 6020	CONC BOX CULV (8 FT X 5 FT)	LF	327.00	84.00	256.00	340.00	103.98%	\$295.19	\$100,364.60
462 6021	CONC BOX CULV (8 FT X 6 FT)	LF	989.00	-5.00	994.00	989.00	100.00%	\$303.72	\$300,379.08
462 6029	CONC BOX CULV (10 FT X 5 FT)	LF	2,280.00	331.00	1,922.00	2,253.00	98.82%	\$400.10	\$901,425.30
464 6003	RC PIPE (CL III)(18 IN)	LF	1,490.00	16.00	1,487.00	1,503.00	100.87%	\$47.73	\$71,738.19
464 6005	RC PIPE (CL III)(24 IN)	LF	16,147.00	451.00	6,438.00	6,889.00	42.66%	\$40.88	\$281,622.32
464 6007	RC PIPE (CL III)(30 IN)	LF	1,404.00	76.00	1,300.58	1,376.58	98.05%	\$69.22	\$95,286.87
464 6008	RC PIPE (CL III)(36 IN)	LF	2,041.00	611.50	336.00	947.50	46.42%	\$83.36	\$78,983.60
464 6012	RC PIPE (CL III)(60 IN)	LF	96.00	90.00	0.00	90.00	93.75%	\$222.79	\$20,051.10
465 6167	INLET (COMPL)(TY AD)	EA	46.00	6.00	25.50	31.50	68.48%	\$2,594.53	\$81,727.70
465 6173	MANH (COMPL)(TY A)	EA	20.00	2.00	7.00	9.00	45.00%	\$3,776.05	\$33,984.45
465 6175	INLET (COMPL)(CURB)(TY C)	EA	67.00	9.50	17.50	27.00	40.30%	\$2,887.64	\$77,966.28
465 6176	INLET (COMPL)(CURB)(TY C1)	EA	27.00	0.50	11.00	11.50	42.59%	\$3,086.97	\$35,500.16
465 6225	JCT BOX (COMPL)(SPL)	EA	24.00	6.00	7.42	13.42	55.91%	\$31,592.48	\$423,934.12
466 6208	WINGWALL (SW - 0) (HW=5 FT)	EA	1.00	1.00	0.00	1.00	100.00%	\$13,646.44	\$13,646.44
476 6044	JACK BOR OR TUN PIPE(60 IN) (RC)(CL III)	LF	110.00	78.00	32.00	110.00	100.00%	\$923.60	\$101,596.00
496 6004	REMOV STR (SET)	EA	93.00	2.00	11.00	13.00	13.98%	\$509.34	\$6,621.42
496 6007	REMOV STR (PIPE)	LF	6,211.00	92.00	439.00	531.00	8.55%	\$23.40	\$12,425.40

# Pay Estimate

Covering Period 07/24/2016 Thru 08/27/2016

Estimate No. 06

Project Name: FM 1093  
 Contractor: Webber, LLC

Project No: 1258-03-042, ETC.  
 Contract No: 1258-03-042, ETC.  
 Job No: 16-035

LINE NO.	ITEM DESCRIPTION	UNIT	CONTRACT OR PROJECT ESTIMATE QUANTITY	TOTAL WORK DONE THIS ESTIMATE QUANTITY	TOTAL WORK DONE PREVIOUS ESTIMATE	TOTAL WORK DONE TO DATE QUANTITY	PERCENT COMPLETE	CONTRACT PRICE	AMOUNT
502 6001	BARRICADES, SIGNS AND TRAFFIC HANDLING	MO	24.00	1.00	5.00	6.00	25.00%	\$31,553.33	\$189,319.98
506 6038	TEMP SEDMT CONT FENCE (INSTALL)	LF	5,000.00	248.00	2,111.66	2,359.66	47.19%	\$2.92	\$6,890.21
508 6001	CONSTRUCTING DETOURS	SY	27,249.00	378.57	366.71	745.28	2.74%	\$55.30	\$41,213.98
512 6021	PORT CTB (DES SOURCE)(LOW PROF)(TY 1)	LF	7,240.00	600.00	0.00	600.00	8.29%	\$6.27	\$3,762.00
512 6022	PORT CTB (DES SOURCE)(LOW PROF)(TY 2)	LF	120.00	20.00	0.00	20.00	16.67%	\$6.52	\$130.40
512 6025	PORT CTB (MOVE)(SGL SLP)(TY 1)	LF	11,900.00	240.00	0.00	240.00	2.02%	\$3.98	\$955.20
512 6049	PORT CTB (REMOVE)(SGL SLP)(TY 1)	LF	8,780.00	60.00	0.00	60.00	0.68%	\$7.89	\$473.40
529 6005	CONC CURB (MONO) (TY II)	LF	84,999.00	116.00	0.00	116.00	0.14%	\$1.79	\$207.64
545 6003	CRASH CUSH ATTEN (MOVE & RESET)	EA	10.00	1.00	0.00	1.00	10.00%	\$4,250.00	\$4,250.00
545 6005	CRASH CUSH ATTEN (REMOVE)	EA	20.00	1.00	0.00	1.00	5.00%	\$950.00	\$950.00
662 6063	WK ZN PAV MRK REMOV (W)4"(SLD)	LF	42,991.00	714.00	2,349.00	3,063.00	7.12%	\$0.60	\$1,837.80
662 6095	WK ZN PAV MRK REMOV (Y)4"(SLD)	LF	71,078.00	1,261.00	7,701.00	8,962.00	12.61%	\$0.60	\$5,377.20
9008 2000	POLICE OFFICER (FORCE ACCOUNT)	DOL	50,000.00	2,115.00	24,345.00	26,460.00	52.92%	\$1.00	\$26,460.00
	Material on Hand 100%			691,619.54				\$1.00	\$691,619.54

Dear Prospective Juror: YOU ARE HEREBY SUMMONED TO APPEAR FOR JURY SERVICE ON THE DATE AND TIME LISTED:

September 13, 2016  
12:30 PM

REPORT TO: FORT BEND COUNTY JUSTICE CENTER  
1422 EUGENE HEIMANN CIRCLE  
ROOM 10196  
RICHMOND, TEXAS 77469

Juror #: 6465-ZY002

**JURY INSTRUCTIONS:**

JUROR QUESTIONNAIRE MUST BE FILLED OUT COMPLETELY AND RETURNED TO OUR OFFICE. PLEASE REFER TO THE BACK OF THIS FORM FOR INSTRUCTIONS

THE FOLLOWING "JUROR QUESTIONNAIRE" IS MANDATED BY GOVERNMENT CODE, SECTIONS 62.0132. Your answers are CONFIDENTIAL and may be disclosed only to the judge, court personnel, the litigant, and the litigant's attorney. JUROR QUESTIONNAIRE (PLEASE TYPE OR PRINT WITH INK ONLY) Please print legibly.

Male  Female Race (required by State Law): Hispanic Age: 58 Date of Birth: 12/17/57  
 Your Name: BENITO RAMOS JR. Home Phone: (281) 961-7390 Cell Phone: (281) 961-7390  
 Home Address: 300 WHEATON ST City: Richmond TX Zip: 77469 County of Residence: FORT BEND  
 Mailing Address (if different from home): \_\_\_\_\_ City \_\_\_\_\_ Zip \_\_\_\_\_ Your Occupation: \_\_\_\_\_  
 Work Phone: 281 633-7500 Your Employer: FORT BEND COUNTY How Long? 8 YR  
 Spouse's Name: \_\_\_\_\_ Spouse's Occupation: \_\_\_\_\_  
 Spouse's Employer: \_\_\_\_\_ How Long? \_\_\_\_\_  
 Please check the highest level of education completed:  Did not receive H.S. Diploma  H.S. Diploma  
 GED  2yr College  4yr College/University  Post-Graduate  Other \_\_\_\_\_

Number of Children: _____ Ranges of Age: from _____ years to _____ years	Yes	No
Are you a U.S. Citizen?	<input checked="" type="checkbox"/>	<input type="checkbox"/>
Have you ever been an accused, complainant, or witness in a criminal case?	<input type="checkbox"/>	<input checked="" type="checkbox"/>
Have you or any family members ever sustained bodily injury that required medical attention?	<input type="checkbox"/>	<input checked="" type="checkbox"/>
Current Marital Status: <input type="checkbox"/> Single <input type="checkbox"/> Married <input type="checkbox"/> Widowed <input checked="" type="checkbox"/> Divorced		
I CERTIFY THAT ALL ANSWERS ARE TRUE AND CORRECT. BENITO RAMOS JR	Have you ever served on a civil jury?	<input type="checkbox"/> <input checked="" type="checkbox"/>
JUROR SIGNATURE: <u>[Signature]</u>	Have you ever served on a criminal jury?	<input type="checkbox"/> <input checked="" type="checkbox"/>
	Have you ever been a party to a lawsuit?	<input type="checkbox"/> <input checked="" type="checkbox"/>

**JUROR BADGE**

Juror#   
6465-ZY002

Bring the lower portion when you report for service. You are to appear promptly as instructed by this summons. Jurors not present by the designated time must reschedule. If you have a special need or disability you are encouraged to notify this office immediately concerning requests for reasonable accommodations

**Mailing Address ONLY:**

Annie Rebecca Elliott  
District Clerk  
301 Jackson  
Richmond, Texas 77469



STATE OF TEXAS  
COUNTY OF FORT BEND  
JURY SUMMONS

PRESORT  
FIRST CLASS



POSTAGE PITNEY BOWES  
ZIP 77469 \$ 000.45  
02 1W  
0001372240 AUG 07 2016

JURY SERVICE IS A MOST VITAL FUNCTION OF CITIZENSHIP

OFFICIAL BUSINESS  
PENALTY FOR PRIVATE USE


Report Date: September 13, 2016

Time: 12:30 PM

BENITO RAMOS JR / 498.00  
300 WHEATON ST  
RICHMOND, TX 77469



Report To The Physical Location At:  
Fort Bend County Justice Center  
1422 Eugene Heimann Circle, Rm. 10196  
Richmond, Texas 77469

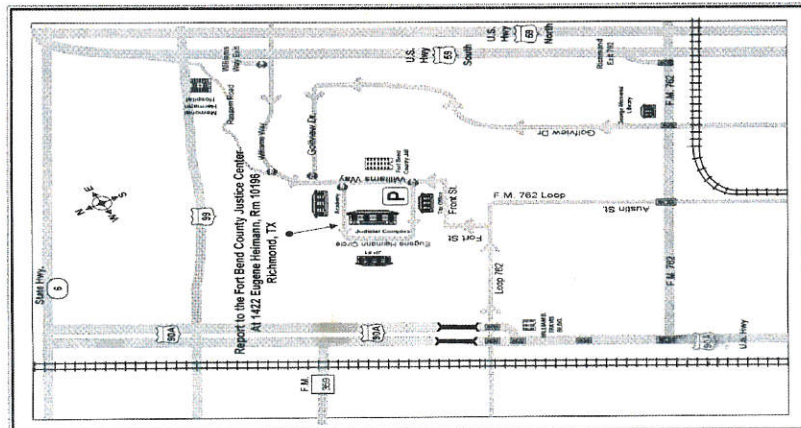

There is parking for persons with disabilities by the entrance to the Fort Bend County Justice Center. Accommodations for the hearing and speech-impaired are available upon request. For information, please call (281) 344-3900
