



AGUIRRE & FIELDS
ENGINEERING INNOVATORS

PO# 138400
ams
Rec 489061

Fort Bend County Engineering Department
301 Jackson Street
Richmond, TX 77469

Invoice Date: 3/31/2019
Invoice No.: 8227
Project No.: 12607.23

Attention: Mr. Richard W. Stolleis, P.E.

Project Name: Greenbusch Road Improvements (Project No. 13312)
PO No.: 138400

Services Performed: March 1, 2019 through March 31, 2019

TOTAL AMOUNT DUE THIS INVOICE:

\$ 24,580.00

	Contract Amount	Percent Complete	Amount Complete	Previously Invoiced	Amount Remaining	Current Invoice
Preliminary Design	\$ 121,397.00	100.00%	\$ 121,397.00	\$ 121,397.00	\$ -	
Final Design	\$ 519,513.75	73.00%	\$ 378,883.75	\$ 354,303.75	\$ 140,630.00	\$ 24,580.00
Scope Change	\$ 14,740.00	100.00%	\$ 14,740.00	\$ 14,740.00	\$ -	
Bid & Construction	\$ 37,000.00	0.00%	\$ -	\$ -	\$ 37,000.00	
Survey	\$ 119,775.00	100.00%	\$ 119,775.00	\$ 119,775.00	\$ -	
ROW Maps	\$ 64,905.00	78.00%	\$ 50,905.00	\$ 50,905.00	\$ 14,000.00	
Geotech	\$ 19,800.00	100.00%	\$ 19,800.00	\$ 19,800.00	\$ -	
Total	\$ 897,130.75	79.00%	\$ 705,500.75	\$ 680,920.75	\$ 191,630.00	\$ 24,580.00

OK, JSA
04/23/19

Progress Report:

AFLP submitted final sign and seal version of construction documents for phase-I. For phase-II, AFLP finished the proposed profile and initiated the road, bridge, and drainage re-design for 28.0 feet back to back curb and gutter configuration.



**FORT BEND MOBILITY PROGRAM
PROJECT STATUS REPORT**

PROJECT: Greenbusch Road Paving and Drainage Improvements
From Gaston Rd to Westheimer Pkwy

CONSULTANT: AGUIRRE & FIEDLS LP

PROJECT PHASE: Final Design

CONTRACT OR PROJECT NO. P.O. Number 138400

DATE: March 31, 2019

AFLP submitted final sign and seal version of construction documents for phase-I. For phase-II, AFLP finished the proposed profile and initiate the road, bridge, and drainage re-design for 28.0 feet back to back curb and gutter configuration.

ACTIVITIES ACHIEVED:

03/04/19 Review comments to 100% plan set
03/11/19 Internal QA/QC for final construction plan set, phase-I
03/18/19 Submitted Phase-I Construction documents
03/22/19 Review profile and road base design

PLANNED ACTIVITIES FOR NEXT PERIOD:

Redesign Greenbusch and Westheimer intersection.
Verify max./min. cross slopes at driveways and street intersections.
Review cut and fill volumes under the flood plain section

03/31/2019





OUTSTANDING ITEMS, NEEDS OR CONCERNS:

Revisit the field to observe changes in the area and validate the survey from 2016

Set vertical alignment and road base line


Bridge design

Drainage design

SCHEDULE UPDATE:

See attachment

PROJECT SCHEDULE

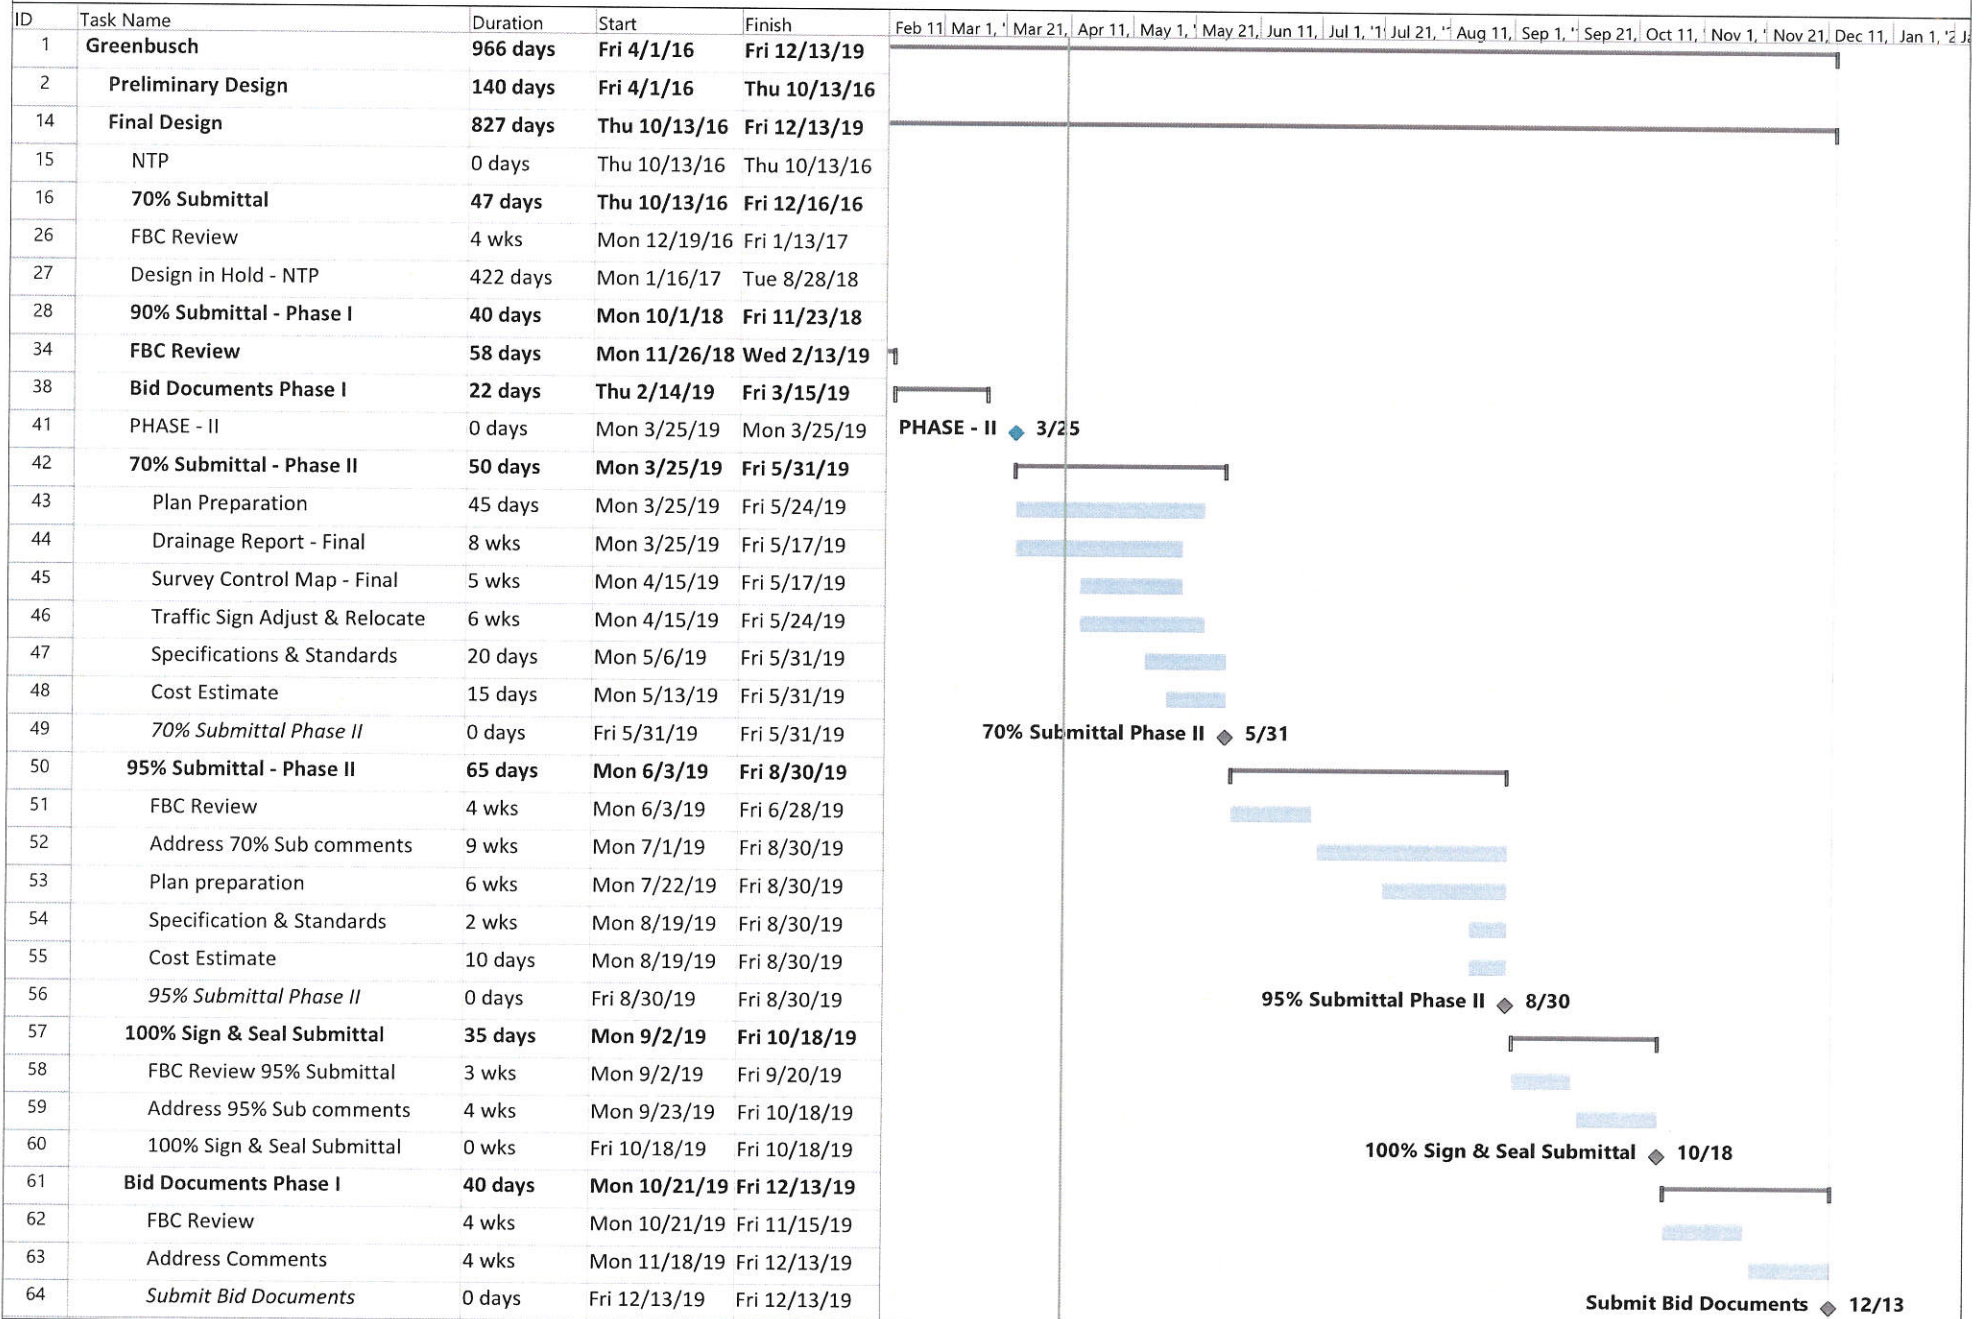

Svatek, Donna

From: Elise Dillow <edillow@spi-eng.com>
Sent: Tuesday, April 23, 2019 11:01 AM
To: ENGINvoices
Cc: Mark Dessens
Subject: Greenbusch Rd Invoice
Attachments: Invoice 8227 12607.23 2019-03-31 FBC.pdf

CAUTION: This email originated from outside of the organization. Do not click links or open attachments unless you recognize the sender and know the content is safe.

Good Morning,

Attached is Aguirre & Fields's invoice for Greenbusch Rd. I have reviewed the invoice and approve it for processing. Please let me know if you have any questions.

Thank you,

Elise Dillow | E.I.T.
p 281.920.0487 | f 281.920.9924



www.SPI-ENG.com
