

# LONNIE LISCHKA COMPANY, L.P.

P.O. BOX 806

BELLVILLE, TEXAS 77418

PHONE: (979) 865-5941 / FAX: (979) 865-3843

July 25, 2011

Mr. Andy Meyers  
Fort Bend County Commissioners Court  
22333 Grand Corner Drive, Suite 105  
Katy, Texas 77494

JUL 25 2011

Re: Cinco Northwest Detention/Amenity Phase 1  
Fort Bend County MUD #58  
Fort Bend County, Texas

Mr. Meyers:

We are requesting approval of the included traffic control plan. Also, enclosed, please find the job information, vicinity map, and proposed detour map of the project.

As you will see from the attached documents, we are contracted to cross Katy-Flewellen with box culverts to provide storm drainage for existing and future development. The proposed date to install these box culverts is August 13, 2011. Our plan will include road removal, box installation and road replacement on this day. We are, however, requesting that due to the possibility of inclement weather that we be permitted to close the road from August 12 - August 15. This additional time will also allow us to install and remove all necessary road and warning signs.

We intend to provide proper notification to all entities including but not limited to the affected school district and the County. A message board is proposed to inform area residents of the closure one (1) week in advance.

We have applied to the County for a right-of-way permit which has been reviewed by Johnny Ortega and subsequently submitted to the Commissioners court. We look forward to coordinating this drainage improvement with the County and appreciate your consideration of these documents.

Sincerely,

LONNIE LISCHKA COMPANY, LP

By:



Mike Day

cc: Nathan Hatcher

**CONTRACTOR INFORMATION SHEET**

General Contractor: Lonnie Lischka Company, LP  
P. O. Box 806  
Bellville, Texas 77418

Date: May 11, 2011

Telephone: (979) 865-5941

Fax: (979) 865-3843

Accounts Payable Contact: Kathie Bunch

**JOB INFORMATION**

Project Name: Cinco Ranch Northwest Detention/Amenity Phase I

Specific Address/Legal Description: South of Crossover Rd., North of Corbitt Street,  
East of FM 1463, West of Katy Flewellen Rd

Project Manager: Justin Lischka

Telephone: (979) 865-5941

Is this job taxable?: No, tax exempt certificate attached

Property Owner: Fort Bend County Municipal Utility District No. 58  
c/o Brown & Gay Engineers, Inc.  
10777 Westheimer, Suite 400  
Houston, Texas 77042



**BONDING INFORMATION**

Surety: AON Risk Services Southwest  
5555 San Felipe, Suite 1500  
Houston, Texas 77056  
Telephone: (832) 476-6767

Bond No. undetermined at this time


Contact: David Wightman

POSTED SPEED (MPH)	"X" SIGN SPACINGS (FEET)
30 OR LESS	120
35	160
40	240
45	320
50	400
55	500
60	600

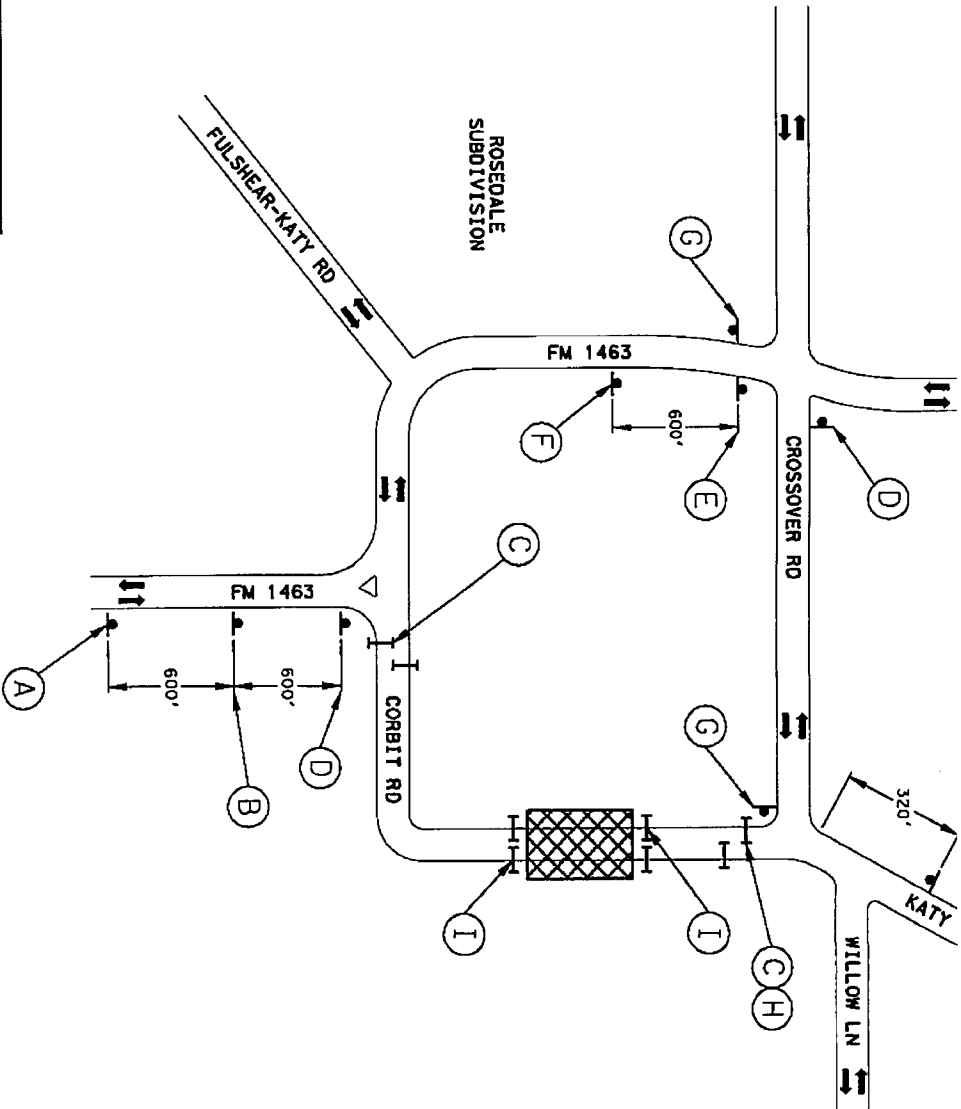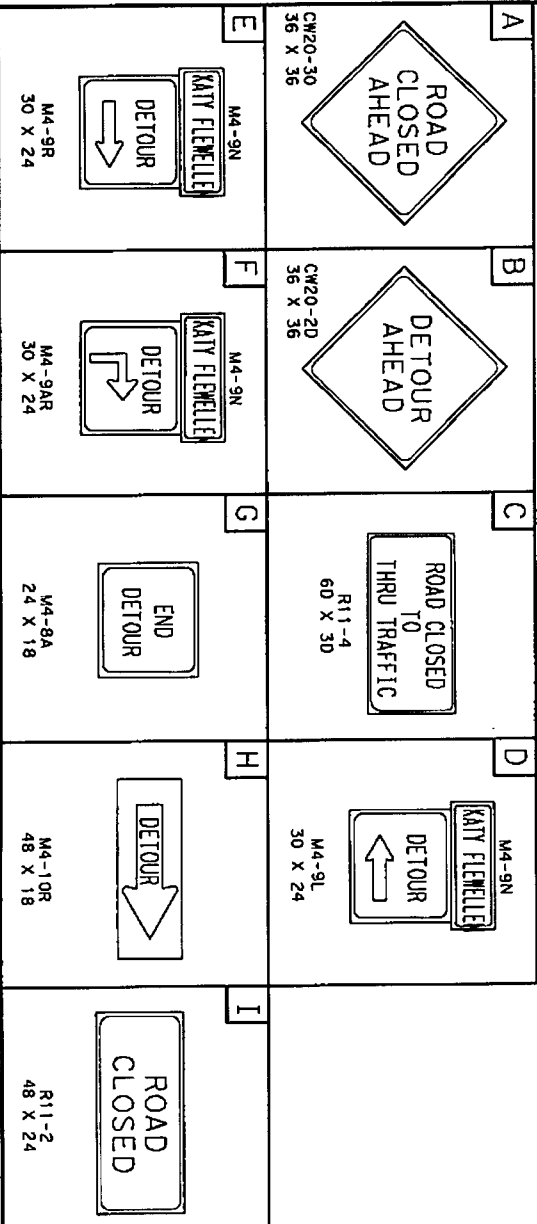

**GENERAL**

1. CONTRACTOR SHALL PROVIDE AND INSTALL T WITH THE TEXAS MANUAL ON UNIFORM TRAFFIC RECENT EDITION WITH REVISIONS) DURING
2. CONTRACTOR TO MAINTAIN ACCESS TO ADJAC
3. APPROVED COPIES OF TRAFFIC CONTROL PLA BE AVAILABLE FOR INSPECTION AT JOB SIT

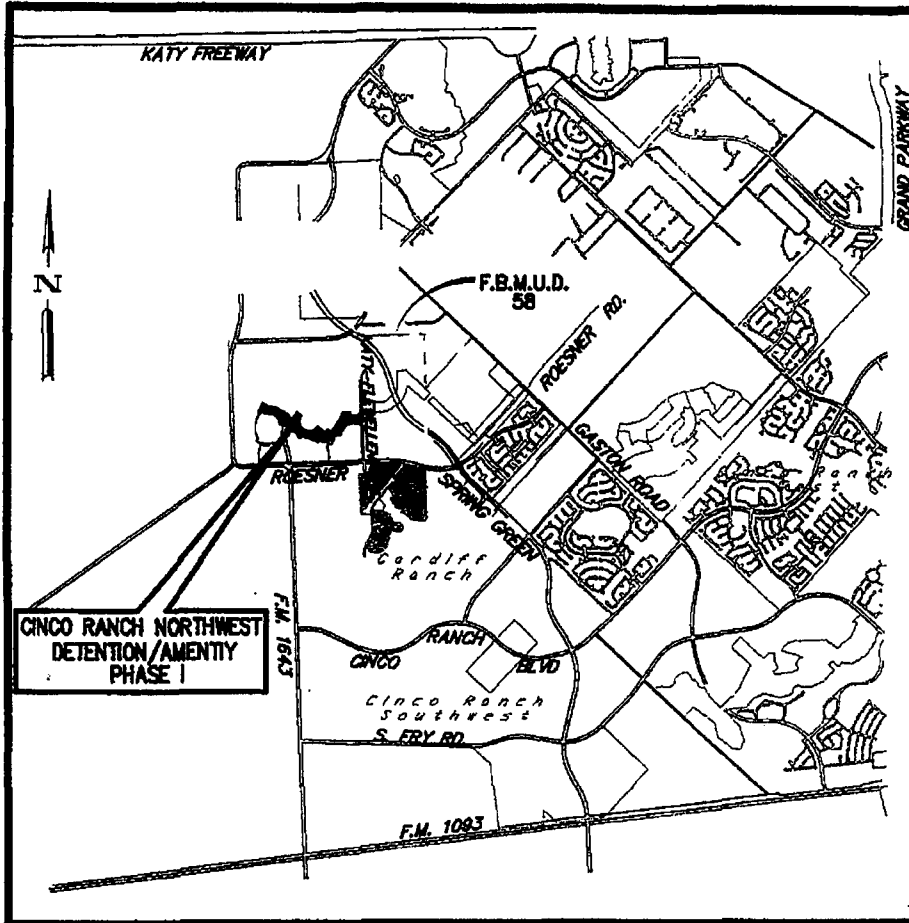

**VICINITY MAP**

N.T.S.

FBC KEY MAP 484 - S

GIMS TILE 4256 D, 4255 B, 4355 A

ZIP CODE: 77494
