

70 116140

CHANGE ORDER

FORT BEND COUNTY ENGINEERING

- Distribution:
- FBC Engineering
 - FBC Judge
 - FBC Purchasing
 - Contractor
 - Consultant

Address: 301 Jackson Street
 Richmond, Texas 77469
Phone: 281-633-7500
Fax: 281-342-7366
Web site: www.FortBendCountyTx.gov

PROJECT:
 Precint 2 - Mobility Projects
 Brand Lane - From Avenue E to US90A
 Fort Bend Count Project 718-769

CHANGE ORDER NUMBER	4
DATE	12-14-15
PROJECT NUMBER	718/769
	Fort Bend County
CONTRACT FOR	
CONTRACT DATE	10-1-14
FBC PURCHASE ORDER NO	116140

CONTRACTOR:
 Allgood Construction Co., Inc.
 1702 Settegast Ranch Rd.
 Richmond, TX 77406

The contract is changed as follows:
 Revised 12" SW Transmisson plans to follow new "Option A Plan." The reason for the change is that an existing 16" waterline was verfyied to be 2 feet lower than original plans determined. The elevation of the waterline has been revised per Option A Plans. Please see attached plans original and Revised Option A.

Not valid until signed by Fort Bend County and Contractor.

The Original (Contract Sum)	\$	6,870,000.00
Net change by previously authorized Change Orders	\$	(263,492.32)
The (Contract Sum) Prior to this Change Order was	\$	6,606,507.68
The (Contract Sum) will be <input checked="" type="checkbox"/> increased <i>or</i> <input type="checkbox"/> decreased <i>or</i> <input type="checkbox"/> unchanged by this Change Order in the amount of		
	\$	22,600.00
The new (Contract Sum) including this Change Order will be	\$	6,629,107.68

The Contract Time will be increased *or* decreased *or* unchanged by **7** days.
 The Date of Substantial Completion as of this Change Order therefore is
 changed *or* unchanged to **April 1, 2016.**

Authorized:

Fort Bend County Engineering
 Rick J. Staigle, PE, PTTOE
 301 Jackson
 Richmond, Texas 77469

CONTRACTOR
 Allgood Construction Co., Inc.
 1702 Settegast Ranch Rd.
 Richmond, TX 77406

Fort Bend County Judge
 Honorable Robert E. Hebert
 301 Jackson St., #719
 Richmond, Texas 77469

By: *Rick J. Staigle, PE, PTTOE*
 (signature)
 DATE: 12/24/15


By: *[Signature]*
 (signature)
 DATE: 12/14/15

By: _____
 (signature)
 DATE: _____

FORT BEND COUNTY PROJECT 718/769
BRAND LANE - FROM AVENUE E TO US90A
Change Order 4 - Option A for Bore Under Highway 90

Change Order 4

Item No.	Spec No.	Item Description	Unit Measure	Unit Quantity	Unit Price	Total in Figures
A. Time Spent to Date on Orginal Drawing						
1		Removal of Trench Safety from Original plans. Reason for removal depth of both bore pits will change in elevation from orginal plans.	LS	1.00	\$1,500.00	\$1,500.00
2		R/A Boring - (Boring Subcontractor Price)	LS	1.00	\$2,500.00	\$2,500.00
3		Labor & equipment - 1 day spent on orginal bore plan and removal of trench saftey (not including installation of trench safety for orginal plan)	LS	1.00	\$4,500.00	\$4,500.00
A. Total - Time Spent to Date on Orginal Drawing						\$8,500.00
B. Option A						
5		Install 12-inch waterline offset on North and South side of Highway 90	EA	2.00	\$4,000.00	\$8,000.00
6		Reinstall trench saftey due to elevation changes of bore pit.	EA	2.00	\$1,500.00	\$3,000.00
7		Labor & Equipment for back filling bore pit on south side and digging deeper on the north side of highway 90 because of elevation changes.	LS	1.00	\$3,100.00	\$3,100.00
B. Total - Option A						\$14,100.00
Total Cost - Change Order 4						\$22,600.00

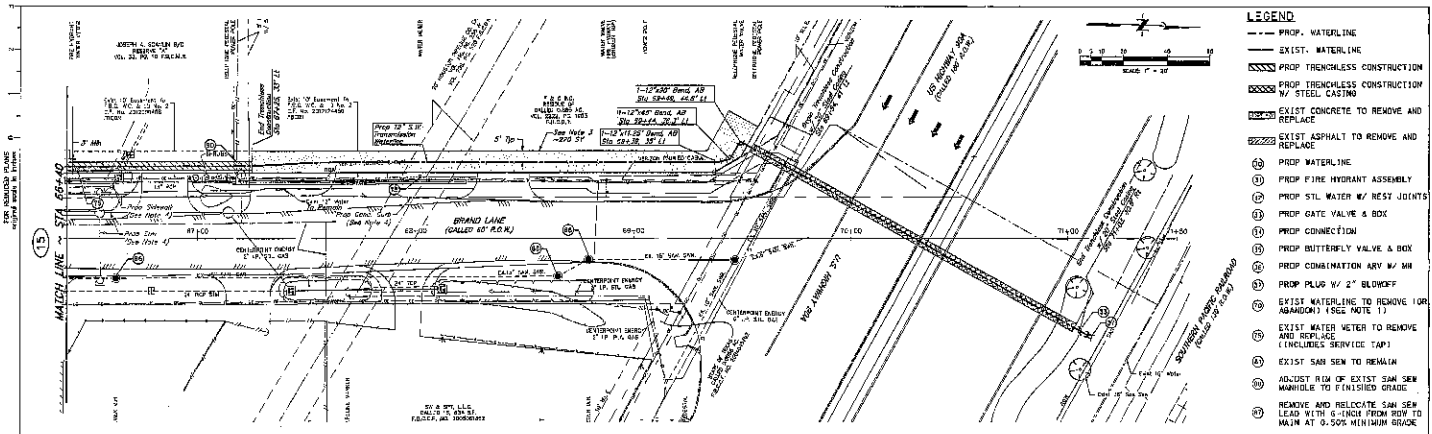


- LEGEND**
- PROP. WATERLINE
 - EXIST. WATERLINE
 - PROP. TRENCHLESS CONSTRUCTION W/ STEEL CASTING
 - PROP. TRENCHLESS CONSTRUCTION W/ STEEL CASTING
 - EXIST. CONCRETE TO REMOVE AND REPLACE
 - EXIST. ASPHALT TO REMOVE AND REPLACE
 - ① PROP. WATERLINE
 - ② PROP. FIRE HYDRANT ASSEMBLY
 - ③ PROP. STL. WATER W/ REST JOINTS
 - ④ PROP. GATE VALVE & BOX
 - ⑤ PROP. CONNECTION
 - ⑥ PROP. BUTTERFLY VALVE & BOX
 - ⑦ PROP. CONNECTION ARY W/ MI
 - ⑧ PROP. PLUS W/ 2" BLOWOFF
 - ⑨ EXIST. WATERLINE TO REMOVE (OR ABANDON) (SEE NOTE 1)
 - ⑩ EXIST. WATER METER TO REMOVE AND REPLACE (INCLUDES SERVICE TAP)
 - ⑪ EXIST. SAN SEW TO REMAIN
 - ⑫ ADJUST RIM OF EXIST. SAN SEW MANHOLE TO FINISHED GRADE
 - ⑬ REMOVE AND RELOCATE SAN SEW LEAD WITH 6" INCH FROM SHIP TO MAIN AT 0.50% MINIMUM GRADE
 - ⑭ EXIST. FENCE TO REMOVE AND REPLACE TO ROW
 - ⑮ EXIST. LANDSCAPING TO REMOVE AND REPLACE

- NOTES:**
1. Contractor to remove and dispose of existing utilities as necessary for construction of roads and utilities. Existing utilities not removed shall be cut, capped, and abandoned in place. Remove all pieces of all steel gate valves and the hydrant.
 2. Proposed system to be installed (1) within Right-of-Way and turned to face the proposed street.
 3. Remove and replace pavement as necessary for construction of this proposed utility, to the nearest joint or transition location.
 4. See Plans and Drainage Plan sheets for details regarding proposed pavement and street gutter location.
 5. For partial subsurface improvements, contractor to use reinforced joints in lieu of concrete barrel blocks.

ADDITIONAL NOTES:
 CITY OF SEASIDE LAND GEOMETRIC CONTROL STATION REFERENCE NO. 222-00-000 TO A 3" BRASS CAP AT THE SOUTHWEST CORNER OF THE INTERSECTION OF JULES AVENUE AND JENSEN LANE EQUIPMENT OF CONCRETE MANHOLE AND 15.7" DIAMETER OF MANHOLE POLE.
 PRIVATE UTILITY LINES SHOWN
 DATE: 11/14/13
 DRAWN BY: [Signature]
 CHECKED BY: [Signature]

BRAND LANE BASELINE "A"

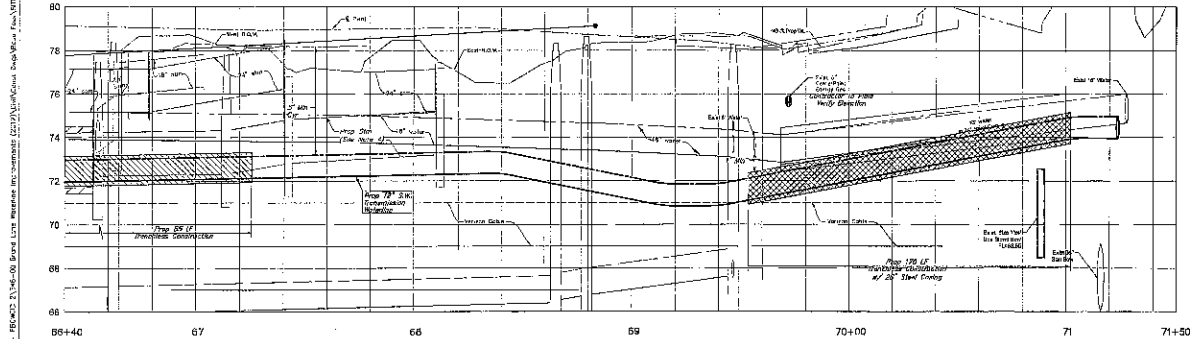

Original Plan

NO.	REVISION	DATE	BY

FORT BEND COUNTY
 ENGINEERING DEPARTMENT



FORT BEND COUNTY W.C. & I.D. NO. 2
 FORT BEND COUNTY, TEXAS
 J.C. JONES & CARTER, INC.
 ENGINEERS & LAND SURVEYORS
 10000 W. STATE HIGHWAY 290, SUITE 100
 HOUSTON, TEXAS 77054



NO.	REVISION	DATE	BY

PROJECT: BRAND LANE - WATERLINE IMPROVEMENTS
 SHEET NO. 28 / 202

From: Jason Kirby
To: Michael Boenig; "Epi Salazar"; Crawford, Wesley; "Kyle H. Kasper"; "Cristin Emshoff"; "Charles Russell"
Subject: RE: Brand lane - Waterline update
Date: Friday, December 18, 2015 8:08:56 AM
Attachments: image001.png

the board approved the bore changes for the shallow option A. you are good to go from the district's aspect.

Jason A. Kirby, P. E.
District Engineer
ForBend County WC&ID No. 2
281-499-2041

----- Original message -----

From: Michael Boenig <michael@allgoodconst.com>
Date: 12/18/2015 8:07 AM (GMT-06:00)
To: Jason Kirby <jkirby@fbcwcid2.com>, 'Epi Salazar' <epi.salazar@seshorizon.com>, "Crawford, Wesley" <Wesley.Crawford@fortbendcountytexas.gov>, "Kyle H. Kasper" <kkaspar@jonescarter.com>, 'Cristin Emshoff' <CEmshoff@staffordtx.gov>, 'Charles Russell' <crussell@cityofstafford.com>
Subject: Brand lane - Waterline update

Jason,

I was wondering if you have received approval from the water district board for the change order amount for the bore under 90? We would like to be able to start the bore Monday morning which would mean we need to get everything set up today. Please let me know as soon as possible so I can inform my guys.

Thank you,

Michael Boenig

Project Manager

Office: 832-847-4071

Cell: 832-451-0393

Email: michael@allgoodconst.com

