Fort Bend County Tabulation Bid 24-059 Construction of African American Memorial Phase One for Fort Bend County

Recommended: SpawGlass Funding: 2020 & 2023 Parks Bonds

Company	Bid Price	Completion Time in Calendar Days
SpawGlass Civil Construction, Inc. Houston, Tx	\$9,498,137.82	365

African American Memorial at Bates M. Allen Park

General Summary		ESTIMATE	CONTRACTOR #1 SPAWGLASS
Division	Work Category	Total	
Division 01	General Conditions	\$696,300.24	\$1,584,561.68
Division 03	Concrete Place & Finish	\$1,135,298.40	\$1,407,757.00
Division 03	Precast Concrete/GFRC	\$3,116,437.00	\$3,550,147.00
Division 04	Masonry & Stone	\$22,929.00	\$60,627.00
Division 05	Metals	\$78,764.50	\$57,842.00
Division 06	Carpentry		\$39,800.00
Division 07	Thermal & Moisture Protection	\$11,104.00	
Division 09	Finishes		
Division 10	Building Specialties	\$60,800.00	\$27,891.00
Division 11	Equipment		
Division 12	*Furnishings (removed from scope of estimate but included in bid from GC)		
Division 13	Special Construction	\$100,000.00	
Division 22	Plumbing		
Division 23	HVAC		
Division 26	Electrical	\$215,707.80	\$346,041.00
Division 31	Earthwork (Includes SWPP)	\$448,499.50	\$307,511.00
Division 32	Exterior Improvements	\$766,422.00	\$1,820,651.00
Division 33	Site Utilities		\$295,309.14
	Subtotal	\$6,652,262.44	\$9,498,137.82
	*GC Fee (Rolled up into General Conditions)		
	Construction Contingency		
	Construction Sub-Total	\$6,652,262.44	\$9,498,137.82
	*Site Lighting (Included in Electrical)	\$2,637,528.00	
	Construction Total	\$2,037,326.00	



COUNTY PURCHASING AGENT Fort Bend County, Texas

Vendor Information

Jaime Kovar Purchasing Agent

Office (281) 341-8640

THE RESERVE THE PROPERTY OF THE PERSON NAMED IN COLUMN TWO IN COLUMN THE PERSON NAMED IN COLUMN THE PE	T			
Legal Company Name (top line of W9)	SpawGlass Civil Construction, Inc.			
Business Name (if different from legal name				
Type of Business	Corporation/LLC Sole Proprietor/Ind	dividual	Partnership Tax Exempt	Age in Business?
Federal ID # or S.S. #	76-049720	05	SAM.gov Unique Entity ID # DX	BNAEKWHX18
SAM.gov CAGE / NCAGE	5DDK5			
Publicly Traded Business	<u>×</u> No Yo	es Ticker Sym	ibol	
Remittance Address	13800 West Road			
City/State/Zip	Houston, TX 77041			
Physical Address	Same as above			
City/State/Zip				
Phone Number		281	-970-5300	
E-mail	Mark Grauvogl			
Contact Person		Mark.Grauvo	gl@SpawGlass.com	
Check all that apply to the company listed above and provide certification number.	DBE-Disadvantaged Business Enterp SBE-Small Business Enterprise HUB-Texas Historically Underutilize WBE-Women's Business Enterprise	ed Business	Certification # Certification # Certification # Certification #	
Company's gross annual	<\$500,000	\$500,000-5	\$4,999,999	
receipts	\$5,000,000-\$16,999,999	\$17,000,00	0-\$22,399,999	>\$22,400,000 <u>xx</u>
NAICs codes (Please enter all that apply)	23	37000, 2	37990, 236220	
Signature of Authorized Representative	Wahlan			
Printed Name	Weston Voss			
Title	President			
Date	05/21/2024			

THIS FORM MUST BE SUBMITTED WITH THE SOLICITATION RESPONSE

Fort Bend County, Texas Invitation for Bid



Construction of African American Memorial Phase One for Fort Bend County BID 24-059

SUBMIT BIDS TO:

Fort Bend County Purchasing Department Travis Annex 301 Jackson, Suite 201 Richmond, TX 77469

Note: All correspondence must include the term "Purchasing Department" in address to assist in proper delivery

SUBMIT NO LATER THAN:

Tuesday, May 21, 2024 2:00 PM (Central)

LABEL ENVELOPE:

BID 24-059 African American Memorial Phase One

ALL BIDS MUST BE RECEIVED IN AND TIME/DATE STAMPED BY THE PURCHASING OFFICE OF FORT BEND COUNTY ON OR BEFORE THE SPECIFIED TIME/DATE STATED ABOVE.

BIDS RECEIVED AS REQUIRED WILL THEN BE OPENED AND PUBLICLY READ.

BIDS RECEIVED AFTER THE SPECIFIED TIME, WILL BE RETURNED UNOPENED.

Results will not be given by phone. Results will be provided to bidder in writing after Commissioners Court award. Requests for information must be in writing and directed to:
Tyler Kendziora
Senior Buyer
Tyler.Kendziora@fortbendcountytx.gov

Vendor Responsibilities:

- Download and complete any addendums. (Addendums will be posted on the Fort Bend County website no Later than 48 hours prior to bid opening)
- > Submit response in accordance with requirements stated on the cover of this document.
- > DO NOT submit responses via email or fax.

Prepared: 04/24/24 Issued: 04/28/24

1.0 GENERAL REQUIREMENTS:

- 1.1 Read this entire document carefully. Follow all instructions. You are responsible for fulfilling all requirements and specifications. Be sure you understand them.
- 1.2 General Requirements apply to all advertised bids; however, these may be superseded, whole or in part, by the scope, special requirements, specifications, special specifications or other data contained herein.
- 1.3 Governing Law: Bidder is advised that these requirements shall be fully governed by the laws of the State of Texas and that Fort Bend County may request and rely on advice, decisions and opinions of the Attorney General of Texas and the County Attorney concerning any portion of these requirements.
- 1.4 Bid Form Completion: Fill out, sign, and return to the Fort Bend County Purchasing Department one (1) complete bid form. An authorized representative of the bidder must sign the Contract Sheet. The bid document must be in a sealed envelope marked with the appropriate bid number and title. The Contract will be binding only when signed by the County Judge, Fort Bend County and a purchase order authorizing the item(s) desired has been issued. The use of corrective fluid is not acceptable and may result in the disqualification of bid. If an error is made, the bidder must draw a line through error and initial each change.
- 1.5 Bid Returns: Bidders must return all completed bids to the Fort Bend County Purchasing Department at 301 Jackson, Suite 201 Richmond Texas no later than 2:00 P.M. on the date specified. Late bids will not be accepted. Bids must be submitted in a sealed envelope, addressed as follows: Fort Bend County Purchasing Agent, Travis Annex, 301 Jackson, Suite 201 Richmond, Texas 77469.
- 1.6 Addenda: No interpretation of the meaning of the drawings, specifications or other bid documents will be made to any bidder orally. All requests for such interpretations must be made in writing addressed to Tyler Kendziora, Senior Buyer, 301, Jackson, Suite 201, Richmond, Texas, 77469, E-mail: Tyler.Kendziora@fortbendcountytx.gov. Any and all interpretations and any supplemental instructions will be in the form of written addenda to the contract documents which will be posted on Fort Bend County's website. Addenda will ONLY be issued by the Fort Bend County Purchasing Agent. It is the sole responsibility of each bidder to insure receipt of any and all addenda. All addenda issued will become part of the contract documents. Bidders must sign and include it in the returned bid package. Deadline for submission of questions and/or clarification is no later than Tuesday, May 14, 2024 at 9:30AM (central) Requests received after the deadline will not be responded to due to the time constraints of this bid process.
- 1.7 References: All bidders must submit, WITH BID, at least three (3) references

- from clients for whom a project similar to that specified herein has been successfully accomplished. References must include, clients' name, contact person and telephone number.
- 1.8 Bid Bond: All bidders must submit, **WITH BID**, a cashier's check or certified check for at least five percent (5%) of the total bid price, payable to the order of Fort Bend County, or a Bid Bond in the same amount issued by a surety, acceptable to Fort Bend County, authorized to do business in the State of Texas, as a guarantee that the Bidder will do the work described herein at the rates stated herein. Unsuccessful bidder's Cashier's Check or Certified Check will be returned only after a written request to do so have been received in the Office of the Fort Bend County Purchasing Agent.
- 1.9 Material Safety Data Sheets: Under the "Hazardous Communication Act", commonly known as the "Texas Right to Know Act", a bidder must provide to Fort Bend County and using departments, with each delivery, material safety data sheets, which are, applicable to hazardous substances defined in the Act. Bidders are obligated to maintain a current, updated file in the Fort Bend County Purchasing Department. Failure of the bidder to maintain such a file will be cause to reject any bid applying thereto.
- 1.10 Pricing: Prices for all goods and/or services shall be firm for the duration of this Contract and shall be stated on the bid sheet. Prices shall be all inclusive. No price changes, additions, or subsequent qualifications will be honored during the course of the Contract. All prices must be written in ink or typewritten. If there are any additional charges of any kind, other than those mentioned above, specified or unspecified, bidder MUST indicate the items required and attendant costs or forfeit the right to payment for such items.
- 1.11 Term Contracts: If the Contract is intended to cover a specific time period, said time will be given in the specifications under scope.
- 1.12 Recycled Materials: Fort Bend County encourages the use of products made of recycled materials and shall give preference in purchasing to products made of recycled materials if the products meet applicable specifications as to quantity and quality. Fort Bend County will be the sole judge in determining product preference application.
- 1.13 Evaluation: Evaluation shall be used as a determinant as to which bid items or services are the most efficient and/or most economical for Fort Bend County. It shall be based on all factors which have a bearing on price and performance of the items in the user environment. All bids are subject to tabulation by the Fort Bend County Purchasing Department and recommendation to Fort Bend County Commissioners Court. Compliance with all bid requirements, delivery and needs of the using department are considerations in evaluating bids. Pricing is NOT the only criteria for making a recommendation. The Fort Bend County Purchasing Department reserves the right to contact any bidder, at any time, to clarify, verify

or request information with regard to any bid.

- 1.14 Disqualification of Bidder: Upon signing this bid document, a bidder offering to sell supplies, materials, services, or equipment to Fort Bend County certifies that the bidder has not violated the antitrust laws of this state codified in section 15.01, et seq., Business & Commerce Code, or the federal antitrust laws, and has not communicated directly or indirectly the bid made to any competitor or any other person engaged in such line of business. Any or all bids may be rejected if Fort Bend County believes that collusion exists among the bidders. Bids in which the prices are obviously unbalanced may be rejected. If multiple bids are submitted by a bidder and after the bids are opened, one of the bids is withdrawn, the result will be that all of the bids submitted by that bidder will be withdrawn; however, nothing herein prohibits a vendor from submitting multiple bids for different products or services.
- 1.15 Awards: Fort Bend County reserves the right to award this Contract on the basis of lowest and best bid in accordance with the laws of the State of Texas, to waive any formality or irregularity, to make awards to more than one bidder, to reject any or all bids. In the event the lowest dollar bidder meeting specifications is not awarded a contract, the bidder may appear before the Commissioners Court and present evidence concerning its responsibility.
- 1.16 Contract Obligation: Fort Bend County Commissioners Court must award the Contract and the County Judge or other person authorized by the Fort Bend County Commissioners Court must sign the Contract before it becomes binding on Fort Bend County or the bidders. Department heads are not authorized to sign agreements for Fort Bend County. Binding agreements shall remain in effect until all products and/or services covered by this purchase have been satisfactorily delivered and accepted.

2.0 SCOPE:

It is the intent of Fort Bend County to contract with one (1) vendor for all materials, supplies, equipment, tools, services, labor and supervision necessary to complete the construction of African American Memorial Phase One located at 630 Charlie Roberts Ln., Kendleton, Texas 77451, hereinafter referred to as the "Project," as specified herein.

2.1 Work means the procurement, delivery and proper construction and/or installation of all materials and facilities and associated appurtenances necessary to fulfill the winning bidder's obligations (hereinafter the "Contractor") under the Contract as awarded for the Project specified herein, including the coordination and administration of all services necessary for Contractor, and/or its agents and/or subcontractors, to fulfill Contractor's obligations under the Contract.

3.0 PRE-BID CONFERENCE:

A pre-bid conference will be conducted on **Tuesday, May 07, 2024 at 9:00 AM** (CST). The pre-bid conference will be held at the Fort Bend County Purchasing Department located in the Travis Annex at 301 Jackson, Suite 201, Richmond, Texas 77469. All bidders are encouraged to attend.

4.0 LIQUIDATED DAMAGES:

The County and the Contractor recognize the delays, expense, and difficulties involved in proving in a legal or arbitration proceeding the actual loss suffered by the County if the work is not complete on time. Accordingly, instead of requiring any such proof, the County and the Contractor agree that as liquidated damages for delay (but not as a penalty) the Contractor shall pay the County \$250.00 for each day that expires after the time specified herein for completion until the Work is complete, unless contract time has been adjusted by extension of time approved by Commissioner's Court.

The Contractor will be placed on one (1) year probation if liquidated damages are accrued. During the probation period, if the Contractor accrues liquidated damages on another project, they will be disqualified from being awarded any County work for two (2) years.

5.0 COMPLETION TIME & PAYMENT:

- 5.1 Fort Bend County shall pay the Contractor in current funds for the Contractor's performance of the Contract the contract sum, as stated herein, after receipt of notice to proceed and a purchase order issued by the Fort Bend County Purchasing Agent.
- 5.2 Based upon Applications for payment submitted to the County Auditor, Fort Bend County shall make progress payments on account of the contract sum to the Contractor as provided below and elsewhere in the contract documents.
 - 5.2.1 The period covered by each application for payment shall be one calendar month ending on the last day of the month.
 - 5.2.2 Provided a customary, accurate and complete application for payment is received by the County Auditor not later than the 15th day of a month, Fort Bend County shall make payment of all undisputed amounts to the Contractor not later than the 15th day of the next month. If an application for payment is received by the County Auditor after the application deadline fixed above, payment shall be made by Fort Bend County not later than 30 days after the County Auditor receives the application for payment.
 - 5.2.3 Application for payment shall indicate the percentage of completion of each portion of the Project as of the end of the period covered by the application for payment.

- 5.2.4 Subject to the provisions of the contract documents, the amount of each progress payment shall be computed as follows:
 - 5.2.4.1 Take that portion of the contract sum properly allocable to completed Project less retainage of ten percent (10%).
 - 5.2.4.2 Add that portion of the contract sum properly allocable to materials and equipment delivered and suitably stored at the site for subsequent incorporation in the completed construction (or, if approved by Fort Bend County, suitably stored off the site at a location agreed upon in writing), less retainage of ten percent (10%).
 - 5.2.4.3 Subtract the aggregate of previous payments made by Fort Bend County.
 - 5.2.4.4 The progress payment amount as determined in above shall be further modified under the following circumstances:

Upon substantial completion of the Project, add a sum sufficient to increase the total payments to one hundred percent (100%) of the contract sum, less such amounts as Fort Bend County shall determine should be deducted for incomplete work and unsettled claims.

- 5.2.4.5 Final payment, constituting the entire unpaid undisputed balance of the contract sum, shall be made by Fort Bend County to the Contractor when Fort Bend County and the Contractor agree that the Contract has been fully performed by the Contractor.
- 5.3 Before the first application for payment, the Contractor shall submit to the Parks Department a schedule of values allocated to various portions of the work, prepared in such form and supported by such data to substantiate its accuracy as the Parks Department may require. This schedule, unless objected to by the Parks Department shall be used as a basis for reviewing the Contractor's application for payment.
- 5.4 Contractor must provide with each application for payment a contractor's affidavit certifying bills against the Contractor for labor, material and expendable equipment employed in the performance of Contractor have been paid in full prior to acceptance of final payment from Fort Bend County.
- 5.5 The Contractor will permit Fort Bend County, or any duly authorized agent of Fort Bend County, to inspect and examine the books and records of the Contractor for the purpose of verifying the amount of work performed under the Contract.

Fort Bend County's right to inspect survives the termination of the Contract for a period of five years.

6.0 LIMIT OF APPROPRIATION:

Prior to the execution of this Contract, Contractor has been advised by County, and Contractor clearly understands and agrees, such understanding and agreement being of the absolute essence to this Contract, that County shall have available only those funds specifically allocated in this Contract to fully discharge any and all liabilities which may be incurred by County in bringing this Project to an absolute conclusion, resulting in a complete, fully furnished, fully equipped and fully usable facility, and that the total of any and all basic construction costs, costs of providing the required services and materials, all fees and compensation of any sort to the Contractor, and any and all costs for any and all things or purposes coming inuring under or out of this Contract, irrespective of the nature thereof, shall not exceed said specifically allocated sum, notwithstanding any word, statement or thing contained in or inferred from the preceding provision of this Contract which might in any light by any person be interpreted to the contrary.

7.0 RIGHT TO ASSURANCE:

Whenever Fort Bend County in good faith has reason to question the Contractor's intent or ability to perform, Fort Bend County may demand that the Contractor give written assurance of its intent to perform and its plan to properly continue performance, including a reasonably detailed timeline. In the event that a demand is made and no assurance is given within five (5) business days, Fort Bend County may treat this failure as an anticipatory repudiation of the Contract.

8.0 PERFORMANCE & PAYMENT BONDS:

Performance and Payment Bonds: In the event the total accepted bid price exceeds \$25,000 the Contractor must provide to the Office of the County Purchasing Agent, a performance bond and a payment bond, each in the amount of 100% of the total contract sum within ten (10) calendar days after receipt of notification of bid award. Such bonds shall be executed by a corporate surety duly authorized and admitted to do business in the State of Texas and licensed in the State of Texas to issue surety bonds with a Best Rating of "A" or better. Fort Bend County reserves the right to accept or reject any surety company proposed by the Contractor. In the event Fort Bend County rejects, the proposed surety company, the Contractor will be afforded five (5) additional days to submit the required bonds issued by a surety company acceptable to Fort Bend County.

9.0 POWER OF ATTORNEY:

An attorney-in-fact who signs a bid bond, performance bond or payment bond must file with each bond a certified and effectively dated copy of his or her power of attorney.

10.0 INSURANCE:

- 10.1 All respondents shall submit, with response, a <u>current</u> certificate of insurance indicating coverage in the amounts stated below. In lieu of submitting a certificate of insurance, respondents may submit, with response, a notarized statement from an Insurance company, authorized to conduct business in the State of Texas, and acceptable to Fort Bend County, guaranteeing the issuance of an insurance policy, with the coverage stated below, to the firm named therein, if successful, upon award of this Contract.
- At contract execution, contractor shall furnish County with properly executed certificates of insurance which shall evidence all insurance required and provide that such insurance shall not be canceled, except on 30 days prior written notice to County. Contractor shall provide certified copies of insurance endorsements and/or policies if requested by County. Contractor shall maintain such insurance coverage from the time Services commence until Services are completed and provide replacement certificates, policies and/or endorsements for any such insurance expiring prior to completion of Services. Contractor shall obtain such insurance written on an Occurrence form (or a Claims Made form for Professional Liability insurance) from such companies having Best's rating of A/VII or better, licensed or approved to transact business in the State of Texas, and shall obtain such insurance of the following types and minimum limits:
 - 10.2.1 Workers' Compensation insurance. Substitutes to genuine Workers' Compensation Insurance will not be allowed.
 - 10.2.2 Employers' Liability insurance with limits of not less than \$1,000,000 per injury by accident, \$1,000,000 per injury by disease, and \$1,000,000 per bodily injury by disease.
 - 10.2.3 Commercial general liability insurance with a limit of not less than \$1,000,000 each occurrence and \$2,000,000 in the annual aggregate. Policy shall cover liability for bodily injury, personal injury, and property damage and products/completed operations arising out of the business operations of the policyholder.
 - 10.2.4 Business Automobile Liability coverage with a combined Bodily Injury/Property Damage limit of not less than \$1,000,000 each accident. The policy shall cover liability arising from the operation of licensed vehicles by policyholder.
- 10.3 County and the members of Commissioners Court shall be named as additional insured to all required coverage except for Workers' Compensation and Professional Liability (if required). All Liability policies including Workers' Compensation written on behalf of contractor, excluding Professional Liability,

- shall contain a waiver of subrogation in favor of County and members of Commissioners Court.
- 10.4 If required coverage is written on a claims-made basis, contractor warrants that any retroactive date applicable to coverage under the policy precedes the effective date of the contract; and that continuous coverage will be maintained or an extended discovery period will be exercised for a period of two (2) years beginning from the time that work under the agreement is completed.
- 10.5 Contractor shall not commence any portion of the work under this Contract until it has obtained the insurance required herein and certificates of such insurance have been filed with and approved by Fort Bend County.
- 10.6 No cancellation of or changes to the certificates, or the policies, may be made without sixty (60) days prior, written notification to Fort Bend County.
- 10.7 Approval of the insurance by Fort Bend County shall not relieve or decrease the liability of the Contractor.
- Builder's Risk Insurance: Contractor is required to provide proof before a Purchase Order is issued for this project and keep in full force and effect until the Transfer Date, Builders Risk Insurance, subject to policy terms and conditions, of direct physical loss or damage to property, materials, equipment and supplies which are to become an integral part of the Project, whether owned by Contractor, or subcontractors of every tier, and in which one or more of same has an insurable interest, while in transit, while at the Construction Site awaiting construction, during construction, and until the Transfer Date. Such insurance shall be maintained to cover, as nearly as practicable, the insurable value of such property, materials, equipment and supplies at risk, and shall contain a waiver of subrogation in favor of Contractor, Architect, subcontractors of any tier and Owner for loss or damage occurring during the Work and shall name Contractor as the named insured and Owner as additional insureds. All Builder's Risk Insurance proceeds shall be paid directly to the Contractor.

11.0 INDEMNIFICATION:

Respondent shall save harmless County from and against all claims, liability, and expenses, including reasonable attorney's fees, arising from activities of respondent, its agents, servants or employees, performed under this agreement that result from the negligent act, error, or omission of respondent or any of respondent's agents, servants or employees.

11.1 Respondent shall timely report all such matters to Fort Bend County and shall, upon the receipt of any such claim, demand, suit, action, proceeding, lien or judgment, not later than the fifteenth day of each month; provide Fort Bend County with a written report on each such matter, setting forth the status of each matter, the schedule or planned proceedings with respect to each matter and the

- cooperation or assistance, if any, of Fort Bend County required by Respondent in the defense of each matter.
- 11.2 Respondent's duty to defend, indemnify and hold Fort Bend County harmless shall be absolute. It shall not abate or end by reason of the expiration or termination of any contract unless otherwise agreed by Fort Bend County in writing. The provisions of this section shall survive the termination of the contract and shall remain in full force and effect with respect to all such matters no matter when they arise.
- 11.3 In the event of any dispute between the parties as to whether a claim, demand, suit, action, proceeding, lien or judgment appears to have been caused by or appears to have arisen out of or in connection with acts or omissions of Respondent, Respondent shall never-the-less fully defend such claim, demand, suit, action, proceeding, lien or judgment until and unless there is a determination by a court of competent jurisdiction that the acts and omissions of Respondent are not at issue in the matter.
- 11.4 Respondent's indemnification shall cover, and Respondent agrees to indemnify Fort Bend County, in the event Fort Bend County is found to have been negligent for having selected Respondent to perform the work described in this request.
- 11.5 The provision by Respondent of insurance shall not limit the liability of Respondent under an agreement.
- 11.6 Respondent shall cause all trade contractors and any other contractor who may have a contract to perform construction or installation work in the area where work will be performed under this request, to agree to indemnify Fort Bend County and to hold it harmless from all claims for bodily injury and property damage that may arise from said Respondent's operations. Such provisions shall be in form satisfactory to Fort Bend County.
- 11.7 Loss Deduction Clause Fort Bend County shall be exempt from, and in no way liable for, any sums of money which may represent a deductible in any insurance policy. The payment of deductibles shall be the sole responsibility of Respondent and/or trade contractor providing such insurance.

12.0 PREVAILING WAGES:

This project is subject to the prevailing wage rate requirements of Chapter 2258 of the Government Code. All persons employed by Contractor shall be compensated at not less than the rates shown below. Contractor shall keep detailed records of each of its workers and said records shall be made available to County for inspection at all reasonable times. The Contractor shall pay Fort Bend County sixty dollars (\$60.00) for each worker employed by the Contractor for the provision of services described herein for each calendar day or part of the day that the

worker is paid less than the below stated rates. Contractors may also visit www.wdol.gov/dba.aspx.

General Decision Number: TX20240247 01/05/2024 Superseded General Decision Number: TX20230247

State: Texas

Construction Type: Building

County: Fort Bend County in Texas.

BUILDING CONSTRUCTION PROJECTS (does not include single family homes or apartments up to and including 4 stories).

Note: Contracts subject to the Davis-Bacon Act are generally required to pay at least the applicable minimum wage rate required under Executive Order 14026 or Executive Order 13658. Please note that these Executive Orders apply to covered contracts entered into by the federal government that are subject to the Davis-Bacon Act itself, but do not apply to contracts subject only to the Davis-Bacon Related Acts, including those set forth at 29 CFR 5.1(a)(1).

If the contract is entered into on or after January 30, 2022, or the contract is renewed or extended (e.g., an option is exercised) on or after January 30, 2022: Executive Order 14026 generally applies to the contract. The contractor must pay all covered workers at least \$17.20 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on the contract in 2024.

If the contract was awarded on or between January 1, 2015 and January 29, 2022, and the contract is not renewed or extended on or after January 30, 2022: Executive Order 13658 generally applies to the contract. The contractor must pay all covered workers at least \$12.90 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on that contract in 2024.

The applicable Executive Order minimum wage rate will be adjusted annually. If this contract is covered by one of the Executive Orders and a classification considered necessary for performance of work on the contract does not appear on this wage determination, the contractor must still submit a conformance request.

Additional information on contractor requirements and worker protections under the Executive Orders is available at http://www.dol.gov/whd/govcontracts.

Modification Number Publication Date 0 01/05/2024

Rates Fringes

ASBE0022-009 07/03/2023

ASBESTOS WORKER/HEAT & FROST INSULATOR (Duct, Pipe and Mechanical System Insulation)	\$ 28.35	16.02
BOIL0074-003 07/01/2023		
BOILERMAKER	\$ 37.00	24.64
CARP0551-008 04/01/2021		
CARPENTER (Excludes Acoustical Ceiling Installation, Drywall Hanging, Form Work and Metal Stud Installation)	\$ 25.86	9.08
ELEC0716-005 08/29/2023		
ELECTRICIAN (Excludes Low Voltage Wiring and Installation of Alarms)	\$ 34.50	10.41
ELEV0031-003 01/01/2023		
ELEVATOR MECHANIC FOOTNOTES:	\$ 49.15	37.335+a+b

A. 6% under 5 years based on regular hourly rate for all hours worked. 8% over 5 years based on regular hourly rate for all hours worked.

ENGI0450-002 04/01/2014

POWER EQUIPMENT OPERATOR

Cranes	\$ 34.85	9.85
IRON0084-002 06/01/2023 IRONWORKER (ORNAMENTAL AND STRUCTURAL)	\$ 27.51	8.13
PLAS0783-001 04/01/2023		
PLASTERER PLUM0068-002 10/01/2023	\$ 31.34	10.30
PLUMBER PLUM0211-010 10/01/2023	\$ 34.86	11.68
PIPEFITTER (Including HVAC Pipe Installation)	\$ 38.31	12.61

B. Holidays: New Year's Day; Memorial Day; Independence Day; Labor Day; Thanksgiving Day; Friday after Thanksgiving Day; Christmas Day; and Veterans Day.

SHEE0054-003 04/01/2020

SHEET METAL WORKER (Excludes HVAC Duct and Unit Installation)	\$ 29.70	13.85
SUTX2014-023 07/21/2014		
ACOUSTICAL CEILING MECHANIC	\$ 16.41 **	3.98
BRICKLAYER CAULKER	\$ 19.86 \$ 15.36 **	0.00 0.00
CEMENT MASON/CONCRETE FINISHER	\$ 13.82 **	0.00
DRYWALL FINISHER/TAPER	\$ 16.30 **	3.71
DRYWALL HANGER AND METAL STUD INSTALLER	\$ 17.45	3.96
ELECTRICIAN (Alarm Installation Only)	\$ 17.97	3.37
ELECTRICIAN (Low Voltage Wiring Only)	\$ 18.00	1.68
FLOOR LAYER: Carpet	\$ 20.00	0.00
FORM WORKER	\$ 11.87 **	0.00
GLAZIER	\$ 19.12	4.41
INSULATOR – BATT	\$ 14.87 **	0.73
IRONWORKER, REINFORCING	\$ 12.10 **	0.00
LABORER: Common or General	\$ 10.79 **	0.00
LABORER: Mason Tender – Brick	\$ 13.37 **	0.00
LABORER: Mason Tender - Cement/Concrete	\$ 10.50 **	0.00
LABORER: Pipelayer	\$ 12.94 **	0.00
LABORER: Roof Tearoff	\$ 11.28 **	0.00
LABORER: Landscape and Irrigation	\$ 9.49 **	0.00
LATHER OPERATOR:	\$ 19.73	0.00

Backhoe/Excavator/Trackhoe	\$ 14.10 **	0.00
OPERATOR: Bobcat/Skid Steer/Skid Loader	\$ 13.93 **	0.00
OPERATOR: Bulldozer	\$ 20.77	0.00
OPERATOR: Drill	\$ 16.22 **	0.34
OPERATOR: Forklift OPERATOR: Grader/Blade	\$ 15.64 ** \$ 13.37 **	0.00
OPERATOR: Loader	\$ 13.55 **	0.94
OPERATOR: Mechanic	\$ 17.52	3.33
OPERATOR: Paver (Asphalt, Aggregate, and Concrete)	\$ 16.03 **	0.00
OPERATOR: Roller	\$ 16.00 **	0.00
PAINTER (Brush, Roller and Spray), Excludes Drywall Finishing/Taping	\$ 16.77 **	4.51
ROOFER	\$ 15.40 **	0.00
SHEET METAL WORKER (HVAC Duct Installation Only)	\$ 17.81	2.64
SHEET METAL WORKER (HVAC Unit Installation Only)	\$ 16.00 **	1.61
SPRINKLER FITTER (Fire Sprinklers)	\$ 22.17	9.70
TILE FINISHER	\$ 12.00 **	0.00
TILE SETTER	\$ 16.17 **	0.00
TRUCK DRIVER: 1/Single Axle Truck	\$ 14.95 **	5.23
TRUCK DRIVER: Dump Truck	\$ 12.39 **	1.18
TRUCK DRIVER: Flatbed Truck	\$ 19.65	8.57
TRUCK DRIVER: Semi-Trailer Truck TRUCK DRIVER: Water Truck	\$ 12.50 ** \$ 12.00 **	0.00 4.11
WATERPROOFER	\$ 14.39 **	0.00

WELDERS - Receive rate prescribed for craft performing operation to which welding is incidental.

** Workers in this classification may be entitled to a higher minimum wage under Executive Order 14026 (\$17.20) or 13658 (\$12.90). Please see the Note at the top of the wage determination for more information. Please also note that the minimum wage requirements of Executive Order 14026 are not currently being enforced as to any contract or subcontract to which the states of Texas, Louisiana, or Mississippi, including their agencies, are a party.

Note: Executive Order (EO) 13706, Establishing Paid Sick Leave for Federal Contractors applies to all contracts subject to the Davis-Bacon Act for which the contract is awarded (and any solicitation was issued) on or after January 1, 2017. If this contract is covered by the EO, the contractor must provide employees with 1 hour of paid sick leave for every 30 hours they work, up to 56 hours of paid sick leave each year. Employees must be permitted to use paid sick leave for their own illness, injury or other health-related needs, including preventive care; to assist a family member (or person who is like family to the employee) who is ill, injured, or has other health-related needs, including preventive care; or for reasons resulting from, or to assist a family member (or person who is like family to the employee) who is a victim of, domestic violence, sexual assault, or stalking. Additional information on contractor requirements and worker protections under the EO is available at https://www.dol.gov/agencies/whd/governmentcontracts.

Unlisted classifications needed for work not included within the scope of the classifications listed may be added after award only as provided in the labor standards contract clauses (29CFR 5.5 (a) (1) (iii)).

The body of each wage determination lists the classification and wage rates that have been found to be prevailing for the cited type(s) of construction in the area covered by the wage determination. The classifications are listed in alphabetical order of ""identifiers"" that indicate whether the particular rate is a union rate (current union negotiated rate for local), a survey rate (weighted average rate) or a union average rate (weighted union average rate).

Union Rate Identifiers

A four letter classification abbreviation identifier enclosed in dotted lines beginning with characters other than ""SU"" or ""UAVG"" denotes that the union classification and rate were prevailing for that classification in the survey. Example: PLUM0198-005 07/01/2014. PLUM is an abbreviation identifier of the union which prevailed in the survey for this classification, which in this example would be Plumbers. 0198 indicates the local union number or district council number where applicable, i.e., Plumbers Local 0198. The next number, 005 in the example, is an internal number used in processing the wage determination. 07/01/2014 is the effective date of the most current negotiated rate, which in this example is July 1, 2014.

Union prevailing wage rates are updated to reflect all rate changes in the collective bargaining agreement (CBA) governing this classification and rate. Survey Rate Identifiers

Classifications listed under the ""SU"" identifier indicate that no one rate prevailed for this classification in the survey and the published rate is derived by computing a weighted average rate based on all the rates reported in the survey for that classification. As this weighted average rate includes all rates reported in the survey, it may include both union and non-union rates. Example: SULA2012-007 5/13/2014. SU indicates the rates are survey rates based on a weighted average calculation of rates and are not majority rates. LA indicates the State of Louisiana. 2012 is the year of survey on which these classifications and rates are based. The next number, 007 in the example, is an internal number used in producing the wage determination. 5/13/2014 indicates the survey completion date for the classifications and rates under that identifier. Survey wage rates are not updated and remain in effect until a new survey is conducted.

Union Average Rate Identifiers

Classification(s) listed under the UAVG identifier indicate that no single majority rate prevailed for those classifications; however, 100% of the data reported for the classifications was union data. EXAMPLE: UAVG-OH-0010 08/29/2014. UAVG indicates that the rate is a weighted union average rate. OH indicates the state. The next number, 0010 in the example, is an internal number used in producing the wage determination. 08/29/2014 indicates the survey completion date for the classifications and rates under that identifier.

A UAVG rate will be updated once a year, usually in January of each year, to reflect a weighted average of the current negotiated/CBA rate of the union locals from which the rate is based.

WAGE DETERMINATION APPEALS PROCESS

- 1.) Has there been an initial decision in the matter? This can be:
- * an existing published wage determination
- * a survey underlying a wage determination
- * a Wage and Hour Division letter setting forth a position on a wage determination matter
- * a conformance (additional classification and rate) ruling

On survey related matters, initial contact, including requests for summaries of surveys, should be with the Wage and Hour National Office because National Office has responsibility for the Davis-Bacon survey program. If the response from this initial contact is not satisfactory, then the process described in 2.) and 3.) should be followed.

With regard to any other matter not yet ripe for the formal process described here, initial contact should be with the Branch of Construction Wage Determinations. Write to:

Branch of Construction Wage Determinations Wage and Hour Division U.S. Department of Labor 200 Constitution Avenue, N.W. Washington, DC 20210

2.) If the answer to the question in 1.) is yes, then an interested party (those affected by the action) can request review and reconsideration from the Wage and Hour Administrator (See 29 CFR Part 1.8 and 29 CFR Part 7). Write to:

Wage and Hour Administrator U.S. Department of Labor 200 Constitution Avenue, N.W. Washington, DC 20210

The request should be accompanied by a full statement of the interested party's position and by any information (wage payment data, project description, area practice material, etc.) that the requestor considers relevant to the issue.

3.) If the decision of the Administrator is not favorable, an interested party may appeal directly to the Administrative Review Board (formerly the Wage Appeals Board). Write to:

Administrative Review Board U.S. Department of Labor 200 Constitution Avenue, N.W. Washington, DC 20210

4.) All decisions by the Administrative Review Board are final.

13.0 PERMITS:

It shall be the sole responsibility of the successful bidder to obtain all required permits in the name of Fort Bend County.

14.0 CONTRACTOR'S RESPONSIBILITY FOR WORK:

- 14.1 <u>Preconstruction Work.</u> Contractor shall do (or cause to be done) the following as preconstruction work:
 - 14.1.1 On written demand as requested by Fort Bend County, cause the Contractor's personnel to meet with Fort Bend County and the Engineer to discuss the status of the Project.
 - 14.1.2 On written demand as requested by Fort Bend County, review drawings and specifications with the Engineer to permit the Contractor and the Engineer to determine the compliance of the proposed facility with applicable building codes.
- 14.2 <u>Construction Work</u>. Contractor shall do (or cause to be done) the following as construction work:

- 14.2.1 Perform (or cause to be performed) all preparatory work at the construction site required herein, including (without limitation) soil and concrete testing and demolition of improvements existing at the construction site and all actions necessary for compliance with all laws and regulations as to actions to be taken by owners or contractors before construction begins, including without limitation those in regard to archaeological and environmental requirements.
- 14.2.2 Construct and install (or cause to be constructed and installed) the Project on the construction site in accordance with this Contract and the drawings and specifications approved by Fort Bend County.
- 14.2.3 Furnish (or cause to be furnished) all materials, supplies, equipment, tools, labor, supervision, utilities, transportation, and other materials and services necessary to complete the Project described herein.
- 14.2.4 Materials testing necessary for the Project and required by laws and regulations, construction industry standards as approved by Fort Bend County and this Contract; the frequency of testing shall be approved by Fort Bend County. It is the contractor's responsibility to engage a material testing laboratory to perform testing on the structural concrete to be used for foundation work in this project. The cost of testing shall be incidental to bid item for drill shaft foundation. Testing of concrete shall comply with current TXDOT criteria. Contractor has to submit the name of the testing laboratory, intended to be used by the contractor for this project, for County's approval.
- 14.3 Standards for Review and Approval. Fort Bend County acknowledges that in order to meet the deadlines for the completion of the Project, and in order to accomplish the efficient completion of the Project, the Contractor may submit matters to Fort Bend County in stages for approval or consent. Upon receipt of any matter submitted by the Contractor for review and approval, Fort Bend County shall review the same and shall diligently and promptly (but in any event within 14 calendar days for any such matter, other than a proposed change order, and within 28 calendar days for a proposed change order) give the Contractor notice of Fort Bend County's approval or disapproval, setting forth in detail all reasons for any disapproval. Fort Bend County's right to disapprove any such matter submitted (other than a proposed change order) shall be limited to the elements thereof (a) which do not conform substantially to matters previously approved, (b) which are new elements not previously presented and approved and the Contractor is unable to demonstrate that such new element is reasonably necessary for completion of the Project, or (c) which depict matters that are violations of this Contract or applicable laws and regulations.
 - 14.3.1 If Fort Bend County disapproves of a particular matter or Proposed Change Order, the Contractor shall have the right to resubmit such matter or Proposed Change Order to Fort Bend County, altered to satisfy Fort

- Bend County's basis for disapproval. Any resubmission shall be subject to review and approval by Fort Bend County.
- 14.3.2 Fort Bend County and the Contractor shall attempt in good faith to resolve any disputes concerning the approval of any aspect of the Project expeditiously, so as not to delay the completion of the Project in accordance with this Contract.
- 14.3.3 Expedited Approvals. Fort Bend County recognizes the importance of expeditious action upon all matters submitted to Fort Bend County for review and approval and of expeditious response to those aspects of the Project requiring approval by governmental authorities having jurisdiction there over. Fort Bend County agrees to exercise its rights of review and approval hereunder with due diligence, reasonableness, and good faith. Fort Bend County shall use its reasonable efforts to expedite any required review of the Project or other matters by any governmental authority.

14.4 Changes.

- 14.4.1 General. Fort Bend County may make changes to the Project by altering, adding to, or deducting from the Project. All changes in the Project which (a) require an adjustment in the contract sum or an adjustment in the final completion date or (b) involve a material change in the overall scope or function of the Project shall be requested and authorized before commencing such changes by use of written change order notices, Proposed Change Orders and Change Orders, which change order procedure shall be the exclusive means to effect such changes in the Project.
- 14.4.2 Change Order Procedure. If at any time Fort Bend County desires to make any change in the Project requiring the issuance of a Change Order, Fort Bend County shall so advise the Contractor in writing by delivery to the Contractor of a written notice describing the change. Upon receipt of such notice initiated by Fort Bend County, the Contractor shall within a reasonable period of time advise Fort Bend County of the Contractor's proposal for the adjustments, if any, in the contract sum, the schedule of values, and the final completion date attributable to such change by delivering a written notice thereof (the "Proposed Change Order") to Fort Bend County. Such Proposed Change Order shall contain a description of the proposed change and shall set forth the Contractor's estimate of the increase or decrease, if any, in the contract sum and the change, if any, in the schedule of values and the final completion date attributable to such change. If the Contractor desires to make a change in the Project requiring the issuance of a change order, the Contractor shall deliver to Fort Bend County a Proposed Change Order. Upon execution by Fort Bend County, a Proposed Change Order shall constitute (and be defined herein as) a "Change Order" for purposes of this Contract. The Contractor shall

forthwith perform the work as changed in accordance with such Change Order. All work performed pursuant to a Change Order shall be performed in accordance with the terms of this Contract. All Proposed Change Orders shall be submitted for approval by Fort Bend County. No action, acquiescence or inaction by Fort Bend County or any representative of Fort Bend County shall be construed to be a waiver of requirements set forth in this Contract in regard to Change Orders or ratification of a violation of such requirements, and all acts in violation of this provision shall be considered void.

- 14.4.3 <u>Change Order Authorization</u>. Each Change Order shall be signed by Fort Bend County and an authorized representative of the Contractor.
- 14.4.4 Contract Sum Adjustments. The contract sum and the schedule of values shall be adjusted only as a result of a Change Order requiring such adjustment. Any extra work performed without a proper Change Order shall be considered voluntary and not subject to additional compensation. The Contractor shall not be entitled to an adjustment in the contract sum (or a Change Order permitting such adjustment) or to damages as a result of any delays in the Project caused by the acts or omissions of Fort Bend County, provided that this sentence is not applicable to delays that constitute more than 90 days in any 365-day period or cause the Project to be interrupted for a continuous period of 45 days through no fault of the Contractor.
- 14.4.5 When Fort Bend County and the Contractor agree upon the adjustments in the contract sum, the schedule of values, and the final completion date attributable to such adjustment, such agreement will be documented by preparation and if approved by the Fort Bend County Commissioners Court, execution of an appropriate Change Order.
- 14.5 <u>Site Access.</u> Prior to the transfer date, Fort Bend County and the Contractor shall have uninterrupted access to the construction site. Subsequent to the transfer date, Fort Bend County will permit the Contractor, the Engineer, and their representatives and subcontractors to enter upon the Project at times reasonably necessary to complete the punch list items.
- Applicable Laws and Regulations. Contractor shall in its performance of the Project comply with all applicable laws and regulations. Any delays in the prosecution of the Project caused by any changes in the laws and regulations or the application or enforcement of the laws and regulations may entitle the Contractor to an extension of time.
- 14.7 <u>Familiarity with Project</u>. The Contractor represents and accepts that it has: (a) visited the property(ies), (b) taken such other steps as may be necessary to ascertain the nature and location of the Project and the general and local conditions which affect the Project or the cost thereof, (c) investigated the labor situation as regards to the Project, (d) examined the property(ies), the obstacles

which may be encountered and all other observable conditions having a bearing upon the performance of the Project, the superintendence of the Project, the time of completion and all other relevant matters, and (e) reported to Fort Bend County the results of all of the foregoing. The Contractor represents that it is familiar with all phases of the Project and the matters that may affect the Project or its prosecution under this Contract.

- 14.8 <u>Standard of Performance</u>. The Contractor shall prosecute (or cause to be prosecuted) the Project in accordance with the best efforts for the construction and development of projects similar to the Project in the State of Texas, using qualified, careful, and efficient contractors and workers and in conformity with the provisions of this Contract. The Contractor shall perform the work in a good and workmanlike manner.
- 14.9 Warranty of Contractor. The Contractor warrants to Fort Bend County that: (i) the Contractor possesses the skill and knowledge ordinarily possessed by wellinformed members of its trade or profession and the Contractor will use its best efforts to ensure that the services provided under this Contract will be performed, delivered, and conducted in accordance with the best professional standards and in accordance with industry standards, and (ii) the Contractor is fully experienced and properly qualified to perform the class of work provided for herein, and that it is properly equipped, organized and financed to perform such work, and (iii) following the date of acceptance of this Contract, the services provided by the Contractor to Fort Bend County will conform to the representations contained in this Contract, including all attachments, schedules and exhibits. All warranties provided by the Contractor in this Contract shall be cumulative, shall be deemed consistent and not in conflict, are intended to be given full force and effect and to be interpreted expansively to give the broadest warranty protection to Fort Bend County.
- 14.10 Contractor's Personnel. Contractor shall employ only competent, skilled personnel for the Project. Prior to the final completion date, the Contractor shall maintain a superintendent who shall be authorized to act on behalf of the Contractor and with whom Fort Bend County may consult at all reasonable times. The superintendent shall not be transferred from the Project without Fort Bend County's consent (which shall not be unreasonably withheld or delayed); provided, however, the superintendent shall not be assigned solely to the Project and shall be entitled to spend reasonable time working on matters unrelated to the Project so long as such work on other matters does not render the superintendent unavailable to the Project or unavailable to Fort Bend County. However, such obligation to furnish the superintendent and such staff personnel shall not be construed (a) to preclude the promotion within the Contractor's organization of any person assigned to the Project or (b) to give rise to any liability of the Contractor if any person assigned to the Project (including, without limitation, the superintendent) leaves the Contractor's employment. If the superintendent is transferred from the Project, Fort Bend County shall have the right to approve the replacement superintendent

(which approval will not be unreasonably withheld or delayed). The Contractor, the Architect, and the other subcontractors shall comply with all applicable health, safety, and loss prevention rules of applicable governmental authorities. The Contractor shall, at its own expense, remove from the Project any person who fails to comply with such rules and instructions. The Contractor shall at all times enforce strict discipline and good order among its employees and shall not employ on the Project any unfit person or anyone not skilled in the work assigned to him. Fort Bend County may, upon written notice to the Contractor, require the Contractor to remove an individual immediately from providing services for the following reasons: violation of the terms and conditions of this Contract; violation of Fort Bend County's or the Contractor's work rules and regulations; criminal activity; or violation of state, federal, or municipal statutes. Fort Bend County may, upon thirty (30) days written notice to the Contractor, require the removal of any individual from providing services without cause.

- 14.11 <u>Inspection</u>. The Project and all parts thereof shall be subject to inspection from time to time by inspectors designated by Fort Bend County. No such inspections shall relieve The Contractor of any of its obligations hereunder. Neither failure to inspect nor failure to discover or reject any of the work as not in accordance with the drawings and specifications or any provision of this Contract shall be construed to imply an acceptance of such work or to relieve the Contractor of any of its obligations hereunder. Fort Bend County agrees that its right of inspection shall be used reasonably and in a timely manner so as not to delay orderly completion of the Project.
- 14.12 Protection Against Risks. The Contractor shall take all precautions which are necessary and adequate, against conditions created during the progress of the Project which involve a risk of bodily harm to persons or a risk of damage or loss to any property. The Contractor shall regularly inspect all work, materials and equipment to discover and determine any such conditions and shall be responsible for discovery, determination, and correction of any such conditions. The Contractor shall comply with all federal, state, and local occupational hazard and safety standards, codes and regulations applicable in the jurisdiction where the Project is being performed. The Contractor shall include the substance of this clause in its entirety in all subcontracts for any work to be performed at the construction site.
- 14.13 Equipment. Except as expressly provided herein to the contrary, the Contractor shall furnish (or cause to be furnished) all construction, transportation, installation, tools, and other equipment and facilities required for the performance of the Project within the times specified herein. Such equipment and facilities shall be serviceable and kept fit for the uses intended. Defective items shall be removed from the construction site promptly and at the Contractor's cost. The Contractor shall schedule (or cause to be scheduled) its other operations so as to not interfere with its duty to timely furnish the necessary equipment and facilities

and personnel to operate the same at the times necessary for the orderly completion of the Project.

- 14.14 <u>Materials</u>. Except as may be specifically provided otherwise in the Contract or approved in advance by Fort Bend County, the Contractor shall provide Fort Bend County with copies of material testing reports and to cause all materials, equipment, and fabricated items incorporated in the Project to be new and of a suitable grade of their respective kinds for their intended use.
- 14.15 <u>Delay, Disruption or Hindrance Damages</u>. Contractor and the County contemplate that Contractor's performance may be delayed, disrupted or interfered with by unanticipated causes including but not limited to the following:
 - a) Severe and unavoidable natural disasters such as fires, floods, epidemics and earthquakes;
 - b) Abnormal weather conditions;
 - c) Acts or failures to act of the County, third party utility owners or other third party entities; and
 - d) Acts of war or terrorism.

Contractor and the County agree and stipulate that an extension of the Contract Time shall be the sole remedy of Contractor for delays in performance of the Work, whether or not such delays are foreseeable, except for delays caused solely by acts of the County that constitute fraud, intentional misrepresentation, gross negligence, intentional arbitrary or capricious acts and/or omissions or intentional interference with Contractor's performance of the Work and then only to the extent such acts continue after Contractor notifies Owner in writing of such conduct. For delays caused by any act(s) other than fraud, intentional misrepresentation, gross negligence, intentional arbitrary or capricious acts and/or omissions or intentional interference with Contractor's performance of the Work Contractor shall not be entitled to any compensation or recovery of any damages including, without limitation, those damages prohibited or limited in Sections 14.15.1 – 14.15.8 below. The County's exercise of any of its rights or remedies under the Contract including, without limitation, ordering changes in the Work or directing suspension, rescheduling, or correction of the Work, in response to any breach or failure by the Contractor to comply with the terms of the Contract Documents or the Contractor's obligations arising therefrom, shall not be construed as intentional interference with Contractor's performance of the Work regardless of the extent or frequency of the County's exercise of such rights or remedies.

Without limiting the foregoing, except as otherwise expressly provided in this Agreement in calculating the amount of any claim recoverable by Contractor, the following limitations on the recovery of damages shall apply:

14.15.1 No indirect or consequential damages will be allowed.

- 14.15.2 No recovery shall be based on a comparison of planned expenditures to total actual expenditures, or on estimated losses of labor efficiency, or on a comparison of planned manloading to actual manloading, or any other analysis that is used to show damages indirectly.
- 14.15.3 Damages, to the extent recoverable, are limited to the additional, actual costs specifically shown to have been directly incurred by the Contractor and solely caused by the proven wrong.
- 14.15.4 No damages will be allowed for home office overhead or other home office charges.
- 14.15.5 No exemplary damages or unjust enrichment damages shall be recoverable.
- 14.15.6 No recovery of attorney's fees shall be recoverable except as expressly permitted under the Agreement.
- 14.15.7 No profit will be allowed on any damage claim, except as expressly recoverable under the Agreement as Fee on Cost of the Work incurred.
- 14.15.8 Notwithstanding any other damage limitation herein the County and the Contractor recognize the delays, expense, and difficulties involved in proving in a legal or arbitration proceeding the actual loss suffered by the Contractor if the County is found to have intentionally interfered with Contractor's performance of the Work by fraud, misrepresentation, gross negligence, or intentional arbitrary or capricious acts and/or omissions. Accordingly, instead of requiring any such proof, the County and the Contractor agree that as liquidated damages (in lieu of any other remedy or damages) for delay, disruption or hindrance (but not as a penalty) the County shall pay the Contractor \$250.00 for each day that a court of competent jurisdiction finds the County's conduct referenced in Section 14.15 (above) is the sole cause of Contractor's delay in completing the Work.

15.0 TERMINATION:

- 15.1 Fort Bend County may terminate the Contract for cause if the Contractor:
 - 15.1.1 Persistently or repeatedly refuses or fails to supply enough properly skilled workers or proper materials.
 - 15.1.2 Fails to make payment to Subcontractors for materials or labor in accordance with the respective agreements between the Contractor and the Subcontractor.

- 15.1.3 Persistently disregards laws, ordinances, or rules, regulations or orders of a public authority having jurisdiction.
- 15.1.4 Otherwise commits substantial breach of a provision of the Contract Documents.
- When any of the above reasons exists, Fort Bend County may, without prejudice to any other rights or remedies of Fort Bend County and after giving the Contractor and the Contractor's surety, if any, seven days' written notice, terminate employment of the Contractor and may, subject to any prior rights of the surety:
 - 15.2.1 Take possession of the site and of all materials, equipment, tools, and construction equipment and machinery thereon owned by the Contractor.
 - 15.2.2 Finish the Project by whatever reasonable method Fort Bend County may deem expedient.
 - 15.2.3 When Fort Bend County terminates the Contract for one of the reasons stated in this section, the Contractor shall not be entitled to receive further payment until the Project is finished. Therefore, the Contractor shall be promptly paid for all work actually and satisfactorily completed.
- 15.3 Termination for Convenience of Fort Bend County

Fort Bend county reserves the right, without breach, to terminate the Contract prior to, or during the performance of the Work, for any reason. Upon such an occurrence, the following shall apply.

- 15.3.1 The County will notify Contractor in writing of the county's determination to terminate the contract for convenience and the effective date of the Contract termination. The notice may also contain instructions necessary for the protection, storage or decommissioning of incomplete work or systems, and for safety.
- 15.3.2 Upon receipt of the notice of termination, Contractor shall immediately proceed with the following obligations, regardless of any dispute in determining or adjusting any amounts due at that point in the Contract:
 - 15.3.2.1 Stop all work.
 - 15.3.2.2 Place no further subcontracts or orders for materials or services.
 - 15.3.2.3 Terminate all subcontracts for convenience.
 - 15.3.2.4 Cancel all materials and equipment orders as applicable.

- 15.3.2.5 Take appropriate action that is necessary to protect and preserve all property related to the Contract which is in the possession of Contractor.
- 15.3.2.6 When the Contract is terminated for Owner's convenience, Contractor may recover from Owner payment for all Work executed. Contractor may not claim lost profits or lost business opportunities.
- 15.4 <u>Settlement on Termination.</u> When the Contract is terminated by the County under 15.3, at any time prior to one hundred eighty (180) days after the effective date of termination, Contractor shall submit a final termination settlement proposal to the County based upon recoverable costs as provided under the Contract. If Contractor fails to submit the proposal within the time allowed, the County may unilaterally determine the amount due to Contractor because of the termination and pay the determined amount to Contractor.

16.0 COMPLETION, TRANSFER, & ACCEPTANCE:

- 16.1 <u>Final Completion</u>. Upon the occurrence of the final completion date, the punch list items shall be promptly commenced and thereafter completed within thirty (30) days after final completion.
- 16.2 <u>Transfer and Acceptance</u>. Upon the occurrence of final completion, care, custody and control of the Project shall pass to Fort Bend County. As referenced herein, the "<u>Transfer Date</u>" shall mean the date on which the care, custody and control of the Project passes to Fort Bend County. Subsequent to the Transfer Date all risk of loss with respect to the Project shall be by Fort Bend County and the Contractor shall be thereafter obligated to cover the Project with their Insurance.

17.0 SUSPENSION BY FORT BEND COUNTY FOR CONVENIENCE:

- 17.1 Fort Bend County may, without cause, order the Contractor in writing to suspend, delay or interrupt the Project in whole or in part for such period of time as Fort Bend County may determine.
- 17.2 An adjustment shall be made for increase in the cost of performance, caused by suspension, delay or interruption. No adjustment shall be made to the extent:
 - 17.2.1 That performance is, was or would have been so suspended, delayed or interrupted by another cause for which the Contractor is responsible.
 - 17.2.2 That an equitable adjustment is made or denied under another provision of this Contract.

17.3 Adjustments made in the cost of performance may have a mutually agreed fixed or percentage fee.

18.0 INDEPENDENT CONTRACTOR:

The Contractor shall be an independent contractor and any provisions of this Contract that may appear to give Fort Bend County the right to direct the Contractor as to the details of the manner of doing the Project shall be deemed to mean that the Contractor shall follow the desires of Fort Bend County in the results of the Project only and not in the means whereby the Project is to be accomplished. The Contractor shall be responsible as to the details of completing the Project. Neither the agents, representatives, nor employees of the Contractor, shall be deemed to be the agents, representatives, or employees of Fort Bend County. The Contractor further represents that it accepts a fiduciary role and responsibility with respect to Fort Bend County and will, to its best abilities, act in the best interests of Fort Bend County and the timely completion of the Project. The Contractor agrees and understands that neither it nor any of its agents or employees may act in the name of Fort Bend County except and unless specifically authorized in writing by Fort Bend County to do so. The Contractor shall furnish construction administration and management services and use the Contractor's best efforts to complete the Project in an expeditious and economical manner consistent with the interests of Fort Bend County.

19.0 NOTICE

- 19.1 All written notices, demands, and other papers or documents to be delivered to Fort Bend County under this Contract shall be delivered to the Parks Department, 301 Jackson, Richmond, Texas 77469, or at such other place or places as Fort Bend County may from time to time designate by written notice delivered to the Contractor. For purposes of notice under this Contract, a copy of any notice or communication hereunder shall also be forwarded to the following address: Fort Bend County, 301 Jackson Street, Richmond, Texas 77469, Attention: County Judge.
- 19.2 All written notices, demands, and other papers or documents to be delivered to the Contractor under this Contract shall be delivered to the Authorized Representative identified in the Contract documents or such other place or places as the Contractor may designate by written notice delivered to Fort Bend County.

20.0 RECORDS:

- 20.1 Fort Bend County shall be the absolute and unqualified owner of all drawings, preliminary layouts, record drawings, sketches and other documents prepared pursuant to the Contract by Contractor.
- 20.2 The Contractor agrees to maintain and preserve for a period of at least five years after the earlier of the expiration of the defects period or termination of this Contract, accurate and complete records relating to the performance of the

Project. The Contractor agrees to, upon request, provide Fort Bend County with such records.

SUCCESSORS & ASSIGNS: 21.0

- Fort Bend County and the Contractor bind themselves and their successors, executors, administrators and assigns to the other party of this Contract and to the successors, executors, administrators and assigns of such other party, in respect to all covenants of this Contract.
- Neither Fort Bend County nor the Contractor shall assign, sublet or transfer its 21.2 interest in this Contract without the prior written consent of the other.
- Nothing herein shall be construed as creating any personal liability on the part of 21.3 any officer or agent of any public and/or governmental body that may be a party hereto.

22.0 **PUBLIC CONTACT:**

Contact with the news media, citizens of Fort Bend County or governmental agencies shall be the sole responsibility of Fort Bend County. Under no circumstances, whatsoever, shall Contractor release any material or information developed in the performance of its services hereunder without the express written permission of Fort Bend County, except where required to do so by law.

23.0 **MODIFICATIONS:**

This instrument contains the entire Contract between the parties relating to the rights herein granted and obligations herein assumed. Any oral or written representations or modifications concerning this instrument shall be of no force and effect excepting a subsequent written modification signed by both parties hereto.

24.0 SILENCE OF SPECIFICATIONS:

The apparent silence of specifications as to any detail, or the apparent omission from it of a detailed description concerning any point, shall be regarded as meaning that only the best commercial practice is to prevail and that only material and workmanship of the finest quality are to be used. All interpretations of specifications shall be made on the basis of this statement. The items furnished under this contract shall be new, unused of the latest product in production to commercial trade and shall be of the highest quality as to materials used and workmanship. Manufacturer furnishing these items shall be experienced in design and construction of such items and shall be an established supplier of the item bid.

SEVERABILITY: 25.0

In the event one or more of the provisions contained in these requirements or the specifications shall for any reason be held to be invalid, illegal or unenforceable in any respect, such invalidity, Initials of Bidder:

illegality, or unenforceability shall not affect any other provision hereof and these requirements or the specifications shall be construed as if such invalid, illegal, or unenforceable provision had never been contained herein.

26.0 GOVERNING FORMS:

In the event of any conflict between the terms and provisions of these requirements and the specifications, the specifications shall govern. In the event of any conflict of interpretation of any part of this overall document, Fort Bend County's interpretation shall govern.

27.0 TAX EXEMPT:

Fort Bend County is exempt from state and local sales and use taxes under Section 151.309 of the Texas Tax Code. This Contract is deemed to be a separate contract for Texas tax purposes, and as such, Fort Bend County hereby issues its Texas Exemption for the purchase of any items qualifying for exemption under this Contract. Contractor is to issue its Texas Resale Certificate to vendors and subcontractors for such items qualifying for this exemption, and further, contractor should state these items at cost.

28.0 ENTIRE AGREEMENT:

The Parties agree that this Contract contains all of the terms and conditions of the understanding of the parties relating to the subject matter hereof. All prior negotiations, discussions, correspondence and preliminary understandings between the parties and others relating hereto are superseded by this Contract. By entering into this Contract, the parties do not intend to create any obligations, express or implied, other than those specifically set out in this Contract.

29.0 APPLICABLE LAW & VENUE

This Contract shall be construed under and in accord with the laws of the State of Texas, and all obligations of the parties created hereunder are performable in Fort Bend County, Texas, and that venue for any litigation arising out of or related to this Contract shall lie solely in the court of appropriate jurisdiction located in Fort Bend County, Texas.

30.0 AWARD:

This contract will be awarded to the overall lowest and best bid.

31.0 TEXAS ETHICS COMMISSION FORM 1295:

31.1 Effective January 1, 2016 all contracts executed by Commissioners Court, regardless of the dollar amount, will require completion of Form 1295 "Certificate of Interested Parties", per the new Government Code Statute §2252.908. All vendors submitting a response to a formal Bid, RFP, SOQ or any contracts, contract amendments, renewals or change orders are required to complete the Form 1295 online through the State of Texas Ethics Commission website. Please

visit: https://www.ethics.state.tx.us/filinginfo/1295/

31.2 On-line instructions:

- 31.2.1 Name of governmental entity is to read: Fort Bend County.
- 31.2.2 Identification number used by the governmental entity is: <u>B24-059</u>.
- 31.2.3 Description is the title of the solicitation: <u>African American Memorial</u> Phase One.
- 31.3 Apparent low bidder(s) will be required to provide the Form 1295 within three (3) calendar days from notification; however, if your company is publicly traded you are not required to complete this form.

32.0 STATE LAW REQUIREMENTS FOR CONTRACTS:

The contents of this section are required by Texas Law and are included by County regardless of content.

- 32.1 Agreement to Not Boycott Israel Chapter 2271 Texas Government Code: Contractor verifies that if Contractor employs ten (10) or more full-time employees and this Agreement has a value of \$100,000 or more, Contractor does not boycott Israel and will not boycott Israel during the term of this Agreement.
- 32.2 Texas Government Code Section 2251.152 Acknowledgment: By signature on vendor form, Contractor represents pursuant to Section 2252.152 of the Texas Government Code, that Contractor is not listed on the website of the Comptroller of the State of Texas concerning the listing of companies that are identified under Section 806.051, Section 807.051 or Section 2253.153.

33.0 HUMAN TRAFFICKING:

By acceptance of this contract, Contractor acknowledges that Fort Bend County is opposed to human trafficking and that no County funds will be used in support of services or activities that violate human trafficking laws

34.0 INDEMNITY FOR BODILY INJURY OR DEATH CLAIMS

Indemnity for certain bodily injury or death claims. To the fullest extent permitted by law, contractor shall indemnify, defend and hold harmless the county from and against all claims, losses, expenses, costs, demands, suits, causes of action, and damages, including without limitation, attorneys' fees and expenses, for bodily injury or death of any employee of contractor, its agents, or its subcontractors of every tier, even if the bodily injury or death is caused by or alleged to have been caused by the sole or partial negligence, fault or strict liability of any indemnitee.

Indemnity for all other claims. For all claims not addressed in the preceding section or section 11.0 above, including, without limitation, claims for damage to or loss of use of property and claims for bodily injury to or death of any person other than that addressed in the immediately preceding section, to the fullest extent permitted by law, contractor shall indemnify, defend and hold harmless the county from and against all claims, losses, expenses, costs, demands, suits, causes of action, and damages, including without limitation, attorneys' fees and expenses, of any nature whatsoever arising out of or related to this contract or the work to be performed under this contract, but only to the extent of the negligence or other fault of the contractor, its agents, representatives, employees or subcontractors of any tier.

35.0 AGREEMENT TO ARBITRATE UNDER THE FEDERAL ARBITRATION ACT

To the maximum extent allowed by law, any controversy or claim arising out of or relating to this contract, or the breach thereof, shall be settled by arbitration under the Federal Arbitration Act, 9 U.S.C. § 1, et seq. administered by the American Arbitration Association under its Construction Industry Arbitration Rules, and judgment on the award rendered by the arbitrator(s) may be entered in any court having jurisdiction thereof. For cases in which the amount in controversy is less than \$250,000, there shall be no discovery other than an expeditious and complete exchange of documents relative to the dispute. For cases in which the amount in controversy is between \$250,000 and \$1,000,000, there shall be no discovery except for an expeditious and complete exchange of such documentary information and up to three (3) depositions per side (including expert depositions, if any). For cases in which the amount in controversy exceeds \$1,000,000, there shall be no discovery except for an expeditious and complete exchange of such documentary information up to five (5) depositions per side (including expert depositions, if any). No formal interrogatories, request for admissions or formal request for production of documents shall be allowed in the arbitration process. The hearing on the merits will be completed no later than ninety (90) days after the initial demand for arbitration is made for disputes involving amounts in controversy of up to \$250,000; no later than no later than one hundred twenty (120) days after the initial demand for arbitration is made for disputes involving amounts in controversy of between \$250,000 and \$1,000,000; and, no later than three hundred sixty five (365) days after the initial demand for arbitration is made for disputes involving amounts in controversy of over \$1,000,000.

36.0 ADDITIONAL REQUIRED FORMS:

All vendors submitting are required to complete and return with submission

- 36.1 Required Proof of Insurance
- 36.2 Vendor Form
- 36.3 W9 Form
- 36.4 Tax Form/Debt/Residence Certification
- 36.5 Contractor Acknowledgement of Stormwater Management Program

Fort Bend County Bid 24-059

36.6 Excel Pricing Sheet

37.0 EXHIBIT:

Exhibit I: Project Manual

Exhibit II: Plans

COUNTY PURCHASING AGENT

Fort Bend County, Texas



(281) 341-8640 Fax (281) 341-8645

May 13, 2024

TO: All Prospective Bidders

RE: Addendum No. 1 – Fort Bend County BID 24-059 – Construction of African American Memorial Phase One for Fort Bend County

Addendum 1:

Attached is addendum 1. Vendors are to utilize Addendum 1 document while preparing their solicitation response. Changes include Q&A#1, Geotechnical report, and GFRC Specifications Provided by Architect.

Immediately upon your receipt of this addendum, please fill out the following information and email this page to Tyler Kendziora at tyler.kendziora@fortbendcountytx.gov

SpawGlass Civil Construction, Inc.

Company Name

Signature of person receiving addendum

5/15/2024 Date

If you have any questions, please contact this office.

Sincerely,

Tyler Kendziora Senior Buyer

Tyler Kendziora

COUNTY PURCHASING AGENT

Fort Bend County, Texas



(281) 341-8640 Fax (281) 341-8645

May 16, 2024

TO: All Prospective Bidders

RE: Addendum No. 2 – Fort Bend County BID 24-059 – Construction of African American Memorial Phase One for Fort Bend County

Addendum 2:

Attached is addendum 2. Vendors are to utilize Addendum 2 document while preparing their solicitation response. Changes include Q&A #2, Spec Section 01 40 00, and Updated B24-059 Pricing Form. Provided by Architect.

Immediately upon your receipt of this addendum, please fill out the following information and email this page to Tyler Kendziora at tyler.kendziora@fortbendcountytx.gov

SpawGlass Civil Construction, Inc.

Company Name

Robin Falks 5/17/2024

Signature of person receiving addendum

Date

If you have any questions, please contact this office.

Sincerely,

Tyler Kendziora Senior Buyer

Tyler Kendziora

Contract Sheet Bid 24-059

THE STATE OF TEXAS COUNTY OF FORT BEND

This memorandum of agreement m	ade and entered into or	the 11 day of	June	, 20_24
by and between Fort Bend County	in the State of Texas	(hereinafter designa	ited County), act	ing herein by
County Judge KP George, by				
SpawGlass Civil Construc				
(company nan	ne)			
WITNESSETH:		•		
The Contractor and the County agree	that the bid and specifi	cations for the Const	truction of Afric	an American
Memorial Phase One which are here				
(when required) shall constitute the fu				
and described; the County agrees to pa				
It is further agreed that this contract s	hall not become binding	or effective until sign	ned by the parties	hereto and a
purchase order authorizing the items de		•		,
Executed at Richmond, Texas this	11day of	June		20_24
			Fort Bend C	ounty, Texas
	By: KPGCO	79L		
	By: M Atal	lin-	County Judge	, KP George
	· \/ \/ \/ \	JW 5	Signature o	f Contractor
	By: Weston Voss	s, President		
			Printed Nat	me and Title

(Rev. October 2018) Department of the Treasury

Request for Taxpayer Identification Number and Certification

Give Form to the requester. Do not send to the IRS.

► Go to www.irs.gov/FormW9 for instructions and the latest information

micma	Tievenide dervice	iotractions and the late	ot initorina								
	1 Name (as shown on your income tax return). Name is required on this line;	do not leave this line blank.									
	SpawGlass Civil Construction, Inc.										
	2 Business name/disregarded entity name, if different from above										
Print or type. Specific Instructions on page 3.								Exemptions (codes apply only to certain entities, not individuals; see instructions on page 3): Exempt payee code (if any) 5			
Print o	LLC if the LLC is classified as a single-member LLC that is disregarded another LLC that is not disregarded from the owner for U.S. federal tax is disregarded from the owner should check the appropriate box for the	from the owner unless the opurposes. Otherwise, a sing	wner of the l le-member L	LLC is	od nat	Exemption from FATCA reporting code (if any) N/A					
ě	Under (see instructions) ▶						ounts mail		outside	the U.S.)	
See S	5 Address (number, street, and apt. or suite no.) See instructions. 13800 West Road		Requester's	s nam	e and a	aaress	(option	iai)			
0)	6 City, state, and ZIP code Houston, TX 77041										
	7 List account number(s) here (optional)										
	Tarana I da A'Ca A' an Nama Lan (TINI)										
Par											
	your TIN in the appropriate box. The TIN provided must match the na		U.G.	ciai s	security	numi	er	_			
	o withholding. For individuals, this is generally your social security not alien, sole proprietor, or disregarded entity, see the instructions fo		ora				_	_1			
	s, it is your employer identification number (EIN). If you do not have a		ta L_								
TIN, la	ter.		or								
	If the account is in more than one name, see the instructions for line	1. Also see What Name a	and Er	nploy	er iden	tificati	on num	ber			
Numb	er To Give the Requester for guidelines on whose number to enter.		7				0 7			-	
			7	6	- o	4	9 7	2	0	5	
Part	II Certification										
Under	penalties of perjury, I certify that:										
2. I am Sen	number shown on this form is my correct taxpayer identification nur not subject to backup withholding because: (a) I am exempt from b rice (IRS) that I am subject to backup withholding as a result of a fail onger subject to backup withholding; and	ackup withholding, or (b)	I have not	been	notifie	d by	the Inte				
3. I am	a U.S. citizen or other U.S. person (defined below); and										
4. The	FATCA code(s) entered on this form (if any) indicating that I am exer	npt from FATCA reportin	g is correct								
you ha acquis	cation instructions. You must cross out item 2 above if you have been we failed to report all interest and dividends on your tax return. For real of tion or abandonment of secured property, cancellation of debt, contribu	estate transactions, item 2 utions to an individual retire	does not ap ement arran	oply. igeme	For mo	rtgag), and	e intere genera	st pa ally, p	id, ayme	ents	
Sign Here	Signature of U.S. person > Bethand Tainer		Date ►	01/0	1/2024						
Ger	neral Instructions	Form 1099-DIV (div funds)	vidends, inc	cludir	ng thos	e fron	n stocl	ks or	mutu	ıal	
Sectio	n references are to the Internal Revenue Code unless otherwise	• Form 1099-MISC (various tvp	es of	incom	e, pri	zes, av	/ards	, or c	ross	

noted.

Future developments. For the latest information about developments related to Form W-9 and its instructions, such as legislation enacted after they were published, go to www.irs.gov/FormW9.

Purpose of Form

An individual or entity (Form W-9 requester) who is required to file an information return with the IRS must obtain your correct taxpayer identification number (TIN) which may be your social security number (SSN), individual taxpayer identification number (ITIN), adoption taxpayer identification number (ATIN), or employer identification number (EIN), to report on an information return the amount paid to you, or other amount reportable on an information return. Examples of information returns include, but are not limited to, the following.

• Form 1099-INT (interest earned or paid)

- proceeds)
- Form 1099-B (stock or mutual fund sales and certain other transactions by brokers)
- Form 1099-S (proceeds from real estate transactions)
- Form 1099-K (merchant card and third party network transactions)
- Form 1098 (home mortgage interest), 1098-E (student loan interest), 1098-T (tuition)
- · Form 1099-C (canceled debt)
- Form 1099-A (acquisition or abandonment of secured property)

Use Form W-9 only if you are a U.S. person (including a resident alien), to provide your correct TIN.

If you do not return Form W-9 to the requester with a TIN, you might be subject to backup withholding. See What is backup withholding,

Job No.:

TAX FORM/DEBT/ RESIDENCE CERTIFICATION

(for Advertised Projects)

Тахра	yer Ide	ntification Num	ber (T.I.N.):	76-0497205						
		me submitting E			Civil Const	truction, In	C.			
	ng Addr	12000 1/		Houston, TX						
	U	tered to do busi	ness in the St	ate of Texas?	Yes	No				
		individual, list the e(s) under which			ny partners	hip of whic	h you are a	general pa	rtner or any	
I.	name	erty: List all ta ss. Include real a ssary.)								
Fort B	end Co	ounty Tax Acct.	No.*	Property address	ss or locati	on**				
	14//									
	y be sto Fort	here the proper ored at a warehout Es, fines, tolls, co	ouse or other Debt - Do you	location. I owe any debts						
	Y	res No	If yes, att	ach a separate p	age explair	ning the del	ot.			
III.	reque	lence Certificatests Residence C	Certification.	§2252.001 et s	seq. of the	Governme	nt Code pr	ovides som		
	(3)	"Nonresident b	idder" refers t	to a person who	is not a res	ident.				
	(4)			a person whose parent compan						
			awGlass Civil [Compar	Construction, Inc. ny Name]	is a Reside	nt Bidder o	f Texas as d	efined in C	Government Co	ode
		§2252.001.			· N'	:1a D:11		1:		
				y Name]			er as defined	ı in Goverr	iment Code	
		§2252.001 and	our principal	place of busines	SS 1S	[City	and State]	······································		



Contractor Acknowledgement of Storm Water Management Program

I hereby acknowledge that I am aware of the stormwater management program and standard operating procedures developed by Fort Bend County in compliance with the TPDES General Permit No. TXR040000. I agree to comply with all applicable best management practices and standard operating procedures while conducting my services for Fort Bend County. I agree to conduct all services in a manner that does not introduce illicit discharges of pollutants to streets, stormwater inlets, drainage ditches or any portion of the drainage system. The following materials and/or pollutant sources must not be discharged to the drainage system as a result of any services provided:

- 1. Grass clippings, leaves, mulch, rocks, sand, dirt or other waste materials resulting from landscaping activities, (except those materials resulting from ditch mowing or maintenance activities)
- 2. Herbicides, pesticides and/or fertilizers, (except those intended for aquatic use)
- 3. Detergents, fuels, solvents, oils and/or lubricants, other equipment and/or vehicle fluids,
- 4. Other hazardous materials including paints, thinners, chemicals or related waste materials,
- 5. Uncontrolled dewatering discharges, equipment and/or vehicle wash waters,
- 6. Sanitary waste, trash, debris, or other waste products
- 7. Wastewater from wet saw machinery,
- 8. Other pollutants that degrade water quality or pose a threat to human health or the environment.


Furthermore, I agree to notify Fort Bend County immediately of any issue caused by or identified by:

SpawGlass Civil Construction, Inc.

(Company/Contractor)

that is believed to be an immediate threat to human health or the environment.

Weston Voss	Digitally signed by Weston Voss Date: 2024.05.15 14:40:30 -05'00'	5/21/2024
Contractor Signature	Date	
Wes	ton Voss	
Printed Name		
Pr	esident	
Title		

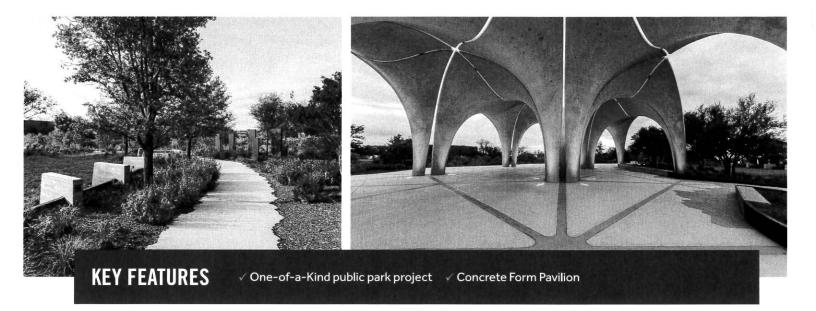

CONSTRUCTION COST Final \$ 8,909,771

OWNER

San Antonio River Foundation/Parkwerks, LLC Stuart Allen 210-370-7005


ARCHITECT Lake Flato Architects Tenna Florian 210-679-2334

CONFLUENCE PARK

SAN ANTONIO, TEXAS


Located along the San Antonio River, this public park includes a primary pavilion constructed of large concrete forms that collect and funnel rainwater, a multipurpose space with a green roof providing thermal mass for passive heating and cooling, restroom facilities, a site-wide water catchment system to collect rainwater into an underground water storage tank, play areas, and satellite pavilions that mirror the form of the primary pavilion.

To preserve the terrain, SpawGlass installed more than 200 COR-TEN steel retaining walls throughout the site. The weathered steel walls were key to the grading and landscape footprint of the site. They protect the new elevations and help add layers to the plant displays. Two-tiered retaining walls along the pathways were designed for a close-up experience, allowing children to touch and feel the native grasses and flowers. Planned as a net-zero energy project, the park features a photovoltaic array that provides 100-percent of its energy on an annual basis.

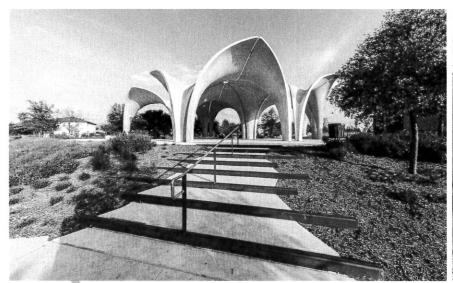





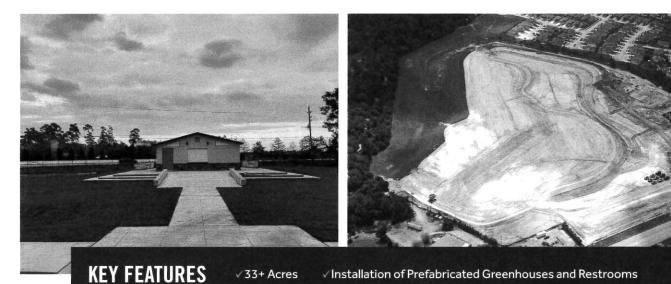

CONSTRUCTION COST FOR DRAINAGE IMPROVEMENTS \$3,024,013

CONSTRUCTION COST FOR PREFAB RESTROOM IMPROVEMENTS \$873,889

OWNER
Harris County
Terry Jones
(713) 274-3647
Terry.Jones@eng.hctx.net

ARCHITECT
Halff Associates, Inc.
Jerry Tipps
(713) 380-4393
jtipps@halff.com


DRAINAGE IMPROVEMENTS FOR MERCER BOTANIC GARDENS & PREFABRICATED RESTROOM IMPROVEMENTS

HUMBLE, TEXAS

We recently completed two projects for Harris County at Mercer Botanic Gardens. The first project consisted of improvements to a 33+ acre parcel at the Botanic Gardens. The work included the clearing of the entire site, excavation of a detention pond, and using 149,000-CY of excavated material as fill for the site. Additional work included 786-SY of slope paving, construction of a parking lot including 3,784-SY of concrete paving, 1,143-LF of curb, 148-SY of sidewalk, and pavement markings and signage. A small storm drainage system was constructed consisting of 1,200-LF of HDPE, RCP, and CMP pipe with 10 inlets and one manhole.

A major component of the project was the fabrication and installation of two greenhouse structures complete with all lime-stabilized/select fill building pads, concrete foundations, plumbing, electrical, lighting, and control systems. A small metered water service and a sanitary service were installed for a future welcome center. SWPP measures and hydroseed grass establishment were included in the contract work. Lastly, two existing greenhouses were demolished and removed from the existing botanic gardens facility.

The second project consisted of the installation of a prefabricated flood-resistant restroom in a less flood-prone zone. In addition, the project requires installed water, sanitary and electrical lines, a lift station, and a parking lot. The work including the construction, delivery, and complete installation of an Americans with Disabilities Act (ADA) accessible prefabricated restroom building, building foundation, site preparation, demolition, flatwork, parking, grading, drainage, and utility infrastructure.

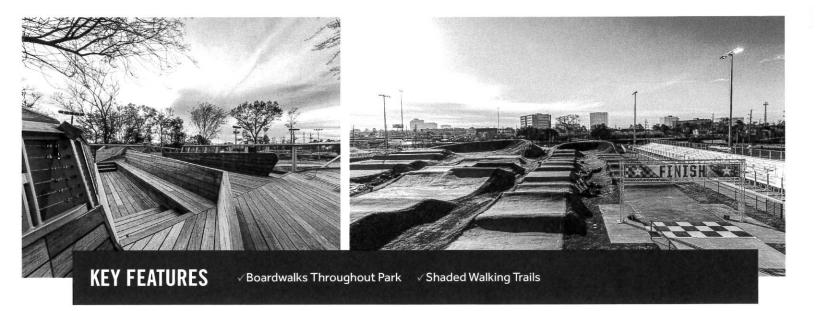

CONSTRUCTION COST \$19,880,965

OWNER North Houston Development Corporation Sally Bradford

(281) 877-9952 sbradford@greenspoint.org

ARCHITECT Jones|Carter Martin Murdock (713) 777-5337 mmurdock@jonescarter.com

ROCKSTAR ENERGY BIKE PARK

HOUSTON, TEXAS

The 20-acre Rockstar Energy Bike Park is full of twists and turns to entice bike riders of all skill levels, including a world-class, competition-level BMX track with grandstand seating for 3,500 spectators. Other structures for both adults and kids include bowls, pump tracks and a street plaza with stairs and rails. There also are plenty of shaded biking and walking trails as well as seating areas to relax, unwind and enjoy the outdoors. Other park amenities include an amphitheater for concerts and other special events as well as a community center.





BASE BID AND ALTERNATE ITEMS (Installed Complete) Addendum No. 2 BIDDER TO COMPLETE LINE ITEM FORM

PART 1 - Unit Prices

T 1 - Unit Prices				
UNIT PRICES	or many provi	no and wa	athere are enough to the large	
Base Bid Items PHASE 1	Qty.	Unit	Unit Cost	Extension
. General Conditions				
1 , Mobilization	1	LS	\$_1,362,023.55 \$_	1,362,023.5
2. Performance and Payment Bonds (For cost of bonds only, no markup)	1	LS	\$\$\$\$	77,737.90
3. Maintenance Bonds (For cost of bonds only, no markup)	1	LS	\$10,000.00 \$	10,000.00
4 . 60 Day Landscape Maintenance	1	LS	\$\$,156.00 \$	5,156.00
5 , Permits & Surveying	1	LS	\$ 96,391.56 \$	96,391.5
6. Tree Protection Fencing	1	LS	\$ 23,751.00 \$	23,751.00
7. Construction Fence around Gravesites	539	LF	\$ 17.63 \$	9,500.00
8	******		\$\$_	
. SWPPP Division V - Storm Water Pollution Control				
	1	EΛ	\$ 79.222.00 \$	78,232.00
Enforcement and Maintenance of TPDES Requirements for Duration of Contract Stabilized Construction Access.	1	EA	\$	
2 . Stabilized Construction Access	1	EA	5,390.00 \$	5,390.00
3 . Concrete Truck Washout Area	1	EA	4,345.00 \$_	4,345.00
		EA	\$\$\$_	1,732.50
5 . Reinforcement Filter Fabric Fence	3162	LF	\$\$	10,608.51
6			\$\$_	
. Civil				
<u>Division 1 - Site Preparation</u>				
Site Preparation: to remove trees, stumps, logs, vegetation, fences, rubbish, debris, organic matter and other objectionable material per the specifications (including debris) and the second state of t				
stripping existing topsoil; stockpiling topsoil; replacing topsoil over all disturbed areas	9.75	AC	\$16,705.67 \$	162,880.30
<u>Division IV - Storm Sewer System</u>				
		EA	\$	21,232.84
		EA	\$5,479.21_\$	32,875.24
3. Specialty Inlet	1	EA	\$ 4,808.21 \$	4,808.2
4. 6" Storm Pipe	264	LF	\$ 84.75 \$	22,374.07
5. 8" Storm Pipe	246	LF	\$ 93.23 \$	22,934.54
6. 12" Storm Pipe	312	LF	\$ 110.66 \$	34,525.24
		LF	\$ 396.81 \$	33,331.91
8 24" Storm Pipe	134	LF	\$ 237.69 \$	31,850.28
9. 24" RCP STORM	0	LF	\$ 0.00 \$	0.00
10 . French Drains	823	LF	\$ 86.81 \$	71,440.91
11 . 24" SET	1	EA	\$ 3,459.61 \$	3,459.6
12 . Culverts	0			
		EA	\$ 0.00 \$	0.00
13 . 24" Head Wall	1	EA	\$15,226.41 \$	15,226.4
14 . Trench Safety System 15 .	1138	LF	\$\$ \$ \$\$	1,251.80
			· · · · · · · · · · · · · · · · · · ·	
<u>Division VI - Paving Items</u>				
1 . Reinforced Concrete Curb	859	LF	\$\$	7,285.30
2. Handicap Parking - All Types, Complete / Compliant	2	EA	\$165.00 \$	330.00
3 . 4" White Parking Lot Stripping	760	LF	\$\$_	2,200.00
			\$\$\$	185,731.70
			\$_	44,323.40
Architecture	2000			
	1	LS	\$ 3,711,364.82 \$	3,711,364.82
1 . Monument (Re: 1/A203)				
1 . Monument (Re: 1/A203) 2 . Pedestrian Portal (Re: A401, A810) 3 .	3	EA	\$ 10,404.85 \$ \$	31,214.54

E.	Electrical			
	Electrical Meter Loop & Panel (Complete & In-Place)	LS	\$ 84,934.55 \$	84,934.55
	B1 - Low scale pathway bollard 35	EA	\$ 371.40 \$	12,999.14
3.	B2 - Pathway lantern 18	EA	\$ 371.40 \$	6,685.27
4.	B3 - Planting bed glowing bollard - 0	EA	\$ 0.00 \$	0.00
5.	B4 - Standard size bollard	EA	\$ 167.94 \$	1,679.37
6.	B5 - Low scale pathway bollard - 0	EA	\$ 0.00 \$	0.00
7.	L1 - Linear LED side mounted for Gabion Wall	LF	\$ 163.21 \$	140,521.23
	L2 - Linear LED mounted in pedestal 36	LF	\$\$	5,875.45
9.	L3 - Linear LED mounted in Pedestrian Portals 6	LF	\$148.37 \$	890.22
	. L4 - Linear in-grade uplight	LF	\$\$	21,053.70
	. L5 - Linear LED integrated in site furniture/walls 280	LF	\$\$	45,697.96
	. L6 - Linear LED integrated in signage	LF	\$163.21 \$	1,632.07
	. L7 - Linear ingrade LED wall washer	LF	\$163.21 \$	4,243.38
	.P1 - Parking lot pole 3	EA	\$1,980.29 \$	5,940.86
	. P2 - Temporary pole for Juneteenth Plaza	EA	\$\$	4,028.97
	. U1 - Stake mounted tree uplight	EA	\$197.38 \$	5,131.98
	. U2 - Stake mounted tree uplight	EA	\$\$	789.54
	. U3 - Adjustable LED ingrade 4	EA	\$ <u>197.38</u> \$	789.54
	. U4 - Stake mounted tree uplight w/ adj spike mount	EA	\$163.21_\$	1,468.86
	. US - Stake mounted uplight - 0	EA	\$\$	0.00
	· U6 - Point source floodlights @ bamboo garde n - 0	EA	\$\$	0.00
	. W1 - Wall recessed step light	EA	\$167.94 \$	1,679.37
	. Aerator Power Supply 0	LS	\$\$	0.00
24			\$\$	
F.	Fountain at Pond			
1.	Aerator Fountain (5 HP Disaply)	EA	\$\$	
2.	Subsurface Diffuser 0	EA	\$ \$	
3.	Fountain Manifold 0	EA	\$ \$	
4.	Airfeeder Pipe Tubing 0	LF	\$ \$	
5.	Control Panel & Compressor Cabinet 0	LS	\$ \$	
6.			\$\$	
7.		-	\$\$	
G.	Pedestrian Hardscape			
2.	Walks - Concrete, 4 1/2" Thick 9,693	SF	\$ 10.54 \$	102,137,38
2	Walks - Concrete, 4 1/2" Thick 9,693 Walks - Specialty Paving 'A' 6,577	SF SF	\$ 10.54 \$ \$ 14.18 \$	102,137.38 93,232.41
	Walks - Specialty Paving 'A' Walks - Specialty Paving 'B' 11,992	SF SF	\$ 14.18 \$ \$ 22.20 \$	93,232.41 266,177.13
4.	Walks - Specialty Paving 'A' Walks - Specialty Paving 'B' Walks - Specialty Paving 'B' Haunched Edge 561	SF SF LF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$	93,232.41 266,177.13 28,676.73
4. 5.	Walks - Specialty Paving 'A' Walks - Specialty Paving 'B' Walks - Specialty Paving 'B' Haunched Edge Walks - Specialty Paving 'C' 0	SF SF LF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$	93,232.41 266,177.13 28,676.73 0.00
4. 5. 6.	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670	SF SF LF SF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61
4. 5. 6. 7.	Walks - Specialty Paving 'A' Walks - Specialty Paving 'B' Walks - Specialty Paving 'B' Haunched Edge Walks - Specialty Paving 'C' 0	SF SF LF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$	93,232.41 266,177.13 28,676.73 0.00
4. 5. 6. 7. 8. 9.	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403	SF SF LF SF SF LF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 91.29 \$ \$ 120.46 \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00
4. 5. 6. 7. 8. 9.	Walks - Specialty Paving 'A' Walks - Specialty Paving 'B' Walks - Specialty Paving 'B' Haunched Edge Walks - Specialty Paving 'C' Walks - Specialty Paving 'C' Walks - Specialty Paving 'D' Walks - Specialty Paving 'E' Walks - Specialty Paving 'E' Walks - Specialty Paving 'E' Haunched Edge Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) Walks - Specialty Paving 'G' 104	SF SF SF SF SF LF SF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 91.29 \$ \$ 120.46 \$ \$ 491.45 \$ \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00
4. 5. 6. 7. 8. 9. 10	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'C' 104 12" Concrete Containment Curb 1,037	SF SF LF SF SF LF SF LF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 91.29 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40
4. 5. 6. 7. 8. 9. 10	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' Haunched Edge 1,811 Walks - Specialty Paving 'E' Hounched Edge 403 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242	SF SF SF SF LF SF LF LF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70
4. 5. 6. 7. 8. 9. 10 11. 12. 13.	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' Haunched Edge 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Iflush Concrete Band 242 Embedded Gravel Strip (Al Juneteenlh Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem-Plaza) 1,354	SF SF LF SF SF LF SF LF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ \$ 73.83 \$ \$ 17.78 \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10
4. 5. 6. 7. 8. 9. 10 11. 12. 13 14	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedom Plaza) 1,354 Gravel at Parking lot 124	SF SF LF SF SF LF SF LF SF SF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 91.29 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ 73.83 \$ \$ 17.78 \$ \$ 17.24 \$ \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30
4. 5. 6. 7. 8. 9. 10 11. 12. 13 14 15.	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem-Plaza) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3	SF SF SF SF LF SF LF SF SF LF SF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 120.46 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ 73.83 \$ \$ 17.78 \$ \$ 17.24 \$ \$ 36.30 \$ \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108.90
4. 5. 6. 7. 8. 9. 10 11. 12. 13. 14. 15. 16.	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' Haunched Edge 1,811 Walks - Specialty Paving 'E' Hounched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem Plaza) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447	SF SF LF SF SF LF SF SF LF LF SF SF LF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ \$ 73.83 \$ \$ 17.78 \$ 17.24 \$ 36.30 \$ \$ 22.00 \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108,90 9,834.00
4. 5. 6. 7. 8. 9. 10 11. 12. 13. 14. 15. 16. 17.	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem-Plaza) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3	SF SF SF SF LF SF LF SF SF LF SF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 120.46 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ 73.83 \$ \$ 17.78 \$ \$ 17.24 \$ \$ 36.30 \$ \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108.90
4. 5. 6. 7. 8. 9. 10 11 12 13 14 15 16 17 18	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' Haunched Edge 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gobions, Monument, & Freedem Plaze) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447 Steel Handrail & Cable Railing (with S.S.Cables) 57	SF SF LF SF SF LF SF LF LF SF SF LF LF SF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ \$ 73.83 \$ \$ 17.78 \$ \$ 17.24 \$ \$ 36.30 \$ \$ 22.00 \$ \$ 196.17 \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108.90 9,834.00 11,083.60
4. 5. 6. 7. 8. 99. 10 11 12 13 14 15 16 17 18 19 20 21	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'B' Haunched Edge 60 Walks - Specialty Paving 'C' 670 Walks - Specialty Paving 'B' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'C' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem Plaza) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447 Steel Handrail & Cable Railing (with S.S.Cables) 57 Adinkra Medallion, Type A1 1 Adinkra Medallion, Type B1 1	SF SF LF SF LF SF LF SF LF LF SF EA LF EA EA	\$ 14.18 \$ 22.20 \$ 51.12 \$ 0.00 \$ 193.68 \$ 44.89 \$ 120.46	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108.90 9,834.00 11,083.60 4,951.10 0.00 3,851.10
4. 5. 6. 7. 8. 8. 9. 10 11 12 13 13 14 15 16 17 18 19 20 21 22 2	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' Haunched Edge 1,811 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12' Concrete Containment Curb 1,037 12' Flush Concrete Band 242 Embedded Gravel Strip (At Junetenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem Plaza) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447 Steel Handrail & Cable Railing (with S.S.Cables) 57 Adinkra Medallion, Type A1 1 Adinkra Medallion, Type B1 1 Adinkra Medallion, Type B2 1	SF SF LF SF LF SF LF SF LF SF EA LF EA EA	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 91.29 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ 73.83 \$ 17.78 \$ 17.24 \$ 36.30 \$ \$ 22.00 \$ 196.17 \$ 4,951.10 \$ \$ 0.00 \$ \$ 3,851.10 \$ \$ 3.851.10 \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108.90 9,834.00 11,083.60 4,951.10 0.00 3,851.10 3,851.10
4. 5. 6. 7. 8. 9. 10 111 12 13 13 14 15 16 17 18 19 20 21 22 23	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' Haunched Edge 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem Plaza) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447 Steel Handrail & Cable Railing (with S.S.Cables) 57 Adinkra Medallion, Type A2 0 Adinkra Medallion, Type B1 1 Adinkra Medallion, Type B2 1 Adinkra Medallion, Type C1 0	SF SF LF SF LF SF SF LF SF SF LF SF EA A EA A EA	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ 73.83 \$ 17.78 \$ 17.24 \$ 36.30 \$ 22.00 \$ 196.17 \$ 4,951.10 \$ 0.00 \$ 3.851.10 \$ 3.851.10 \$ 3.851.10 \$ \$ 3.851.10 \$ \$ 3.851.10 \$ \$ 0.00 \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108,90 9,834.00 11,083.60 4,951.10 0.00 3,851.10 0.00
4. 5. 6. 7. 8. 9. 10 111 12 13 13 14 15 16 17 18 19 20 21 22 23	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem Plaza) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447 Steel Handrail & Cable Railing (with S.S.Cables) 57 Adinkra Medallion, Type A1 1 Adinkra Medallion, Type B1 1 Adinkra Medallion, Type B2 1 Adinkra Medallion, Type C2- 0 Adinkra Medallion, Type C2- 0	SF SF LF SF LF SF LF SF LF SF EA LF EA EA	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 91.29 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ 73.83 \$ 17.78 \$ 17.24 \$ 36.30 \$ \$ 22.00 \$ \$ 196.17 \$ \$ 4,951.10 \$ \$ 0.00 \$ \$ 3,851.10 \$ \$ 3.851.10 \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108.90 9,834.00 11,083.60 4,951.10 0.00 3,851.10 3,851.10
4. 5. 6. 7. 8. 9. 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'B' Haunched Edge 60 Walks - Specialty Paving 'C' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem Plaza) 1,354 Gravel Trough (At Gabions, Monument, & Freedem Plaza) 3 Bender Board, 1x12 447 Steel Handrail & Cable Railing (with S.S.Cables) 3 Adinkra Medallion, Type A1 1 Adinkra Medallion, Type B1 1 Adinkra Medallion, Type B2 1 Adinkra Medallion, Type C1 0 Adinkra Medallion, Type C2 0 Outdoor Classroom Only	SF SF LF SF LF SF LF SF LF LF SF EA LF EA EA EA EA	\$ 14.18 \$ 22.20 \$ 51.12 \$ 0.00 \$ 193.68 \$ 44.89 \$ 91.29 \$ 120.46 \$ 3 491.45 \$ 61.03 \$ 28.53 \$ 73.83 \$ 17.78 \$ 17.24 \$ 36.30 \$ 22.00 \$ 196.17 \$ 4.951.10 \$ 0.00 \$ 3.851.10 \$ 3.851.10 \$ 0.00 \$ 5 0.00 \$ 5	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108.90 9,834.00 11,083.60 4,951.10 0.00 3,851.10 0.00 0.00
4. 5. 6. 7. 8. 8. 9. 10 111 122 133 144 155 166. 17 188 199 200 21 222 233 244 255	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem Plaza) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447 Steel Handrail & Cable Railing (with S.S.Cables) 57 Adinkra Medallion, Type A1 1 Adinkra Medallion, Type B1 1 Adinkra Medallion, Type B2 1 Adinkra Medallion, Type C1 0 Adinkra Medallion, Type C2- 0 Outdoor Classroom Only Polished Concrete Wing Walls 90	SF SF LF SF LF SF LF SF LF SF LF LF SF EA LF LF A EA EA EA	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 91.29 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ 73.83 \$ 17.78 \$ 17.24 \$ 36.30 \$ \$ 22.00 \$ 196.17 \$ \$ 4.951.10 \$ \$ 0.00 \$ \$ 3.851.10 \$ \$ 3.851.10 \$ \$ 3.851.10 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108.90 9,834.00 11,083.60 4,951.10 0.00 3,851.10 0.00 0.00
4. 5. 6. 7. 8. 9. 10 111 12 13 144 155 166 17 18 19 20 21 22 23 24 25 26	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' Haunched Edge 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem Plaza) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447 Steel Handrail & Cable Railing (with S.S.Cables) 57 Adinkra Medallion, Type A1 1 Adinkra Medallion, Type B1 1 Adinkra Medallion, Type C1 0 Adinkra Medallion, Type C2 0 Outdoor Classroom Only Polished Concrete Wing Walls 90 Polished Steel Han	SF SF LF SF SF LF SF SF LF SF SF LF LF SF LF LF SF LF LF SF LF LF SF LF LF SF LF LF SF LF LF SF LF LF LF LF LF LF LF LF LF LF LF LF LF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ 73.83 \$ 17.78 \$ 17.24 \$ 36.30 \$ 22.00 \$ 196.17 \$ 4,951.10 \$ 3.8	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108,90 9,834.00 11,083.60 4,951.10 0.00 3,851.10 3,851.10 0.00 0.00
4. 5. 6. 7. 8. 8. 9. 10 111 12 13 144 155 166 17 18 19 20 21 22 23 24 25 26 27	Walks - Specialty Paving 'A' 6,577 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'C' 0 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Flush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem Plaza) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447 Steel Handrail & Cable Railing (with S.S.Cables) 57 Adinkra Medallion, Type A1 1 Adinkra Medallion, Type B1 1 Adinkra Medallion, Type B2 1 Adinkra Medallion, Type C1 0 Adinkra Medallion, Type C2- 0 Outdoor Classroom Only Polished Concrete Wing Walls 90	SF SF LF SF LF SF LF SF LF SF LF LF SF EA LF LF A EA EA EA	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 91.29 \$ \$ 120.46 \$ \$ 491.45 \$ \$ 61.03 \$ \$ 28.53 \$ 73.83 \$ 17.78 \$ 17.24 \$ 36.30 \$ \$ 22.00 \$ 196.17 \$ \$ 4.951.10 \$ \$ 0.00 \$ \$ 3.851.10 \$ \$ 3.851.10 \$ \$ 3.851.10 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108.90 9,834.00 11,083.60 4,951.10 0.00 3,851.10 0.00 0.00
4. 5. 6. 7. 8. 8. 9. 10 111 122 13 144 155 166 17 18 19 20 21 22 23 24 25 26 27 28	Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'B' Haunched Edge 670 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Hush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedom Plaze) 1,354 Gravel at Parking lot 124 2.4" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447 Steel Handrail & Getble Railing (with S.S.Cables) 57 Adinkra Medallion, Type A1 1 Adinkra Medallion, Type B1 1 Adinkra Medallion, Type B2 1 Adinkra Medallion, Type C2 0 Outdoor Classroom Only Polished Steel Handrail 90 Cast Bronze FB County Seal (At Wall) 1	SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF SF SF SF SF SF SF SF SF SF SF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 120.46 \$ \$ 491.45 \$ 61.03 \$ \$ 28.53 \$ \$ 17.78 \$ 17.24 \$ 36.30 \$ \$ 22.00 \$ \$ 196.17 \$ 4,951.10 \$ \$ 0.00 \$ \$ 3.851.10 \$ \$ 3.851.10 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$ 0.00 \$ \$	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 6,904.70 3,691.60 24,069.10 2,137.30 108.90 9,834.00 11,083.60 4,951.10 0.00 3,851.10 0.00 0.00 7,638.99 13,380.40 3,301.10
4. 5. 6. 7. 8. 9. 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29	Walks - Specialty Paving 'B' 11,992 Walks - Specialty Paving 'B' Haunched Edge 561 Walks - Specialty Paving 'B' Haunched Edge 670 Walks - Specialty Paving 'D' 670 Walks - Specialty Paving 'E' 1,811 Walks - Specialty Paving 'E' Haunched Edge 142 Walks - Specialty Paving 'F' (CLL Deck; Includes Concrete Base) 403 Walks - Specialty Paving 'G' 104 12" Concrete Containment Curb 1,037 12" Hush Concrete Band 242 Embedded Gravel Strip (At Juneteenth Lawn) 50 Gravel Trough (At Gabions, Monument, & Freedem Plaze) 1,354 Gravel at Parking lot 124 24" Bullrock ring (At Civil inlets in Planting Beds) 3 Bender Board, 1x12 447 Steel Handrail & -Cable Railing (with S.S.Cables) 57 Adinkra Medallion, Type A2 0 Adinkra Medallion, Type B1 1 Adinkra Medallion, Type B2 1 Adinkra Medallion, Type C1 0 Adinkra Medallion, Type C2 0 Adinkra Medallion, Type C3 0 Adinkra Medallion, Type C4 0 Adinkra Medal	SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF LF SF SF SF SF SF SF SF SF SF SF SF SF SF	\$ 14.18 \$ \$ 22.20 \$ \$ 51.12 \$ \$ 0.00 \$ \$ 193.68 \$ \$ 44.89 \$ \$ 120.46 \$ \$ 491.45 \$ 61.03 \$ \$ 28.53 \$ 73.83 \$ 17.78 \$ 17.24 \$ 36.30 \$ 22.00 \$ 196.17 \$ 4.951.10 \$ 0.00 \$ 3.851.10	93,232.41 266,177.13 28,676.73 0.00 129,765.61 81,297.46 12,962.53 48,545.00 51,111.00 63,287.40 24,069.10 21,37.30 108,90 9,834.00 11,083.60 4,951.10 0.00 3,851.10 3,851.10 0.00 0.00 7,638.99 13,380.40 3,301.10 5,501.10

	<u>Dedication Plaza Only</u>				
31	Cast Bronze FB County Seal (Paving)	ī	EA	\$ 11,001.10	\$ 11,001.10
	Pedestal, incl. Cast Stone	4	FA	\$ 42,266,27	\$ 169,065.07
OZ.	Walks - Donor Pavers (6x12, 60mm)	V-1	L) (Ψ	Ψ
33	Temporary use paver w/ Adinkra engraving	44	EA	\$ 89.38	\$ 3,932.50
	Replacement paver w/ name engraving (attic stock)	44	EA	\$ 62.98	\$ 2,770.90
	Walks - Donor Pavers (12x12, 60mm)			1	
35	Temporary use paver w/ Adinkra engraving	80	EA	\$ 178.75	\$ 14,300.00
36	Replacement paver w/ name engraving (attic stock)	80	EA	\$ 125.95	\$ 10,076.00
37	Walks - Donor Pavers, (12x12, 60mm) Permanent Paver w/ Adinkra engraving	12	EA	\$ 178.75	\$ 2,145.00
	Axis Memorial Only				
38	Wood Topper System @ Gabions	200	LF	\$166.89	\$33,378.00
	Lynching Monument Plaza Only				
39	Concrete Bulkhead	0	LF	\$	\$
40	lpe Wood Topped Concrete Seatwall	0	LF	\$	\$
41	Concrete Planter (Height Varies)	0	LF	\$	\$
40	Replica Art Piece Steel Support & Installation, (Includes coordination to receive Replica from			· ·	5 11
42	FB-County)	0	LS	\$	\$
43				\$	\$
44			NECOS ALTERNA	\$	\$
					•
Н.	Hardscape Walls: Gabion Walls				
1.	Gabion Walls @ Monument Plaza (Height Varies)	1	LS	\$ 917,601.90	\$ 917,601.90
2.	Gabion Walls @ CLL Axis Memorial (Height Varies)	1	LS	\$ 127,336.00	\$127,336.00
3.	Gabion Planter Walls @ Parking Lot	1	LS	\$ 79,767.88	\$ 79,767.88
4.	Signage @ Gabion Planter wall	1	EA	\$ 11,657.80	\$ 11,657.80
5.				\$	\$
6.			-	\$	\$
i	Site Furnishings				
	Landscape Forms Bench - 70" Backless (Ipe)	10	EA	\$ 2,226.00	\$ 22,260.00
	Landscape Forms Bench - 70" Backed (Ipe)	6	EA	\$ 3,159.72	\$ 18,958.32
	Landscape Forms Table - Charlie Picnic Table	0	EA	\$ 0.00	\$ 0.00
	Keystone Ridge Design Eve3-32 E-Everett 32 Gal Litter Receptacle	3	EA	\$ 5,476.36	\$ 16,429.08
	Concrete Base, Polished - Single	2	EA	\$ 11,992.38	\$ 23,984.76
	Concrete Base, Polished - Double	3	EA	\$ 15,204.26	\$ 45,612.79
7.	Concrete Base, Polished - Dedication Plaza	1	LS	\$ 16,465.06	\$ 16,465.06
8.	Concrete Base, Polished - CLL Axis	1	LS	\$ 14,126.48	\$ 14,126.48
9.	Ipe Deck Bench (Incl. Concrete Base)	2	EA	\$ 18,381.56	\$ 36,763.11
	Ipe Deck Bench w/ Drainage Inlet (Incl. Concrete Base)	1	EA	\$ 33,756.36	\$ 33,756.36
	Flag Poles on Concrete base	3	EA	\$ 9,297.13	\$ 27,891.39
12.				\$	\$
13				\$	\$
J.	Irrigation				
	Automatic underground irrigation system	1	LS	\$ 79,836.90	\$ 79,836.90
1.	* Includes Contractor-provided design-build irrigation drawings	<u>_</u>		4	· + _ //,000./0
	madada Caminada Provincia designi belia ingalian diamings				

AFRICAN AMERICAN MEMORIAL at BATES M. ALLEN PARK

1. Sed Preparation - Shrubs & Groundcover 15,811 \$F \$ 3.88 \$ 60,827.25 2. Mulch - Hinsettow Mulch D' Depth (plactolumor sweet Gums) 9,13 \$F \$ 1.58 \$ 1.46.55 pg 3. Mulch - Hardwood Mulch 2" Depth (Shrubs & Groundcover) 15,811 \$F \$ 0.05 \$ 9,217.81 4. Fertilizer (Shrubs & Groundcover) 15,811 \$F \$ 0.01 \$ 1.73.72 5. Shrub - Bicclor Iris, 3 Gal. 422 \$F \$ 0.05 \$ 1.721.71 6. Shrub - Red Yucca, 3 Gal. 422 \$F \$ 0.05 \$ 1.721.71 6. Shrub - Red Yucca, 3 Gal. 66 \$F \$ 2.65.75 \$ 1.721.71 6. Shrub - Red Yucca, 3 Gal. 66 \$F \$ 3.030.36 8. Shrub - Clyde Redmond Louisiana Iris, 3 Gal. 59 \$F \$ 3.000 \$ 2.183.39 7. Shrub - Red Velved Birbs (budisiana Iris, 3 Gal. 59 \$F \$ 3.000 \$ 2.183.39 8. Shrub - Clyde Redmond Louisiana Iris, 3 Gal. 59 \$F \$ \$ 3.000 \$ 2.183.39 9. Shrub - Red Velved Birbs (budisiana Iris, 3 Gal. 59 \$F \$ \$ 3.000 \$ 2.183.39 10. Shrub - White Cloud Muhly Grass, 3 Gal. 102 \$F \$ \$ 2.9.60 \$ 3.019.30 11. Shrub - Sociely Garlic, 3 Gal. 102 \$F \$ \$ 2.9.60 \$ 3.019.30 12. Groundcover - Sandy Leaf Irig Iry, 1 Gal. 2108 \$F \$ \$ 2.00 \$ \$ 2.0034.43 13. Groundcover - Purple Iraling Lantana, 1 Gal. 246 \$F \$ \$ 2.00 \$ \$ 2.0034.43 14. Plant Material—Bambeo 0 \$F \$ 0.00 \$ \$ 0.00 15. Tree - Columnar Sweet Gurn, 65 gal \$F \$ 0.00 \$ \$ 0.00 16. Tree - Tulip Paplar, 65 gal \$F \$ 0.00 \$ \$ 0.00 17. Tree - Southern Live Colk, 200 gal, [transplanted from Tree Form] 14 \$F \$ 1.437.70 \$ 1.437.70 18. Tree - Tulip Paplar, 65 gal \$F \$ 1.18 \$ 5.121.46 19. Bird Material—Bambeo 10 \$F \$ 0.00 \$ \$ 0.00 \$ 0.00 19. Wildflowers 10.00 \$ \$ 0.00 \$ 0	K.	Softscape					
2. Mulch - Pinestrow Mulch 3" Depth (at Columnor sweet Gums)	1	. Bed Preparation - Shrubs & Groundcover	15,811	SF	\$	3.85 \$	60,872.35
3. Mulch - Hardwood Mulch 2" Depth (shrubs & Groundcover) 15.811 \$F \$ 0.58 \$ 2.217.81 \$ 1.781	2	. Mulch - Pinestraw Mulch 3" Depth (at Columnar Sweet Gums)	9,132	SF	\$		
4. Ferfilizer (Shubas A Gioundeceen) 5. Shuth - Bicolor Iris, 3 Gol. 6. Shuth - Red Yucca, 3 Gol. 6. Shuth - Red Yucca, 3 Gol. 6. Shuth - Red Yucca, 3 Gol. 7. Shuth - Acadian Mist Jouisiana Iris, 3 Gol. 8. Shuth - Chyde Redmond Louisiana Iris, 3 Gol. 8. Shuth - Chyde Redmond Louisiana Iris, 3 Gol. 8. Shuth - Chyde Redmond Louisiana Iris, 3 Gol. 8. Shuth - Chyde Redmond Louisiana Iris, 3 Gol. 8. Shuth - Chyde Redmond Louisiana Iris, 3 Gol. 8. Shuth - Shuth - Red Velvet Bivis Louisiana Iris, 3 Gol. 8. Shuth - Red			15,811	SF	\$	0.58 \$	9,217.81
5. Shrufb - Bicolor lis, 3 Gal. 422 EA \$ 26.59 \$ 11.219.71 6. Shrufb - Red Yucca, 3 Gal. 66 EA \$ 25.59 \$ 1.754.74 7. Shrufb - Acadian Miss Louisiana Iris, 3 Gal. 86 EA \$ 35.31 \$ 3.036.66 8. Shrufb - Clyde Redmond Louisiana Iris, 3 Gal. 59 EA \$ 37.02 \$ 2.183.89 9. Shrufb - Red Velvel Elvis Louisiana Iris, 3 Gal. 479 EA \$ 27.69 \$ 13.262.07 11. Shrufb - Sociely Gartic, 3 Gal. 479 EA \$ 27.69 \$ 13.262.07 11. Shrufb - Sociely Gartic, 3 Gal. 2108 EA \$ 29.00 \$ 3.019.30 12. Groundcover - Sondy Leaf Fig Iry, 1 Gal. 2108 EA \$ 9.50 \$ 20.034.43 13. Groundcover - Sondy Leaf Fig Iry, 1 Gal. 246 EA \$ 5.71 \$ 1.404.41 14. Feat-Huffer Barnbae 0 5 F \$ 0.00 \$ 0.00 15. Tree - Columnar Sweet Gurn, 65 gal 95 EA \$ 547.80 \$ 52.041.00 16. Tree - Tulip Poplar, 65 gal 1 EA \$ 440.00 \$ 2.640.00 17. Tree - Southern Live Ook, 200 gal, [transplanled from Tree Farm] 1 EA	4	. Fertilizer (Shrubs & Groundcover)	15,811	SF	\$		173.92
7. Shurb - Acadian Miss Louisiana Iris, 3 Gal. 8. Shurb - Clyde Redmond Louisiana Iris, 3 Gal. 9. Shurb - Red Velvet Bivis Louisiana Iris, 3 Gal. 9. Shurb - Red Velvet Bivis Louisiana Iris, 3 Gal. 10. Shurb - White Cloud Muhly Grass, 3 Gal. 11. Shurb - Society Garlic, 3 Gal. 11. Shurb - Society Garlic, 3 Gal. 12. Groundcover - Sandy Leaf Eig Ivy, 1 Gal. 13. Groundcover - Purple Trailling Lantana, 1 Gal. 14. Fleath-Material-Bambee 15. Groundcover - Purple Trailling Lantana, 1 Gal. 16. Iree - Columnar Sweet Gum, 65 gal 16. Iree - Columnar Sweet Gum, 65 gal 16. Iree - Columnar Sweet Gum, 65 gal 17. Iree - Southern Live Ook, 200 gal, (Transplanted from Tree Form) 18. Iree - Chaste Iree, 45 gal 19. Wildflowers 17. Separabee 19. Wildflowers 17. Separabee 19. Wildflowers 17. Separabee 19. Let Separab	5	. Shurb - Bicolor Iris, 3 Gal.	422	EA	\$		11,219.71
8. Shurtb - Clycle Redmond Louisland Iris, 3 Gal. 9. Shurtb - Red Velvet Elvis Louisland Iris, 3 Gal. 10. Shurtb - While Cloud Muthly Grass, 3 Gal. 11. Shurtb - While cloud Muthly Grass, 3 Gal. 11. Shurtb - Society Garlic, 3 Gal. 12. Groundcover - Purple Iralling Lantana, 1 Gal. 12. Groundcover - Purple Iralling Lantana, 1 Gal. 13. Groundcover - Purple Iralling Lantana, 1 Gal. 14. Plant-Mathetial—Barmbae 15. Face - Columnar Sweet Gum, 65 gal 16. Tree - Columnar Sweet Gum, 65 gal 16. Tree - Columnar Sweet Gum, 65 gal 16. Tree - Columnar Sweet Gum, 65 gal 17. Tree - Southern Live Oak, 200 gal. [transplanted from Tree Farm] 18. Tree - Chaste Tree, 45 gal 19. Wildflowers 17. September 19. Sept			66	EA	\$	26.59 \$	1,754.74
9. Shurb - Red Velvet Bfvis Louislana Iris, 3 Gal. 10. Shurb - White Cloud Muhly Grass, 3 Gal. 11. Shurb - White Cloud Muhly Grass, 3 Gal. 12. Groundcover - Sandy Leaf Fig Ivy, 1 Gal. 13. Groundcover - Sandy Leaf Fig Ivy, 1 Gal. 14. Groundcover - Sandy Leaf Fig Ivy, 1 Gal. 15. Groundcover - Sandy Leaf Fig Ivy, 1 Gal. 16. Iree - Columnar Sweet Gum, 65 gal 16. Iree - Columnar Sweet Gum, 65 gal 16. Iree - Tulip Poplar, 65 gal 16. Iree - Tulip Poplar, 65 gal 17. Iree - Southern Live Ook, 200 gal. (Iransplanted from Tree Farm) 18. Iree - Chaste Tree, 45 gal 19. Ifee - Chaste Tree, 45 gal 19. Ifee - Southern Live Ook, 200 gal. (Iransplanted from Tree Farm) 19. Isode - Chaste Tree, 45 gal 19. Isode - Common Bermuda (includes fine grading) 19. Sode - C	7	. Shurb - Acadian Miss Louisiana Iris, 3 Gal.	86	EA	\$	35.31 \$	3,036.66
10 Shurb - White Cloud Muhly Grass, 3 Gal. 477 EA \$ 27.69 \$ 13,262.07 11 Shurb - Society Garlic, 3 Gal. 478 EA \$ 27.60 \$ 3.019.30 12 Groundcover - Sandy Leaf Fig Ivy, 1 Gal. 2108 EA \$ 9.50 \$ 2.0034.43 13 Groundcover - Purple Trailing Lantana, 1 Gal. 246 EA \$ 5.71 \$ 1.404.41 14 Plant-Material - Barmbee 35 50.00 \$ 0.00 15 Tree - Columnar Sweet Gum, 65 gal 95 EA \$ 547.80 \$ 52.041.00 16 Tree - Tulijp Poplar, 65 gal 6 EA \$ 440.00 \$ 2.640.00 16 Tree - Columnar Sweet Gum, 65 gal 6 EA \$ 440.00 \$ 2.640.00 16 Tree - Columnar Sweet Gum, 65 gal 1 EA \$ 440.00 \$ 2.640.00 16 Tree - Columnar Sweet Gum, 65 gal 1 EA \$ 440.00 \$ 2.640.00 16 Tree - Chaste Tree, 45 gal 1 EA \$ 440.00 \$ 6.160.00 19 Wildflowers 1 EA \$ 440.00 \$ 6.160.00 10 EA \$ 1.405.00 \$ 6.100.00 10 EA \$ 1.405.0	8	. Shurb - Clyde Redmond Louisiana Iris, 3 Gal.	59	EA	\$	37.02 \$	2,183.89
1 1 1 2 1 2 2 2 3 2 2 3 2 2 3 3	9	. Shurb - Red Velvet Elvis Louisiana Iris, 3 Gal.	58	EA	\$	36.98 \$	2,144.96
12 Groundcover - Sandy Leaf Fig Ivy, 1 Gal. 2108 EA \$ 9.50 \$ 20.034.43 \$ 13. Groundcover - Purple Trailling Lantana, 1 Gal. 246 EA \$ 5.71 \$ 1.404.41 \$ 14. Pikant-Materical - Barnboe 0 5F \$ 0.00 \$ 5 \$ 0.00 \$ 5 \$ 0.00 \$ 5 \$ 0.00 \$ 5 \$ 0.00 \$ 5 \$ 0.00 \$ 5 \$ 0.00 \$ 5 \$ 0.00 \$ 0.00 \$ 5 \$ 0.00 \$ 0.00 \$ 5 \$ 0.00 \$ 0.00 \$ 5 \$ 0.00 \$ 0.0	10	. Shurb - White Cloud Muhly Grass, 3 Gal.	479	EA	\$	27.69 \$	13,262.07
2108 EA \$ 9.50 \$ 20,034.43 31. Groundcover - Sandy Leaf fig Ivy, 1 Gal. 1246 EA \$ 5.71 \$ 1.404.41 31. Groundcover - Purple Trailing Lantana, 1 Gal. 246 EA \$ 5.71 \$ 1.404.41 31. Free - Columnar Sweet Gum, 65 gal 95 EA \$ 547.80 \$ 52,041.00 31. Tree - Columnar Sweet Gum, 65 gal 6 EA \$ 440.00 \$ 2.464.00 31. Tree - Lulip Poplar, 65 gal 6 EA \$ 440.00 \$ 2.464.00 31. Tree - Southern Live Oak, 200 gal. (Transplanted from Tree Farm) 1 EA \$ 4.40.00 \$ 1.437.70 31. Tree - Chaste Tree, 45 gal 14 EA \$ 4.40.00 \$ 1.437.70 31. Wildflowers 713 SF \$ 7.18 \$ 5.121.48 32. Bio-Barrière Barmboe 0 LF \$ 0.00 \$ 0.00 31. Sod - Common Bermuda (includes fine grading) 3.603 SF \$ 1.18 \$ 4.240.73 32. Sod - Zoysia 'Ermerald'@ Juneleenth Lavis Memorial (includes fine grading) 3.603 SF \$ 1.18 \$ 4.240.73 32. Hydromulch - Common Bermuda (includes fine grading) 3.603 SF \$ 1.18 \$ 4.240.73 32. Hydromulch - Common Bermuda (includes fine grading) 3.603 SF \$ 1.18 \$ 4.240.73 32. Hydromulch - Common Bermuda (includes fine grading) 3.603 SF \$ 1.18 \$ 4.240.73 32. Hydromulch - Common Bermuda (includes fine grading) 3.603 SF \$ 1.18 \$ 4.240.73 32. Hydromulch - Common Bermuda (includes fine grading) 3.603 SF \$ 1.18 \$ 4.240.73 33. Hydromulch - Common Bermuda (includes fine grading) 3.603 SF \$ 1.18 \$ 4.240.73 34. Forestation 12.025 SF \$ 0.85 \$ 1.01 \$ 5.18 35. Forestation - Pinestraw Mulch 3" Depth 2.025 SF \$ 0.85 \$ 1.01 \$ 5.18 36. Forestation - Pinestraw Mulch 3" Depth 2.025 SF \$ 0.85 \$ 1.025 \$ 5.000 37. Tree - Loblolly Pine, 4" Machine Moved 11 EA \$ 0.00 \$ 0.00 38. Tree - Loblolly Pine, 4" Machine Moved 7 EA \$ 319.95 \$ 2.239.62 39. Tree - Loblolly Pine, 5 gal 3 EA \$ 207.90 \$ 2.239.62 30. Tree - Loblolly Pine, 5 gal 3 EA \$ 207.90 \$ 2.239.62 39. Tree - Loblolly Pine	11	. Shurb - Society Garlic, 3 Gal.	102	EA	\$	29.60 \$	3,019.30
14. Plant-Material - Bambeo 0 SF 0.00 0.00 15. Tree - Columnar Sweet Gum, 65 gal 6 6 6 4 440.00 \$ 52.041.00 16. Tree - Tulip Poplar, 65 gal 6 6 8 440.00 \$ 2.640.00 17. Tree - Southern Live Oak, 200 gal. (Transplanted from Tree Farm) 1 EA \$ 1.437.70 \$ 1.437.70 18. Tree - Chaste Tree, 45 gal 14 EA 440.00 \$ 6.160.00 19. Wildflowers 71 SF 7.18 \$ 5.121.48 20. Bio-Barrier - Bamboo 0 LF 0.00 0.00 21. Sod - Common Bermuda (includes line grading) 3.062 SF 1.18 4.240.73 22. Sod - Coysia ("Emerated") Juneteenth Lawn & CLL Axis Memorial (includes line grading) 3.062 SF 1.18 4.240.73 23. Hydromulch - Common Bermuda (includes line grading) 264.494 SF 0.10 26.184.91 24. Forestation ("Zones A & B.) 24. Forestation Pinestraw Mulch 3" Depth 12.025 SF 0.85 10.185.18 25. Forestation - Pinestraw Mulch 3" Depth 12.025 SF 2.29 15.476.18 26. Tree - Drummond Red Maple, 30 gal 7 EA 2.211.5 2.038.04 27. Tree - Savannah Holly, 15 gal 3 EA 2.16.70 6.50.10 28. Tree - Loblolly Pine, 30 gal 7 EA 3.19.95 2.239.62 29. Tree - Loblolly Pine, 30 gal 7 EA 3.19.95 2.239.62 20. Tree - Loblolly Pine, 5 gal 3 EA 3.20.79 2.702.70 31. Tree - Water Oak, 30 gal 7 EA 3.38.30 3.20.30 32. Tree - Water Oak, 30 gal 7 EA 3.38.30 3.20.30 34. Tree - Exaxs Red Oak, 30 gal 7 EA 4.40.00 3.308.00 35. Tree - Exaxs Red Oak, 30 gal 7 EA 4.40.00 3.308.00 36. Tree - Exaxs Red Oak, 30 gal 7 EA 4.40.00 3.308.00 37. Shrub - Yaupon Holly, 7 gal 3 EA 5.57.2 724.30 38. Shrub - Wax Myrtle, 7 gal 3 EA 5.57.2 724.30 39. Tree - Devand Holly, 7 gal 3 EA 5.57.2 724.30 39. Tree - Devand Holly, 7 gal 3 EA 5.57.2 724.30 39. Tree - Devand Holly, 7 gal 3 EA 5.57.2 724.30 39. Tree - Devand H			2108	EA	\$	9.50 \$	
15. Tree - Columnar Sweet Gum, 65 gal 95 EA \$ 547.80 \$ 52.041.00 16. Tree - Tulip Poplar, 65 gal 6 EA \$ 440.00 \$ 2.640.00 17. Tree - Southern Live Oak, 200 gal. [Transplanted from Tree Farm] 1 EA \$ 1.437.70 \$ 1.437.70 18. Tree - Chaste Tree, 45 gal 14 EA \$ 440.00 \$ 6.160.00 19. Wildflowers 713 SF 7.18 \$ 5.121.48 19. Bi- Bearrier Bambee 0 LF \$ 0.00 \$ 0.000 11. Sad - Common Bermuda (includes fine grading) 3,603 SF \$ 1.18 \$ 4.240.73 12. Sad - Zoysia "Emerald"@ Juneteenth Lawn & CLL Axis Memorial (includes fine grading) 13,062 SF 1.49 17,397.07 17. Tree - Loysia "Emerald"@ Juneteenth Lawn & CLL Axis Memorial (includes fine grading) 264.494 SF 0.00 \$ 0.000 24. Forestation Zones A & B.] 24. Forestation 25. Forestation			246	EA	\$	5.71 \$	1,404.41
16 Tree - Tulip Poplar, 65 gal 2.640.00 3.2640.00 17 Tree - Southern Live Oak, 200 gal. [Transplanted from Tree Farm] 1 EA 1.437.70 3.1437.70 3.1437.70 3.1437.70 3.1737.00 3.18 3.1740.00 3.18 3.1740.00 3.18 3.1740.00 3.18 3.1740.00 3.18 3.1740.00 3.18 3.1740.00 3.18 3.1740.00 3.18			0	SF	\$	0.00 \$	0.00
1	15	. Tree - Columnar Sweet Gum, 65 gal	95	EA	\$	547.80 \$	52,041.00
18. Tree - Chaste Tree, 45 gal 14 EA \$ 440.00 \$ 6.160.00 19. Wildflowers 713 SF \$ 7.18 \$ 5,121.48 20. Bio-Barrier-@ Barneboe 0 LF \$ 0.00 \$ 0.00 21. Sod - Common Bermuda (includes fine grading) 3,603 SF \$ 1.18 \$ 4,240.73 22. Sod - Zoysia 'Ernerald'@ Juneteenth Lawn & CLL Axis Memorial (includes fine grading) 13,062 SF \$ 1.09 \$ 19,397.07 23. Hydromulch - Common Bermuda (includes fine grading) 264,49 SF \$ 0.10 \$ 26,184.91 Forestation (Iones A & B) 24. Forestation - Bed Preparation (Incl. Bed Amendments) 12,025 SF \$ 0.85 \$ 10,185.18 25. Forestation - Pinestraw Mulch 3" Depth 12,025 SF \$ 0.85 \$ 10,185.18 26. Tree - Drummond Red Maple, 30 gal 7 EA \$ 291.15 \$ 2,038.04 27. Tree - Savannah Holly, 15 gal 3 EA \$ 216.70 \$ 650.10 28. Tree - Loblolly Pine, 4" Machine Moved 11 EA \$ 10,00 \$ 0.00 29. Tree - Loblolly Pine, 15 gal 17 EA \$ 207.00 \$ 2,202.70			6	EA	\$	440.00 \$	2,640.00
19. Wildflowers			1	EA	\$	1,437.70 \$	1,437.70
20 . Bio-Barrier @ Barmboe 0 LF \$ 0.00 \$ 0.00 21 . Sod - Common Bermuda (includes fine grading) 3,603 SF \$ 1.18 \$ 4,240.73 22 . Sod - Zoysia 'Emerald'@ Juneteenth Lawn's CLL Axis Memorial (includes fine grading) 264,494 SF \$ 0.10 \$ 19,397.07 23 . Hydromulch - Common Bermuda (includes fine grading) 264,494 SF \$ 0.10 \$ 26,184.91 Forestation (Zones A & B) 24 . Forestation - Bed Preparation (Incl. Bed Amendments) 12,025 SF \$ 0.85 \$ 10,185.18 25 . Forestation - Pinestraw Mulch 3" Depth 12,025 SF \$ 0.85 \$ 10,185.18 26 . Tree - Drummond Red Maple, 30 gal 7 EA \$ 291.15 \$ 2,038.04 27 . Tree - Savannah Holly, 15 gal 3 EA \$ 216.70 \$ 650.10 28 . Tree - Loblolly Pine, 4" Machine Moved 11 EA \$ 0.00 \$ 0.00 29 . Tree - Loblolly Pine, 30 gal 7 EA \$ 319.95 \$ 2,239.62 30 . Tree - Loblolly Pine, 15 gal 13 EA \$ 207.90 \$ 2,702.70 31 . Tree -			14	EA	\$	440.00 \$	6,160.00
21 . Sod - Common Bermuda (includes line grading) 3,603 SF 1.18 4,240.73	19	. Wildflowers	713	SF	\$	7.18 \$	5,121.48
22 . Sod - Zoysia 'Emerald'@ Juneteenth Lawn & CLL Axis Memorial (includes fine grading) 13,062 SF 1.49 19,397.07 23 . Hydromulch - Common Bermuda (includes fine grading) 264,494 SF 0.10 26,184.91			0	LF	\$	0.00 \$	0.00
264,494 SF \$ 0.10 \$ 26,184.91			3,603	SF	\$	1.18 \$	4,240.73
Forestation (Tones A & B	22	. Sod - Zoysia 'Emerald'@ Juneteenth Lawn & CLL Axis Memorial (includes fine grading)	13,062	SF	\$	1.49 \$	19,397.07
24 . Forestation - Bed Preparation (Incl. Bed Amendments) 12,025 SF 0.85 \$ 10,185,18 25 . Forestation - Pinestraw Mulch 3" Depth 12,025 SF 1.29 \$ 15,476,18 26 . Tree - Drummond Red Maple, 30 gal 7 EA \$ 291,15 \$ 2,038,04 27 . Tree - Savannah Holly, 15 gal 3 EA \$ 216,70 \$ 650,10 28 . Tree - Loblolly Pine, 4" Machine Moved 11 EA \$ 0,00 \$ 0,00 29 . Tree - Loblolly Pine, 30 gal 7 EA \$ 319,95 \$ 2,239,62 30 . Tree - Loblolly Pine, 15 gal 13 EA \$ 207,90 \$ 2,702,70 31 . Tree - Loblolly Pine, 5 gal 19 EA \$ 49,50 \$ 940,50 32 . Tree - Mexican Sycamore, 30 gal 7 EA \$ 358,60 \$ 2,510,20 33 . Tree - Water Oak, 30 gal 7 EA \$ 440,00 \$ 3,080,00 34 . Tree - Willow Oak, 5 gal 3 EA \$ 50,41 \$ 151,24 35 . Tree - Texas Red Oak, 30 gal 7 EA \$ 412,50 \$ 2,887,50 36 . Tree - Cedar Elm, 5 gal 7 EA \$ 49,97 \$ 349,81 <	23	. Hydromulch - Common Bermuda (includes fine grading)	264,494	SF	\$	0.10 \$	26,184.91
25 . Forestation - Pinestraw Mulch 3" Depth 26 . Tree - Drummond Red Maple, 30 gal 27 . Tree - Savannah Holly, 15 gal 28 . Tree - Loblolly Pine, 4" Machine Moved 29 . Tree - Loblolly Pine, 4" Machine Moved 30 . Tree - Loblolly Pine, 30 gal 31 . Tree - Loblolly Pine, 30 gal 32 . Tree - Loblolly Pine, 5 gal 33 . Tree - Loblolly Pine, 5 gal 34 . Tree - Water Oak, 30 gal 35 . Tree - Water Oak, 30 gal 36 . Tree - Willow Oak, 5 gal 37 . Shrub - Yaupon Holly, 7 gal 38 . Shrub - Wax Myrtle, 7 gal 39 . Shrub - Wax Myrtle, 7 gal 30 . Tree - Wax Myrtle, 7 gal 31 . Tree - Wax Myrtle, 7 gal 32 . Tree - Wax Myrtle, 7 gal		Forestation (Zones A & B)					
25 . Forestation - Pinestraw Mulch 3" Depth 26 . Tree - Drummond Red Maple, 30 gal 27 . Tree - Savannah Holly, 15 gal 28 . Tree - Loblolly Pine, 4" Machine Moved 29 . Tree - Loblolly Pine, 4" Machine Moved 30 . Tree - Loblolly Pine, 30 gal 31 . Tree - Loblolly Pine, 30 gal 32 . Tree - Loblolly Pine, 5 gal 33 . Tree - Loblolly Pine, 5 gal 34 . Tree - Water Oak, 30 gal 35 . Tree - Water Oak, 30 gal 36 . Tree - Willow Oak, 5 gal 37 . Shrub - Yaupon Holly, 7 gal 38 . Shrub - Wax Myrtle, 7 gal 39 . Shrub - Wax Myrtle, 7 gal 30 . Tree - Wax Myrtle, 7 gal 31 . Tree - Wax Myrtle, 7 gal 32 . Tree - Wax Myrtle, 7 gal	24	. Forestation - Bed Preparation (Incl. Bed Amendments)	12,025	SF	\$	0.85 \$	10.185.18
26 . Tree - Drummond Red Maple, 30 gal 7 EA \$ 291.15 \$ 2,038.04 27 . Tree - Savannah Holly, 15 gal 3 EA \$ 216.70 \$ 650.10 28 . Tree - Loblolly Pine, 4" Machine Moved 11 EA \$ 0.00 \$ 0.00 29 . Tree - Loblolly Pine, 30 gal 7 EA \$ 319.95 \$ 2,239.62 30 . Tree - Loblolly Pine, 15 gal 13 EA \$ 207.90 \$ 2,702.70 31 . Tree - Loblolly Pine, 5 gal 19 EA \$ 49.50 \$ 940.50 32 . Tree - Mexican Sycamore, 30 gal 7 EA \$ 358.60 \$ 2,510.20 33 . Tree - Water Oak, 30 gal 7 EA \$ 440.00 \$ 3,080.00 34 . Tree - Willow Oak, 5 gal 3 EA \$ 50.41 \$ 151.24 35 . Tree - Texas Red Oak, 30 gal 7 EA \$ 412.50 \$ 2,887.50 36 . Tree - Cedar Elm, 5 gal 7 EA \$ 49.97 \$ 349.81 37 . Shrub - Yaupon Holly, 7 gal 13 EA \$ 55.72 \$ 724.30 38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30			12.025		\$		
27 . Tree - Savannah Holly, 15 gal 3 EA \$ 216.70 \$ 650.10 28 . Tree - Loblolly Pine, 4" Machine Moved 11 EA \$ 0.00 \$ 0.00 29 . Tree - Loblolly Pine, 30 gal 7 EA \$ 319.95 \$ 2,239.62 30 . Tree - Loblolly Pine, 15 gal 13 EA \$ 207.90 \$ 2,702.70 31 . Tree - Loblolly Pine, 5 gal 19 EA \$ 49.50 \$ 940.50 32 . Tree - Mexican Sycamore, 30 gal 7 EA \$ 358.60 \$ 2,510.20 33 . Tree - Water Oak, 30 gal 7 EA \$ 440.00 \$ 3,080.00 34 . Tree - Willow Oak, 5 gal 3 EA \$ 50.41 \$ 151.24 35 . Tree - Texas Red Oak, 30 gal 7 EA \$ 412.50 \$ 2,887.50 36 . Tree - Cedar Elm, 5 gal 7 EA \$ 49.97 \$ 349.81 37 . Shrub - Yaupon Holly, 7 gal 13 EA \$ 55.72 \$ 724.30 38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30	26	. Tree - Drummond Red Maple, 30 gal			\$		
28 . Tree - Loblolly Pine, 4" Machine Moved 29 . Tree - Loblolly Pine, 30 gal 30 . Tree - Loblolly Pine, 15 gal 31 . Tree - Loblolly Pine, 15 gal 31 . Tree - Loblolly Pine, 5 gal 32 . Tree - Mexican Sycamore, 30 gal 33 . Tree - Water Oak, 30 gal 34 . Tree - Water Oak, 30 gal 35 . Tree - Fexas Red Oak, 30 gal 36 . Tree - Texas Red Oak, 30 gal 37 . Shrub - Yaupon Holly, 7 gal 38 . Shrub - Wax Myrtle, 7 gal 39	27	. Tree - Savannah Holly, 15 gal	3		-		
29 . Tree - Loblolly Pine, 30 gal 7 EA \$ 319.95 \$ 2,239.62 30 . Tree - Loblolly Pine, 15 gal 13 EA \$ 207.90 \$ 2,702.70 31 . Tree - Loblolly Pine, 5 gal 19 EA \$ 49.50 \$ 940.50 32 . Tree - Mexican Sycamore, 30 gal 7 EA \$ 358.60 \$ 2,510.20 33 . Tree - Water Oak, 30 gal 7 EA \$ 440.00 \$ 3,080.00 34 . Tree - Willow Oak, 5 gal 3 EA \$ 50.41 \$ 151.24 35 . Tree - Texas Red Oak, 30 gal 7 EA \$ 412.50 \$ 2,887.50 36 . Tree - Cedar Elm, 5 gal 7 EA \$ 49.97 \$ 349.81 37 . Shrub - Yaupon Holly, 7 gal 13 EA \$ 55.72 \$ 724.30 38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30	28	, Tree - Loblolly Pine, 4" Machine Moved	11	EA	\$		
30 . Tree - Loblolly Pine, 15 gal 13 EA \$ 207.90 \$ 2,702.70 \$ 1 . Tree - Loblolly Pine, 5 gal 19 EA \$ 49.50 \$ 940.50 \$ 32 . Tree - Mexican Sycamore, 30 gal 7 EA \$ 358.60 \$ 2,510.20 \$ 33 . Tree - Water Oak, 30 gal 7 EA \$ 440.00 \$ 3,080.00 \$ 34 . Tree - Willow Oak, 5 gal 7 EA \$ 50.41 \$ 151.24 \$ 55 . Tree - Texas Red Oak, 30 gal 7 EA \$ 412.50 \$ 2,887.50 \$ 36 . Tree - Cedar Elm, 5 gal 7 EA \$ 49.97 \$ 349.81 \$ 37 . Shrub - Yaupon Holly, 7 gal 13 EA \$ 55.72 \$ 724.30 \$ 38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30 \$ 39	29	. Tree - Loblolly Pine, 30 gal	7	EA	\$		2,239,62
32 . Tree - Mexican Sycamore, 30 gal 7 EA \$ 358.60 \$ 2,510.20 33 . Tree - Water Oak, 30 gal 7 EA \$ 440.00 \$ 3,080.00 34 . Tree - Willow Oak, 5 gal 3 EA \$ 50.41 \$ 151.24 35 . Tree - Texas Red Oak, 30 gal 7 EA \$ 412.50 \$ 2,887.50 36 . Tree - Cedar Elm, 5 gal 7 EA \$ 49.97 \$ 349.81 37 . Shrub - Yaupon Holly, 7 gal 13 EA \$ 55.72 \$ 724.30 38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30 39	30	. Tree - Loblolly Pine, 15 gal	13	EA	\$		
32 . Tree - Mexican Sycamore, 30 gal 7 EA \$ 358.60 \$ 2.510.20 \$ 33 . Tree - Water Oak, 30 gal 7 EA \$ 440.00 \$ 3,080.00 \$ 4 . Tree - Willow Oak, 5 gal 3 EA \$ 50.41 \$ 151.24 \$ 55. Tree - Treas Red Oak, 30 gal 7 EA \$ 412.50 \$ 2,887.50 \$ 7 EA \$ 49.97 \$ 349.81 \$ 7 Shrub - Yaupon Holly, 7 gal 13 EA \$ 55.72 \$ 724.30 \$ 38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30 \$ 39	31	. Tree - Loblolly Pine, 5 gal	19	EA	\$	49.50 \$	940.50
33 . Tree - Water Oak, 30 gal 7 EA \$ 440.00 \$ 3,080.00 \$ 34 . Tree - Willow Oak, 5 gal 3 EA \$ 50.41 \$ 151.24 \$ 55.70 \$ 2,887.50 \$ 36 . Tree - Cedar Elm, 5 gal 7 EA \$ 49.97 \$ 349.81 \$ 37 . Shrub - Yaupon Holly, 7 gal 38 . Shrub - Wax Myrtle, 7 gal 39	32	. Tree - Mexican Sycamore, 30 gal	7	EA	\$		
34 . Tree - Willow Oak, 5 gal 3 EA \$ 50.41 \$ 151.24 35 . Tree - Texas Red Oak, 30 gal 7 EA \$ 412.50 \$ 2,887.50 36 . Tree - Cedar Elm, 5 gal 7 EA \$ 49.97 \$ 349.81 37 . Shrub - Yaupon Holly, 7 gal 13 EA \$ 55.72 \$ 724.30 38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30 39			7		\$		
35 . Tree - Texas Red Oak, 30 gal 7 EA \$ 412.50 \$ 2,887.50 36 . Tree - Cedar Elm, 5 gal 7 EA \$ 49.97 \$ 349.81 37 . Shrub - Yaupon Holly, 7 gal 13 EA \$ 55.72 \$ 724.30 38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30 39	34	. Tree - Willow Oak, 5 gal	3		\$		
36 . Tree - Cedar Elm, 5 gal 7 EA \$ 49.97 \$ 349.81 37 . Shrub - Yaupon Holly, 7 gal 13 EA \$ 55.72 \$ 724.30 38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30 39	35	. Tree - Texas Red Oak, 30 gal	7		\$		
37 . Shrub - Yaupon Holly, 7 gal 13 EA \$ 55.72 \$ 724.30 38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30 39	36	. Tree - Cedar Elm, 5 gal	7				
38 . Shrub - Wax Myrtle, 7 gal 13 EA \$ 55.72 \$ 724.30 39	37	. Shrub - Yaupon Holly, 7 gal	13	EA	\$		
39					\$		
	39	· · · · · · · · · · · · · · · · · · ·			т		
	40	<u> </u>			\$	\$	

GRAND TOTAL BASE BID \$ 9,498,137.82

PART 2 - Alternates

2.1 SCHEDULE OF ALTERNATES

Alternate Bid Item Notes:

- Reference Sheet G001 for Phase 1 scope areas to be bid.
 Each Alternate Bid Item (boxed below) will be considered for acceptance independently from other Alternate Bid Items.
- 3. Contractor to provide Unit Prices for Alternate Bid Items.
- 4. Final quantities of Alternate Bid Items may vary from those listed.

4	. Final quantities of Alternate Bid Items may vary from those listed.				
	Allemates Architecture Res C001	Qty	Unit	Unit Cost	Extension
A. 1	Alternates: Architecture. Re: G001 . Monument Material	ALTERNATE N	In A 1	1 1	1 075 505 24
,	Subtract: Base Bid Item No.	ALIERNAIE	LS	\$ 2711.244.92 \$	1,075,505.34 -3,711,364.82
	Replace with: GFRC system @ Monument in lieu of Architectural Precast	4	LS	\$3,711,364.82	4,786,870.16
	replace with evice system a manerial in modern actinication at the cast	1 5	LU	φ_4,700,070.10 φ_	4,700,070.10
2	. Pedestrian Portals (Re: A401, A810)	ALTERNATE N	lo. A2	3	-32,104.76
	Subtract: Base Bid Item No. (portals)	3	EA	\$ -10,404.85 \$	-31,214.54
	Subtract: Base Bid Item No. (portal lighting)	6	LF	\$ -148.37 \$	-890.22
12					
В.	Alternates: Pedestrian Hardscape - Specialty Paving				
	. Specialty Paving 'A'	ALTERNATE N	-	<u> </u>	-20,463.88
	Subtract: Base Bid Item No.	6,577	SF	\$\$	-93,232.41
	Replace with: Standard Concrete Walk	6,577	SF	\$11.06 \$_	72,768.53
		_			
2	. <u>Specialty Paving 'B' Finish</u>	ALTERNATE N	lo. B.2	\$	-7,671.58
	Subtract: Base Bid Item No.	11,992	SF	\$ -22.20 \$	-266,177.13
	Replace with: Integral Color Conc. (Red) with Heavy Broom Finish	11,992	SF	\$ 21.56 \$	258,505.55
				'	
3	. Specialty Paving 'C'	ALTERNATE N	lo. B.3	\$	0.00
	Subtract; Base Bid Item No.	0	SF	\$ <u></u>	0.00
	Replace with: Valentino Glowpath Pavers	0	SF	\$ \$	0.00
	AUTOR PROTEST CONTINUED DE CONTINUE CONTINUE DE CONTINUE DE CONTINUE CONTIN	4			
4	. <u>Specialty Paving 'D'</u>	ALTERNATE N	lo. B.4	\$	-3,839.11
	Subtract: Base Bid Item No.	670	SF	\$193.68 \$	-129,765.61
	Replace with: Stamped Adinkra Symbols on Standard Conc Walk (Keep Heavy	470	SF		105 007 50
	directional Broom Finish)	670		\$187.95 \$_	125,926.50
5	. Specialty Paving 'E'	ALTERNATE N	lo. B.5	\$	-15,105.41
	Subtract: Base Bid Item No.	1,811	SF	\$ -44.89 \$	-81,297.46
	Replace with: Integral Color Conc. (Charcoal) with Heavy Broom Finish	1,811	SF	\$ 36.55 \$	66,192.05
		1,011		ΨΨ	00,172.00
6	. Specialty Paving 'F'				
	Subtract: Base Bid Item No.	403	SF	\$ -120.46 \$	-48,545.00
	A OPTION A: Replace IPE with Trex Deck on Conc. Base	403	SF		soften and a service of the service
	B OPTION B: Replace with Specialty Paving 'B'	403	SF	\$ 105.77 \$	42,626.20
	S OF HOMB. Replace will specially raving B	ALTERNATE N		\$ 22.20 \$	8,945.08
				<u> </u>	-5,918.80
		ALTERNATE N	o. B.6.B	3	-39,599.92
7	. Specialty Paving 'G'	ALTERNATE N	lo R 7	Te Te	-23,272.80
,	Subtract: Base Bid Item No.	104	SF	401.45 ¢	
	Replace with: Stamped Standard Concrete Walk (Wood Plank Look)	0.5.00	SF	\$\$	-51,111.00
	Replace with. Statisped Statisdard Concrete Walk (Wood Flank Look)	104	31	\$267.68 \$_	27,838.20
С.	Alternates: Hardscape Walls				
	Walls @ Monument Plaza (Height Varies)				
	Subtract: Base Bid Item No. (Gabions)	1	LS	\$917,601.90 \$_	-917,601.90
	Option A: Replace with Concrete Walls Battered (Re: A/L1,29)	1	LS	\$ 1,132,841.92 \$	1,132,841.92
-B	. Option B: Replace with Concrete Walls, 12" wide (Re: B/ L1.29; Re: Civil) * Includes contractor-provided enaineered shop grawings	1	LS	\$1,089,093.60 \$_	1,089,093.60
	male and contractor provided origination at 3 hop didwings	ALTERNATE NO	. C.1.A	15	215,240.02
		ALTERNATE NO		\$	171,491.70
				_	

AFRICAN AMERICAN MEMORIAL at BATES M. ALLEN PARK

2 . Walls @ CLL Axis Memorial (Height Varies) Subtract: Base Bid Item No. (Gabions) Subtract: Base Bid Item No. (Wood Topper with Steel Pipe Supports) *A. Option A: Replace with Concrete Walls Battered (Re: A, C, D/ L1.29) *B . Option B: Replace with Concrete Walls, 12" width (Re: B, C, D/ L1.29; Re: Civil) * Includes contractor-provided engineered shop drawings	1 200 1 1 ALTERNATE NO. ALTERNATE NO.	STREET, SQUARE, SQUARE,	\$ -127,336.00 \$ -166.89 \$ 624,634.08 \$ 499,722.72 \$ \$	-127,336.00 -33,378.00 624,634.08 499,722.72 463,920.08 339,008.72
 3 . Planter Walls @ Parking Lot Subtract: Base Bid Item No. (Gabions) *A. Option A: Replace with Concrete Walls Battered (Re: A/ L1.29) *B . Option B: Replace with Concrete Walls, 12" wide (Re: B/ L1.29; Re: Civil) * Includes contractor-provided engineered shop drawings 	1 1 1 ALTERNATE NO. ALTERNATE NO.		\$	-79,767.88 312,317.60 249,861.92 232,549.72 170,094.04
D. Alternates: Site Furnishings 1. Landscape Forms Backless Benches (Universe System) Subtract: Base Bid Item No. Replace with: Thermally Modified Ash Landscape Forms Bench (Universe System)	ALTERNATE NO 10 10	EA EA	\$ -2,226.00 \$ \$ 1,981.28 \$	-2,447.20 -22,260.00 19,812.80
Landscape Forms Backed Benches (Universe System) Subtract: Base Bid Item No. Replace with: Thermally Modified Ash Landscape Forms Bench (Universe System)	ALTERNATE No. 6	EA EA	\$ -3,159.72 \$ \$ 2,815.17 \$	-2,067.30 -18,958.32 16,891.02
3 . <u>Deck Bench</u> - Juneteenth Plaza Subtract: Base Bid Item No. Replace with: Trex (Incl. Concrete Base)	ALTERNATE No. 2 2	EA EA	\$ -18,381.56 \$ \$ 17,575.46 \$	-1,612.20 -36,763.11 35,150.91
4 . <u>Deck Bench w/ Drainage Inlet</u> - Juneteenth Plaza Subtract: Base Bid Item No. Replace with: Trex (Incl. Concrete Base)	ALTERNATE NO	EA EA	\$ -33,756.36 \$ \$ 32,949.76 \$	-806.60 -33,756.36 32,949.76
5 . <u>Litter Receptacle</u> Subtract: Base Bid Item No. (Incl. Concrete Base) Replace with: Keystone MT3D-32 RTS MIDTOWN Dual Recycle Trash Receptacle (Incl. Concrete Base)	ALTERNATE NO 3 3	EA EA	\$ -5,476.36 \$ \$ 4,818.22 \$	-1,974.42 -16,429.08 14,454.66
E. Alternates: Landscape Maintenance (12 Month) Subtract: Base Bid Item No. A.4 (60 Day Landscape Maintenance) 1 January 2 February 3 March 4 April 5 May 6 June 7 July 8 August 9 September 10 October 11 November 12 December	 1 1 1 1 1 1 1 1	LS L	\$ -5,156,00 \$ 14,418,85 \$ 14,4	-5,156.00 14,418.85 14,418.85 14,418.85 14,418.85 14,418.85 14,418.85 14,418.85 14,418.85 14,418.85 14,418.85 14,418.85 14,418.85

AFRICAN AMERICAN MEMORIAL at BATES M. ALLEN PARK

PART 3 - Bid Summary

3.1	GRAND TOTAL BASE BID	\$	9,498,137.82
3.2	TOTAL MATERIAL NOT USED	\$	NOT USED
3.3	TOTAL LABOR AND EQUIPMENT NOT USED	\$	NOT USED
3.4	TOTAL ALTERNATES NOT USED	\$	NOT USED
3.5	TOTAL WORKING DAYS		365
PART 4 -	Sub Contractor List - Insert company names of sub-contractors OR self-perform		
Α	. Architecture Monument	Enterprise	Precast Concrete
В	. Hardscape Walls (Gabions)		GreenTeams
C	. Hardscape Walls (C.I.P. Concrete)		SpawGlass
D	. Planting		GreenTeams
Е	. Irrigation		GreenTeams
F	. Metal Work		Renfrow
G	. Sidewalks		SpawGlass

CERTIFICATE OF INTERESTED PARTIES

FORM **1295**

1 of 1

					1011	
	Complete Nos. 1 - 4 and 6 if there are interested parties. Complete Nos. 1, 2, 3, 5, and 6 if there are no interested parties.			OFFICE USE ONLY CERTIFICATION OF FILING		
1	ame of business entity filing form, and the city, state and country of the business entity's place			Certificate Number:		
	of business. SpawGlass Civil Construction, Inc.			2024-1161929		
	Houston, TX United States			Date Filed:		
2	Name of governmental entity or state agency that is a party to the contract for which the form is			05/15/2024		
	being filed. Fort Bend County			Date Acknowledged: 06/11/2024		
3	Provide the identification number used by the governmental enti- description of the services, goods, or other property to be provided				ride a	
	B24-059					
	African American Memorial Phase One					
4				Nature of interest		
	Name of Interested Party City, State, Country (place of busin		siness)			
Voss, Weston		Houston, TX United States	X Controlling	Intermediary		
Stone, Joel		New Braunfels, TX United Sta	X			
Emmons, Michael		New Braunfels, TX United Sta	Х			
Friedel, Robert		New Braunfels, TX United Sta	Х			
SG Enterprises, Inc.		Selma, TX United States	×			
SpawGlass Employee Holding Co		Selma, TX United States	Х			
SpawGlass Holding LP		Selma, TX United States	Х			
5	Check only if there is NO Interested Party.					
6	UNSWORN DECLARATION					
	My name is	, and my date of birth is				
	My address is			_,	,	
	(street)	(city)	(state)	(zip code)	(country)	
	I declare under penalty of perjury that the foregoing is true and correc	t.				
	Executed inCounty	, State of, on the	ne	_day of	, 20	
				(month)	(year)	
	Signature of authorized agent of contracting business entity (Declarant)					
